EXPECTED PROJECT PLAN · 12 OCTOBER 2026

# From Kick-off on 15 October to Go-live on 1 January

The Odoo 19 upgrade for six companies and Urban Eats on Odoo POS, planned task by task. Dates are expected dates from Execution Plan v1.2 of 12 October 2026. Handover follows on 14 January, then support to 30 June 2027.

| KICK-OFF | UPGRADE SIGN-OFF | UAT ENVIRONMENT | GO-LIVE | SUPPORT |
|---|---|---|---|---|
| 15 Oct | 29 Oct | 1 Dec | 1 Jan | 30 Jun |
| Thu · 2026 | six companies | Tue · committed | Fri · all outlets on Odoo POS | 2027 · six months |

## FIVE PHASES

| PHASE 1 | PHASE 2 | PHASE 3 | PHASE 4 | PHASE 5 |
|---|---|---|---|---|
| **Mobilise, design & upgrade** | **Build Urban Eats** | **UAT & training** | **Cutover & go-live** | **Hypercare & SLA support** |
| 15 Oct–8 Nov | 1–30 Nov | 1–24 Dec | 27 Dec–1 Jan | 1 Jan–30 Jun |

**Standard Odoo first**
Standard, then configuration, Studio, a supported module, and custom development last. Each custom item is justified in writing and approved before it is built.

**Staging first, production last**
Every department validates on staging, and finance signs off each company before production is touched.

**Dated and linked**
Every task has a start, an end, an owner and the task or input it depends on, tracked live in Odoo Project.

**Scope unchanged**
Scope, prices and terms are as in proposal CX-TARA-2026-02 Rev. 1. This plan does not change them.

| DOCUMENT | BASED ON | COMPANION TO | DATE |
|---|---|---|---|
| Expected Project Plan | Execution Plan v1.2 | CX-TARA-2026-02 Rev. 1 | 12 October 2026 |

OVERVIEW

# The Plan at a Glance

Work starts on Thursday 15 October 2026. The UAT environment opens on Tuesday 1 December and every outlet goes live on Odoo POS on Friday 1 January 2027, with six months of support after that.

### Part 1: Odoo 18 to 19 upgrade

- All six existing companies move to **Odoo 19 in the same database**, with history intact.
- Everything is validated on staging first, and **finance signs off each company** before production is touched.

### Part 2: Urban Eats on Odoo 19

- Structure and finance, central kitchen, **POS and Kitchen Display**, delivery platforms, payments, ZATCA, WhatsApp, loyalty, and the **exit from Foodics**.
- Scope, prices and terms are as in proposal **CX-TARA-2026-02 Rev. 1**.

## Milestones


Fifteen milestones from kick-off to the end of support. The two committed dates are the UAT environment on 1 December and go-live on 1 January.

| # | MILESTONE | DATE | NEEDS | CONFIRMED BY | EVIDENCE |
|---|---|---|---|---|---|
| **M0** | **Agreement signed & kick-off held** | Thu 15 Oct 2026 | I-01, I-02 | Both parties | Signed agreement; kick-off minutes |
| **M1** | **Assessment, module register & architecture approved** | Thu 29 Oct | 0.6, 0.7 | Tara Owner | Approved documents |
| **M2** | **Upgrade signed off on staging (six companies)** | Thu 29 Oct | 1.5–1.8 | Tara Finance, per company | Signed before / after report per company |
| **M3** | **Production upgraded to Odoo 19** | Weekend 6–7 Nov | M2, D-03 | Tara Finance + IT | Post-upgrade checks signed |
| **M4** | **Urban Eats foundation configured** | Thu 12 Nov | M1, I-11, I-12 | Tara Owner | Shown on staging |
| **M5** | **Central kitchen, POS & payments ready** | Thu 26 Nov | M4, I-14, I-19 | Kitchen + Operations | Staging walk-through; pilot-outlet test |
| **M6** | **Delivery platforms connected in test** | Thu 26 Nov | D-01, platform approvals | Tara Operations | Test order per connected platform |
| **M7** | **Internal testing complete; data loaded** | Mon 30 Nov | M5, M6, 12.6 | Code-ox | Internal test report |
| **M8** | **Production-ready UAT environment live** | Tue 1 Dec 2026 | M7 | Committed date | Logins, scripts, data handed over |
| **M9** | **UAT acceptance** | Thu 24 Dec | 13.5, 13.6 | Tara Owner | No open Critical or High issue |
| **M10** | **Go / No-Go** | Tue 29 Dec | M9, 14.5 | Sponsor + Co-founder | Signed checklist |
| **M11** | **Cutover complete: Foodics closed for transactions** | Thu 31 Dec (night) | M10 | Both parties | Runbook steps complete |
| **M12** | **Production go-live: all outlets on Odoo POS** | Fri 1 Jan 2027 | M11 | Committed date | POS selling, ZATCA accepted, orders flowing |
| **M13** | **Source & documentation handed over** | Thu 14 Jan | M12 | Tara Owner + IT | Signed handover pack |
| **M14** | **Six-month support ends** | Wed 30 Jun 2027 | M12 | Both parties | Close-out; AMC optional |

TIMELINE

# Gantt: Kick-off to Handover

Seventeen workstreams across thirteen weeks, Thursday 15 October 2026 to Thursday 14 January 2027. Weeks run Sunday to Thursday.

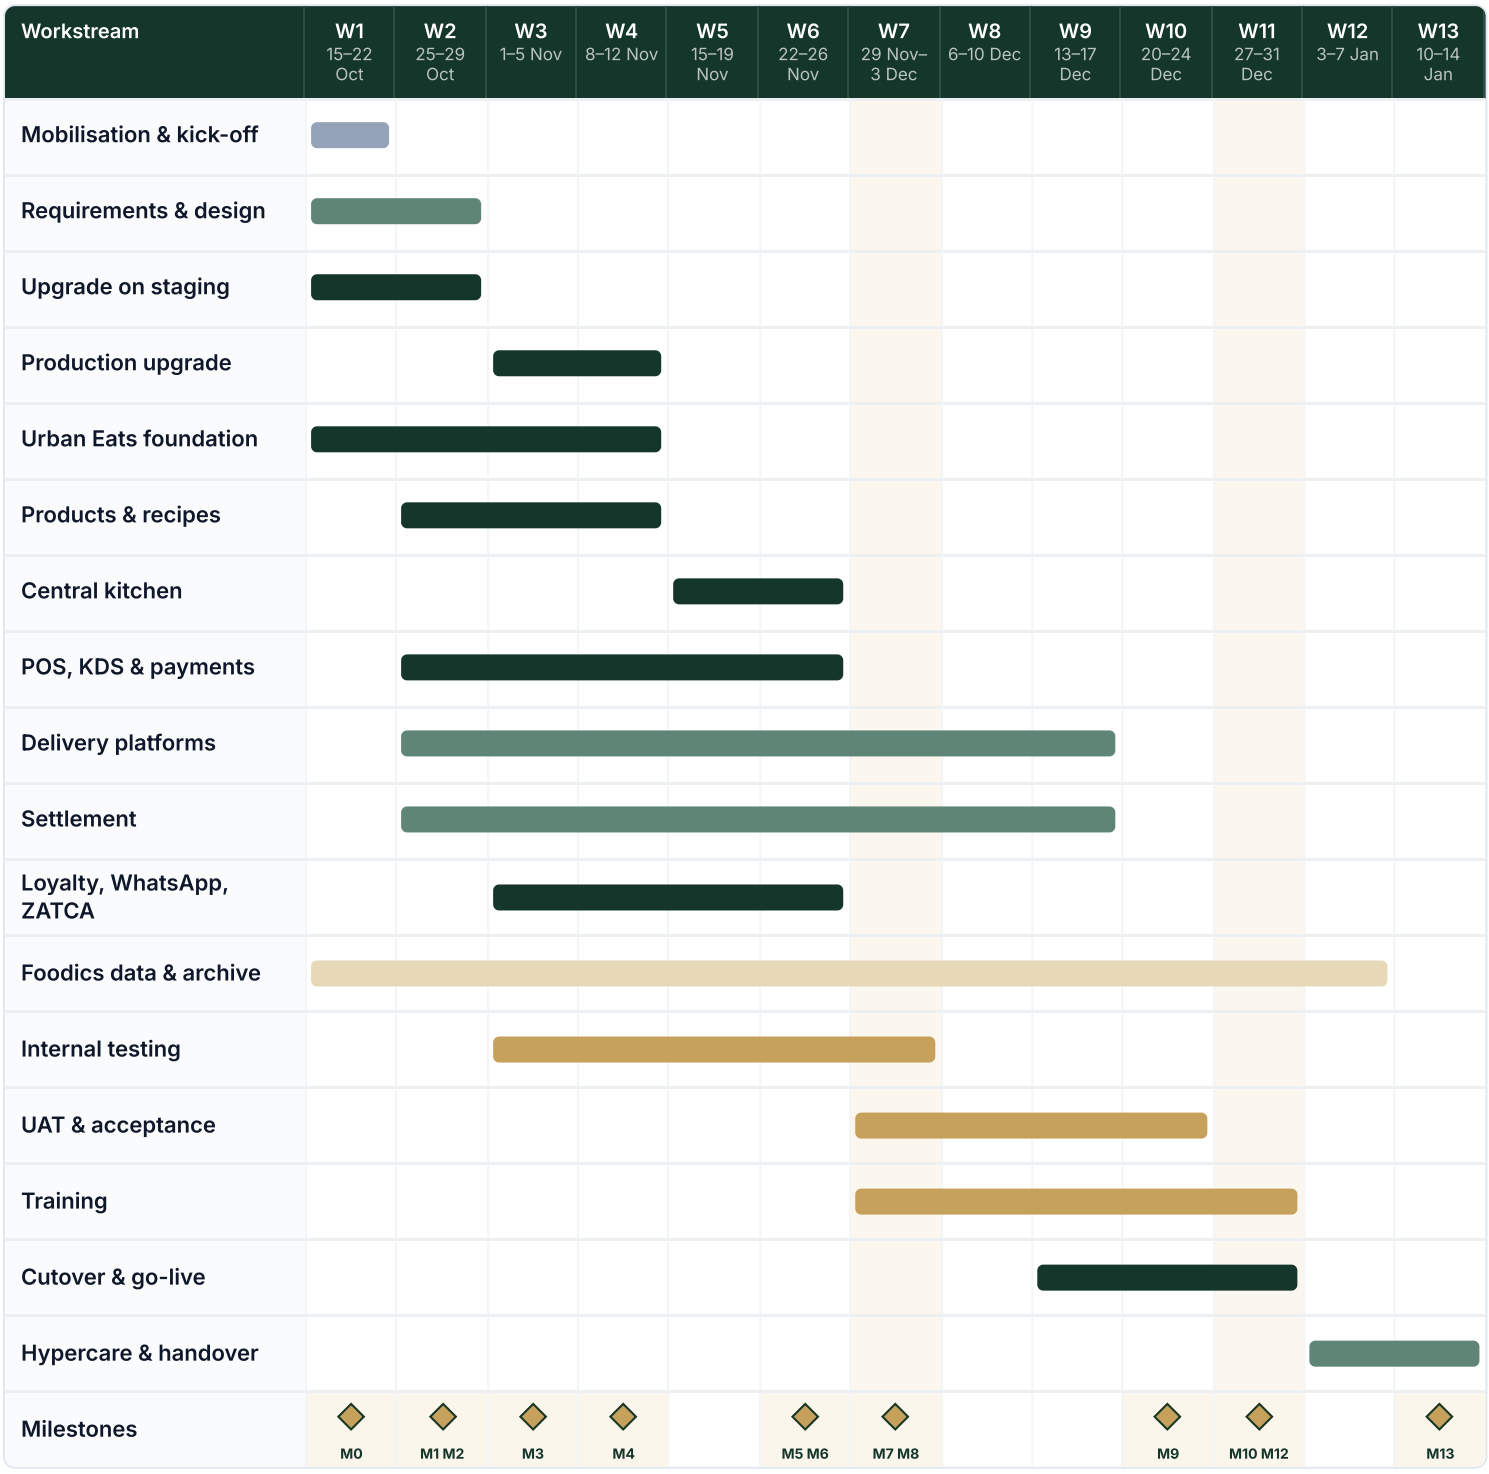


**UPGRADE BEFORE CUTOVER**

The upgrade is signed off by **29 October** and production is upgraded on the weekend of **6–7 November**, so cutover night carries only the Urban Eats switch.

**HIGHLIGHTED WEEKS**

**W7**: the UAT environment goes live on Tue 1 Dec. **W11**: cutover week, ending on the night of 31 Dec for go-live on Fri 1 Jan 2027. M11 (cutover night) sits between M10 and M12.

TASK LIST

# Tasks by Workstream

Every task with its expected dates, owner, dependency and output. Green tags are Code-ox roles; gold tags are Tara Holding; grey tags are third parties. Gold rows are milestones.

## WS 0 Mobilisation

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| P.1 | Solution demo on Odoo 19: Brand / Branch / Channel as standard objects, brand POS and product visibility, central kitchen loop, 3 L bottle → litres conversion | 12–13 Oct | Co-founder, Project Manager | — | Demo held |
| 0.1 | Financial acceptance; agreement signed; advance invoice | by Thu 15 Oct | Engagement Lead, Sponsor | — | Signed agreement |
| 0.2 | Kick-off: scope, team, this plan, cadence, access checklist; D-01 confirmed M0 | Thu 15 Oct | Engagement Lead, Project Manager, Owner | 0.1 | Minutes · M0 |
| 0.3 | Access: Odoo.sh collaborator, staging URL + admin login, GitHub read access, Foodics console + API; Code-ox registered as partner on the subscription | 15–18 Oct | IT | 0.2 | Access checklist · critical path |
| 0.4 | Tracker live in Code-ox Odoo Project: tasks, sub-tasks, dates, dependencies; portal users for Tara; Helpdesk team for UAT and support | 15–20 Oct | Project Manager | 0.2 | Portal access sent |
| 0.5 | Kick-off pack: contacts, cadence, severity definitions, requirement questionnaires per area, data templates | Thu 15 Oct | Project Manager | — | Pack issued |

## WS 0 Requirements & design

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 0.6 | Upgrade assessment & module register: each module's function, Odoo 19 version, treatment (retain, migrate, replace, consolidate, retire), licence cost, risk | 15–22 Oct | Technical, Project Manager | 0.3 | Assessment + register |
| 0.7 | Urban Eats architecture document (Section 5): company, analytic plans, warehouses and routes, POS and journals, presets, payment methods, access model | 18–22 Oct | Project Manager, Co-founder | 0.2 | Document for approval |
| 0.8 | Data migration plan, import templates, Foodics gap report | 15–22 Oct | Project Manager, Functional | 0.3 | Plan + templates |
| 0.9 | Requirement workshops (2 hrs each): finance & ZATCA · procurement & inventory · central kitchen · outlets & POS · platforms & settlement · marketing | 18–29 Oct | Project Manager, Functional, Finance, Procurement, Kitchen Lead, Operations, Marketing | 0.5 | Signed workshop notes |
| 0.10 | Integration plan per platform (Option A) or UrbanPiper plan (Option B) | 25–29 Oct | Technical, Engagement Lead | D-01, 6.1 | Integration plan |
| 0.11 | POS hardware & network specification per outlet | 25–29 Oct | Technical | I-09 | Spec for ordering |
| 0.12 | Approval of assessment, register and architecture; decisions D-02, D-04, D-05 M1 | Thu 29 Oct | Co-founder, Owner | 0.6, 0.7 | M1 |

TASK LIST

# Tasks by Workstream (continued)

## WS 1 Odoo 18 → 19 upgrade

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 1.1 | Full backup of production; staging branch from the latest backup | Thu 15 Oct | Technical | 0.3 | Backup reference |
| 1.2 | Staging copy upgraded to Odoo 19 through Odoo's upgrade service | 15–18 Oct | Technical Odoo | 1.1 | Odoo 19 staging |
| 1.3 | Studio customisations checked item by item: fields, views, reports, automations, server actions, access rules | 18–21 Oct | Functional Technical | 1.2 | Studio checklist |
| 1.4 | Third-party modules per register: simplify_access_management advanced_web_domain_widget auditlog hide_menu_user Hikvision attendance muk_web_utils notify_email_inbox muk_mcp muk_mcp_access paymob pos_paymob, and any found in the environment scan. paymob → Odoo 19 standard Paymob provider; MCP replacement proposed (D-04). Nothing removed without approval. | 18–22 Oct | Technical IT | 1.2, I-04 | Status per module |
| 1.5 | Pre-validation per company (six), before vs after: trial balance, aged AR/AP, tax reports, fiscal positions, stock valuation, open invoices and bills; every difference explained | 20–22 Oct | Project Manager QA | 1.3, 1.4 | Report per company |
| 1.6 | Key flows on the agreed checklist: purchase → receipt → bill → payment; sale → delivery → invoice → payment; journals; bank reconciliation; inter-company; access rights | 20–22 Oct | QA Functional | 1.3, 1.4 | Checklist results |
| 1.7 | Department validation: finance per company, procurement, inventory and every department on their own POs, journals and invoices | 25–28 Oct | Finance Departments | 1.5, 1.6 | Issue list |
| 1.8 | Fixes and re-tests for every issue raised | 25–29 Oct | Technical | 1.7 | Issues closed |
| 1.9 | Finance sign-off, per company M2 | Thu 29 Oct | Finance | 1.8 | Signed forms · M2 |
| 1.10 | Production runbook: timings, owners, checks, rollback by restore of the pre-upgrade backup | 1–3 Nov | Technical | M2 | Runbook |
| 1.11 | Production upgrade outside working hours: backup → upgrade → technical checks → finance spot checks → released before Sunday M3 | Fri–Sat 6–7 Nov | Technical Finance IT | 1.10, D-03 | Post-upgrade checks · M3 |
| 1.12 | First-week monitoring; priority support for all Odoo 19 users | 8–12 Nov | Project Manager | M3 | Issue log |

TASK LIST

# Tasks by Workstream (continued)

## WS 2 Structure, finance & access

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 2.1 | Architecture: one company Urban Eats (one CR, VAT, chart of accounts); analytic plans Brand (MYLK, Finjan, Shared) and Branch (one per outlet + Central Kitchen); warehouse + POS per outlet; Odoo “Branches” not used | 18–22 Oct | Project Manager Co-founder | 0.9 | Approved 29 Oct |
| 2.2 | D-02 POS revenue tagging: Option 1 standard (journal per POS) or Option 2 module (existing community module tested first) | by 29 Oct | Owner Finance | 2.1 | Decision |
| 2.3 | Company: CR, VAT, ZATCA address fields, fiscal year, Saudi chart of accounts, taxes, banks, one sales + invoice journal per POS | 1–3 Nov | Functional | M1, I-11 | Configured |
| 2.4 | Analytic plans and accounts; applicability mandatory on income and expense; distribution models by product category, supplier and account | 3–5 Nov | Functional | 2.3 | Configured |
| 2.5 | Shared finance: “Urban Eats – Shared” tagging and allocation rule; B2B sales team, pricelist, payment terms | 8–10 Nov | Functional | 2.4 | Configured |
| 2.6 | Access & brand visibility: user groups per role; POS employee PIN; POS restricted categories per brand; backend access rule per brand group; outlet staff on own POS and warehouse only | 8–12 Nov | Functional Technical | 2.1, I-18 | Role matrix |
| 2.7 | Option 2 module (if chosen): Brand / Branch on POS configuration, stamped on session revenue lines and POS invoices; built on an upgrade-safe hook | 8–19 Nov | Technical | D-02 | Module + note |

## WS 3 Product master, procurement & inventory

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 3.1 | Product structure: categories (Purchased · Semi-finished BASE · Finished per brand · Shared), naming rule, internal references, AVCO costing | 25–29 Oct | Project Manager Functional | 0.9 | D-05 · 29 Oct |
| 3.2 | Templates completed: suppliers, vendor prices, pack sizes, supplier barcodes | by Thu 5 Nov | Procurement | 0.8 | Templates |
| 3.3 | Warehouses: Main (buy), Central Kitchen (manufacture, resupplied from Main), one per outlet incl. portable units (resupplied from Main and Central Kitchen); routes | 1–5 Nov | Functional | M1 | Configured |
| 3.4 | Units & packagings (Odoo 19): e.g. Bottle 3 L = 3 L, Carton 12 × 1 L, ml; lots and expiry where needed | 1–5 Nov | Functional | 3.1 | Configured |
| 3.5 | One generic material per ingredient; supplier products as vendor lines (code, purchase unit, price); packaging barcodes. Test: 4 bottles received = 12 L | 8–12 Nov | Functional | 3.2, 3.4 | Receipt test passed |
| 3.6 | Initial min / max levels per location | by Thu 12 Nov | Inventory | 3.3 | Levels sheet |
| 3.7 | Reordering rules at Main, Central Kitchen and outlets; Replenishment report tested | 15–19 Nov | Functional | 3.5, 3.6 | Rules active |

TASK LIST

# Tasks by Workstream (continued)

## WS 3 Product master, procurement & inventory

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 3.8 | Scrap reasons; production cost from materials (labour and overhead per D-10) | 15–19 Nov | Functional | 3.5 | Configured |
| 3.9 | Foundation configured, shown on staging M4 | Thu 12 Nov | Project Manager Owner | 2.3–3.5 | M4 |

## WS 4 Central kitchen manufacturing

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 4.1 | Recipe / BoM template: ingredients, quantities, yield, shelf life, make-to-stock, make-to-order or no-carry-over | Thu 15 Oct | Project Manager | — | Template |
| 4.2 | BoM workshops with the kitchen lead: recipes built from scratch (Foodics holds none), top sellers first | 25 Oct–5 Nov | Functional Kitchen Lead | 4.1, 3.1 | Completed templates |
| 4.3 | BoMs loaded: manufacture BoMs (multi-level for BASE items) and kit BoMs for outlet menu items | 8–12 Nov | Functional | 4.2, 3.5 | Signed by kitchen lead |
| 4.4 | Daily plan: Master Production Schedule + reordering rules → manufacturing orders in Central Kitchen → automatic consumption → transfers to outlets | 15–19 Nov | Functional | 4.3, 3.7 | Flow on staging |
| 4.5 | “What to make today” on the Shop Floor screen: produce, record quantity, scrap | 15–19 Nov | Functional | 4.4 | Screen shown |
| 4.6 | Expiry dating (first-expiry-first-out); end-of-day disposal list for no-carry-over items; waste with reasons | 22–24 Nov | Functional | 4.4 | Configured |
| 4.7 | Kits at outlets: each POS sale deducts ingredients from that outlet’s stock | 22–26 Nov | Functional | 4.3, 5.4 | Stock deduction verified |
| 4.8 | Kitchen flow ready: walk-through with the kitchen lead M5 | Thu 26 Nov | Kitchen Lead | 4.4–4.7 | M5 |

## WS 5 Restaurant POS & Kitchen Display

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 5.1 | Hardware & network spec issued; devices ordered: POS units, receipt and kitchen printers, KDS screens, terminals | Spec 29 Oct · on site 26 Nov<br>Spec issued 29 Oct; devices on site 26 Nov | Technical IT | 0.11 | Devices on site |
| 5.2 | Menus per brand validated from the Foodics export: items, prices, active status | by Thu 5 Nov | Operations | 12.2 | Validated files |
| 5.3 | POS per outlet × brand: restaurant mode, outlet warehouse, own journals, restricted categories, pricelist, presets (dine-in, takeaway, delivery), payment methods incl. one per platform, receipt header, cash control | 8–12 Nov | Functional | 2.3, 3.3 | Configured |

TASK LIST

# Tasks by Workstream (continued)

## WS 5 Restaurant POS & Kitchen Display

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 5.4 | Menus loaded: POS categories, products, attributes (modifiers), combos, pricelists, taxes | 8–19 Nov | Functional | 5.2, 5.3 | Checked by outlet lead |
| 5.5 | Receipts with ZATCA QR; floor plans and tables for dine-in outlets | 15–19 Nov | Functional | 5.3 | Receipt approved |
| 5.6 | Kitchen Display per outlet: stations by POS category, stages | 15–19 Nov | Functional | 5.4 | Routing tested |
| 5.7 | Outlet procedure: network loss, session open / close, cash | 22–24 Nov | Project Manager | 5.3 | Procedure |
| 5.8 | Pilot-outlet hardware test: printers, KDS, terminals, network | 24–26 Nov | Technical IT Operations | 5.1, 8.5 | Test record |
| 5.9 | POS & payments ready M5 | Thu 26 Nov | Operations | 5.3–5.8 | M5 |

## WS 6 Delivery platforms (both options)

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 6.1 | Store map: every outlet × brand × platform with store IDs and merchant accounts | by Thu 22 Oct | Project Manager Operations | I-09 | Store map |

## WS 6A Delivery platforms: Option A hub

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 6.A1 | API access per merchant account, requested on Tara's behalf; weekly follow-up. Confirmed: HungerStation, Keeta, Jahez (incl. Noon). In progress: The Chefz, ToYou, Ninja, Mrsool | From 15 Oct · weekly<br>Ongoing from kick-off with weekly follow-up; no end date in v1.2 | Engagement Lead Platforms | 6.1 | API status weekly |
| 6.A2 | Integration plan per platform: endpoints, order states, menu / stock sync, cancellations | 25–29 Oct | Technical | 6.A1 | Plan |
| 6.A3 | Hub core in Tara's repository: Brand › Branch › Platform store › POS mapping; secure webhooks; orders into POS + KDS; menu and price push; sold-out sync; status write-back; retry queue, logs, alerts | 1–19 Nov | Technical | 6.A2, 5.3 | Core on staging |
| 6.A4 | Connectors: HungerStation, Jahez (incl. Noon), Keeta | 8–26 Nov | Technical | 6.A3 | Test orders end to end |
| 6.A5 | The Chefz, ToYou, Ninja, Mrsool: each built and tested once its API is issued | As APIs arrive<br>No fixed dates in v1.2: each connector is built when its API is issued | Technical Platforms | 6.A3 | Test orders |
| 6.A6 | Platform testing or certification where required | 22 Nov–17 Dec | Technical Platforms | 6.A4 | Platform confirmation |

TASK LIST

# Tasks by Workstream (continued)

## WS 6A Delivery platforms: Option A hub

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 6.A7 | A platform without API by go-live keeps its tablet; connected when ready, within scope | Go / No-Go v1.2: reviewed at Go / No-Go (Tue 29 Dec) | Engagement Lead | 6.A5 | Status per platform |

## WS 6B Delivery platforms: Option B UrbanPiper

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 6.B1 | Joint Odoo / UrbanPiper meeting: confirm Saudi coverage (Keeta, ToYou, The Chefz, Ninja), fees, onboarding time; subscription ordered via Odoo | by Thu 22 Oct | Owner Odoo UrbanPiper | I-07 | Coverage in writing |
| 6.B2 | UrbanPiper store per outlet × brand created from POS; platforms linked and "go live" requested per store | 25 Oct–19 Nov | Project Manager UrbanPiper | 6.B1, 5.3 | Stores linked |
| 6.B3 | Food Delivery Connector: products flagged for delivery, menu sync, store timings, payment method per platform, routing to POS + KDS; combos mapped to attributes (not supported by UrbanPiper) | 15–26 Nov | Functional | 6.B2, 5.4 | Configured |
| 6.B4 | Connector shown on staging; HungerStation orders are rejected in the HungerStation app, not in Odoo | Thu 26 Nov | Project Manager | 6.B3 | Demo held |

## WS 6 Delivery platforms (both options)

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 6.9 | Platforms connected in test (either option), subject to platform approvals M6 | Thu 26 Nov | Operations | 6.A4 / 6.B4 | M6 |

## WS 7 Settlement & reconciliation

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 7.1 | Payout statements and reports: three months per platform | 25 Oct–5 Nov | Project Manager Finance | I-07 | Samples |
| 7.2 | Settlement plan and automation level, following Odoo's official response | 8–12 Nov | Project Manager Functional | 7.1, D-09 | Settlement plan |
| 7.3 | Clearing account per platform; import of statements; commission bill with VAT; promotions, refunds, cancellations, penalties, delivery charges; bank reconciliation | 15–26 Nov | Functional | 7.2 | Configured |
| 7.4 | Reports by platform, brand and branch; tested with a real payout per platform | 6–17 Dec | Functional Finance | 7.3 | UAT result |

## WS 8 Payments

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 8.1 | Odoo 19 availability confirmed for Geidea, NearPay and Paymob terminals, before you commit | 25–29 Oct | Technical | I-09 | Note → D-06 by 5 Nov |

TASK LIST

# Tasks by Workstream (continued)

## WS 8 Payments

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 8.2 | Merchant accounts and keys, test and live: Paymob (Saudi), Tabby, Tamara | by Thu 5 Nov | Finance | — | Keys shared securely |
| 8.3 | Paymob (standard Odoo 19 provider): test mode, methods synchronised, card incl. Mada. Apple Pay route per D-14 (not in Odoo's Paymob connector today) | 8–12 Nov | Technical | 8.2 | Test payments |
| 8.4 | Tabby & Tamara: through Paymob where enabled on your Paymob account (standard); a Code-ox module only for a method Paymob does not provide | 8–19 Nov | Technical | 8.2, 8.3 | Payments + refunds |
| 8.5 | POS terminal integration for the provider(s) in D-06 | 15–26 Nov | Technical IT | D-06, I-19 | Pilot-outlet test |
| 8.6 | Rules: paid only on terminal or gateway confirmation; refunds to original method; failed payments retried or switched; split payments | 22–26 Nov | QA | 8.3–8.5 | Test cases passed |

## WS 9 WhatsApp

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 9.1 | Meta Business verification, dedicated number, Business Manager access | by Thu 5 Nov | Marketing Meta | — | Verified account |
| 9.2 | Odoo WhatsApp connected to Meta (no third-party provider); templates on POS orders and invoices: receipts, order confirmations, customer messages | 8–12 Nov | Functional | 9.1 | Drafts |
| 9.3 | Templates submitted to Meta; kitchen and delivery status messages reviewed case by case (D-08) | by Thu 19 Nov | Functional Marketing | 9.2 | Meta approval |
| 9.4 | Automatic sending through automation rules; tested | 22–26 Nov | Functional | 9.3 | Messages received |

## WS 10 Loyalty, promotions & rewards

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 10.1 | Management session: each loyalty idea classed as standard, configuration, supported app or custom | 1–5 Nov | Project Manager Marketing | — | Ideas assessed |
| 10.2 | Programs agreed (D-07) | by Thu 12 Nov | Marketing | 10.1 | Program list |
| 10.3 | Discount & Loyalty programs per brand (limited to that brand's POS and website): points, rewards, coupons, promo codes, Buy X Get Y, gift cards, eWallet | 15–26 Nov | Functional | 10.2, 5.4 | Configured |
| 10.4 | Demo to your team; Foodics loyalty and gift-card balances loaded as available | Thu 26 Nov | Project Manager | 10.3, 12.1 | Demo held |

TASK LIST

# Tasks by Workstream (continued)

## WS 11 ZATCA Phase 2

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 11.1 | Saudi e-invoicing modules incl. POS; company ZATCA fields; invoice journal per POS; default walk-in customer | 1–12 Nov | Functional | 2.3 | Configured |
| 11.2 | Fatoora administrator nominated with simulation access | by Thu 19 Nov | Finance | — | Access confirmed |
| 11.3 | Simulation onboarding per POS journal (one-time code valid 60 minutes, scheduled together) and compliance checks | 22–26 Nov | Functional Finance ZATCA | 11.1, 11.2 | Compliance passed |
| 11.4 | UAT: simplified and standard invoices, credit notes, B2B clearance, rejected-invoice handling | 6–17 Dec | QA Finance | 11.3 | UAT result |
| 11.5 | Production onboarding per POS journal (switch is one-way) | 27–30 Dec | Functional Finance | M10 | Certificates |

## WS 12 Foodics extraction, loads & archive

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 12.1 | Foodics console and API access; data inventory; gap report on what cannot be exported (e.g. balances) | 15–22 Oct | Project Manager IT | I-05 | Gap report |
| 12.2 | Full extraction: menus, categories, products, modifiers, customers; history to date: orders, payments, discounts, refunds, inventory, balances, tax and financial reports, branch set-up | 15 Oct–5 Nov | Technical IT | 12.1 | Data set v1 in your storage |
| 12.3 | Field mapping per brand | 25 Oct–5 Nov | Functional | 12.2 | Mapping sheet |
| 12.4 | Clean-up by your team: prices, active items, duplicate customers | 1–5 Nov | Operations Marketing | 12.3 | Validated files |
| 12.5 | Trial load 1 into build environment; counts and samples checked | 8–12 Nov | Technical | 12.4, 3.9 | Load report |
| 12.6 | Trial load 2 into UAT environment | 29 Nov–1 Dec | Technical | 12.5 | Load report |
| 12.7 | Top-up export of new Foodics transactions | 13–17 Dec | Technical | 12.2 | Archive updated |
| 12.8 | Rehearsal load with the cutover method; timings recorded | 20–24 Dec | Technical | 14.2 | Rehearsal report |
| 12.9 | Menu freeze in Foodics; later changes applied in both systems by Code-ox | from Sun 27 Dec<br>v1.2: from Sun 27 Dec; end set to 31 Dec (last Foodics sale) as an assumption | Operations | — | Freeze notice |
| 12.10 | Final export after the last Foodics transaction | Thu 31 Dec (night) | Technical | M11 | Final export |
| 12.11 | Opening stock from physical count at every outlet, Main Warehouse and Central Kitchen, posted before the first sale | Thu 31 Dec (night) | Project Manager Inventory Operations | I-23 | Count sheets + adjustment |

TASK LIST

# Tasks by Workstream (continued)

## WS 12 Foodics extraction, loads & archive

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 12.12 | Final archive with index and data dictionary: dataset, period, content | 3–7 Jan | Project Manager | 12.10 | Archive handed over |

## WS 13 Testing, UAT & training

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 13.1 | Build testing: each item tested before it is shown to Tara | 1–26 Nov | QA Functional | — | Each item tested before it is shown |
| 13.2 | System integration test: end-to-end flows including platforms, payments and ZATCA simulation M7 | 22–30 Nov | QA Technical | 13.1 | Internal test report · M7 |
| 13.3 | UAT scenarios, scripts and calendar issued | 26 Nov | QA Project Manager Project Owner | 13.1, I-21 | UAT scripts (DL-12) |
| 13.4 | Key-user training (train-the-trainer) before UAT; role guides and quick-reference cards ready by Thu 3 Dec | 29 Nov–3 Dec | Project Manager Functional Key users | 13.3 | Key users trained; attendance recorded |
| 13.5 | UAT cycle 1: key users run all scenarios, guided by Code-ox; defects logged in Helpdesk | 6–10 Dec | QA Project Manager Finance Kitchen Lead Operations | M8, I-21 | All scenarios run; defects logged |
| 13.6 | UAT cycle 2 and day-in-the-life: re-tests with kitchen and one outlet team; a full trading day simulated | 13–17 Dec | QA Project Manager Finance Kitchen Lead Operations | 13.5 | Re-tests passed; full trading day simulated |
| 13.7 | Role training: finance (2 sessions), procurement & warehouse, central kitchen, marketing | 13–17 Dec | Project Manager Functional Finance Procurement Kitchen Lead Marketing | 13.4 | Attendance recorded per session |
| 13.8 | Outlet managers and cashiers by outlet group; IT / developer session | 20–24 Dec | Project Manager Functional Operations IT | 13.7 | Attendance recorded per session |
| 13.9 | Regression testing before UAT acceptance | 20–24 Dec | QA | 13.6 | Regression results; no open Critical or High issue |
| 13.10 | Refresher and go-live briefing | 27–30 Dec | Project Manager Operations Finance | 13.8 | Briefing held |

TASK LIST

# Tasks by Workstream (continued)

## WS 14 Cutover preparation

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 14.1 | Cutover runbook and contingency plan (within Odoo) | 13–17 Dec | Project Manager Technical | 13.5 | Runbook |
| 14.2 | Cutover rehearsal on a fresh production copy; timings recorded | 20–24 Dec | Technical IT | 14.1 | Rehearsal report |
| 14.3 | UAT acceptance; code freeze M9 | Thu 24 Dec | Owner | 13.6 | M9 |
| 14.4 | Count teams, count sheets, outlet go-live contacts; Foodics end date (D-12) | by Thu 24 Dec | Inventory Operations | I-23 | Count plan |
| 14.5 | Urban Eats deployed to production: modules from your repository, configuration, master data, users (no transactions) | 27–28 Dec | Technical Project Manager | M9 | Deployment checklist |
| 14.6 | Go / No-Go against the checklist below M10 | Tue 29 Dec | Co-founder Owner Sponsor | 14.5 | M10 |
| 14.7 | ZATCA production onboarding per POS journal; refresher training | 29–30 Dec | Functional Finance | M10 | Certificates |
| 14.8 | Final checks at every outlet: devices, printers, KDS, terminals, network, platform stores | Wed 30 Dec | Technical Operations | 14.5 | Outlet checklist |

## WS 15 Hypercare, handover & support

| ID | TASK | WHEN | OWNER | NEEDS | OUTPUT |
|---|---|---|---|---|---|
| 15.1 | Hypercare: daily check-in with the Project Owner; tickets through Helpdesk, phone or WhatsApp under the SLA | 3–14 Jan | Project Manager Engagement Lead | M12 | Issue log |
| 15.2 | Final Foodics archive with index and data dictionary (12.12) | 3–7 Jan | Project Manager | 12.10 | Archive |
| 15.3 | Go-live report: what went live, open items, platform status, next steps | Thu 7 Jan | Project Manager Co-founder | M12 | Report |
| 15.4 | Go-live acceptance feedback within 5 business days | by Thu 7 Jan | Owner | 15.3 | Acceptance |
| 15.5 | Handover pack: source in your repository, deployment notes, migration scripts, technical, integration / API and configuration documents, walked through with your developer M13 | 10–14 Jan | Technical IT | M12 | Signed · M13 |
| 15.6 | Six months of support under the SLA M14 | 1 Jan–30 Jun 2027 | Engagement Lead | M12 | M14 |

INPUTS AND DECISIONS

# What Tara Holding Provides

Tara Holding owes 24 inputs and 14 decisions. Ten of the inputs fall due by 22 October, so the first week carries the most. A late input moves the tasks that depend on it.

| 24 | 10 | 14 | 1 Dec |
|---|---|---|---|
| inputs from Tara Holding | inputs due by 22 October | decisions | UAT environment, committed |

## Inputs

| ID | INPUT | DUE | OWNER | UNBLOCKS |
|---|---|---|---|---|
| I-01 | Signed agreement and advance payment | Thu 15 Oct | Sponsor | 0.1 |
| I-02 | Project owner and key users named per area | Thu 15 Oct | Sponsor | 0.9 |
| I-03 | Odoo.sh access, staging URL + admin login, GitHub read access; Code-ox on the subscription | Thu 15 Oct | IT | 1.1 · critical |
| I-04 | Licences and source of third-party modules | Thu 15 Oct | IT | 1.4 |
| I-05 | Foodics items F1–F9 | 15–22 Oct | IT, Operations | 12.1 |
| I-06 | Requirement questionnaires answered per area | Thu 22 Oct | All leads | 0.9 |
| I-07 | Platform merchant accounts (A) or UrbanPiper order (B); payout samples | Thu 22 Oct | Operations | 6.A1 / 6.B1 |
| I-08 | Finance validator per company; validation checklist input | Thu 22 Oct | Finance | 1.5 |
| I-09 | Outlet list: brand, address, hours, devices, platform store IDs | Thu 22 Oct | Operations | 6.1, 0.11 |
| I-10 | Repository for custom code in Tara's name | Thu 22 Oct | IT | 2.7, 6.A3 |
| I-11 | Urban Eats CR, VAT, address, accounts, banks | Thu 29 Oct | Finance | 2.3 |
| I-12 | Suppliers, vendor prices, pack sizes, barcodes | Thu 5 Nov | Procurement | 3.5 |
| I-13 | Paymob, Tabby, Tamara merchant accounts and keys | Thu 5 Nov | Finance | 8.3 |
| I-14 | Validated menus per brand; recipes / BoMs | Thu 5 Nov | Operations, Kitchen Lead | 4.3, 5.4 |
| I-15 | Meta verification, WhatsApp number, access | Thu 5 Nov | Marketing | 9.2 |
| I-16 | Initial minimum stock levels | Thu 12 Nov | Inventory | 3.7 |
| I-17 | Fatoora administrator and access | Thu 19 Nov | Finance | 11.3 |
| I-18 | User list with roles, incl. cashiers | Thu 19 Nov | Operations | 2.6 |
| I-19 | POS hardware, KDS, terminals, network on site | Thu 26 Nov | IT | 5.8, 8.5 |
| I-20 | Odoo subscription updated (count from Code-ox by 12 Nov) | Thu 26 Nov | IT | M8 |
| I-21 | UAT testers and calendar | Thu 26 Nov | Owner | 13.5 |
| I-22 | Training attendance lists | Thu 3 Dec | Operations | Training |
| I-23 | Stock count teams; outlet go-live contacts | Thu 24 Dec | Inventory | 12.11 |
| I-24 | Fatoora codes on call; outlet managers on cutover night | 27–31 Dec | Finance, Operations | 11.5, 14 |

TEAM AND GOVERNANCE

# Team, Roles & Governance

Raghib Ali Rafeeque is Tara's single point of contact, Shayar CV runs delivery day to day, and Thayif Kabir oversees the engagement and chairs five steering reviews between 29 October and 24 December.

### Code-ox Technologies

- **Engagement Lead**: Raghib Ali Rafeeque. First contact for Tara: commercial matters, change requests, platform API requests, joint Odoo / UrbanPiper meetings.
- **Project Manager**: Shayar CV. Runs delivery day to day across all workstreams; owns the tracker and the Thursday status report.
- **Overall monitoring**: Thayif Kabir, Co-founder. Odoo 19 certified solution architect. Approves the architecture and every custom module design, reviews quality at M1, M2, M8 and Go / No-Go, and is the final escalation.
- **Head of Operations**: Shabeeb K. Resourcing and team allocation.

### Tara Holding

- **Project Owner**: Eng. AbdulRahman Al-Nouman. Decisions, approvals and access; chairs Go / No-Go with the sponsor.
- **Executive Sponsor**: To be confirmed. Steering member; final Go / No-Go.
- **Area leads**: Finance (plus one validator per company), Procurement & Inventory, Central Kitchen, Operations and outlet managers, Marketing, IT. Validation, recipes, menus, POS, loyalty, WhatsApp, access, devices and handover.

## How we stay in sync

| FORUM | WHEN | WHO | COVERS |
|---|---|---|---|
| **Kick-off** | Thu 15 Oct, 2 hours | Both teams, sponsor, Co-founder | Scope, this plan, access checklist, requirement questionnaires, D-01 |
| **Status report** | Every Thursday | Project Manager to Project Owner | Per workstream: on track, at risk or late; done, next, risks, Tara actions due |
| **Steering review** | 29 Oct, 12 Nov, 26 Nov, 10 Dec, 24 Dec | Co-founder, Engagement Lead, Project Manager, Owner, Sponsor | Milestones, risks, decisions, change requests |
| **Live tracker** | Always | Everyone, via portal | Code-ox Odoo Project: tasks, dates, dependencies, Gantt; Helpdesk for UAT defects and support tickets |

**CHANGE CONTROL**

Change requests are logged in the tracker, and the impact on scope, cost and dates is given before any work starts. Work begins only on written approval. Code freeze starts on **24 December**, with Critical fixes only.

INPUTS AND DECISIONS

# Decisions Needed from Tara Holding

Each decision is due on the date shown so the tasks that depend on it can start on time.

| ID | DECISION | DUE |
|---|---|---|
| D-01 | Delivery layer: Option A (Code-ox hub) or B (UrbanPiper) | Thu 15 Oct |
| D-02 | POS revenue tagging: Option 1 standard or Option 2 module | Thu 29 Oct |
| D-03 | Production upgrade window: 6–7 Nov (planned) or 31 Dec | Thu 29 Oct |
| D-04 | Treatment of each third-party module, incl. MCP replacement | Thu 29 Oct |
| D-05 | Product categories, naming and coding | Thu 29 Oct |
| D-06 | POS terminal provider(s): Geidea, NearPay, Paymob | Thu 5 Nov |
| D-10 | Labour and overhead in production cost | Thu 5 Nov |
| D-14 | Apple Pay route on the website | Thu 5 Nov |
| D-07 | Loyalty and promotion programs | Thu 12 Nov |
| D-08 | Kitchen / delivery status messages on WhatsApp | Thu 12 Nov |
| D-09 | Settlement automation level | Thu 12 Nov |
| D-11 | Training languages and format | Thu 26 Nov |
| D-12 | Foodics end date (read-only until archive verified) | Thu 24 Dec |
| D-13 | Go / No-Go | Tue 29 Dec |

**DATES AND CONDITIONS**

The 1 December and 1 January dates hold if the agreement is signed and kick-off is held by **15 October**, inputs arrive on the dates in this plan, UAT feedback is timely, and delivery-platform approvals come through.

**DATES IN THIS PLAN**

Dates are expected dates from Execution Plan v1.2 (12 October 2026). They move with the signed agreement, Tara's inputs and platform approvals.

RISKS

# Top Risks and How They Are Managed

Twelve risks are reviewed every Thursday. The ones that can most directly move the 1 December and 1 January dates are late delivery-platform APIs (R1, R2), rebuilding product and recipe data (R5), and validating six companies in one week (R4).

| ID | RISK | MITIGATION | OWNER |
|---|---|---|---|
| **R1** | **Platform APIs issued late (A)** | Requested already; weekly follow-up; built in order of arrival; late platform keeps its tablet | Code-ox |
| **R2** | **UrbanPiper coverage (B): ToYou and The Chefz are not in Odoo's UrbanPiper list today; Ninja not listed for KSA** | Confirm in the joint meeting by 22 Oct; uncovered platform stays on tablet or uses a direct connector | Tara, UrbanPiper |
| **R3** | **A third-party module has no Odoo 19 version** | Register by 22 Oct; migrate or replace; nothing removed without approval | Code-ox |
| **R4** | **Six companies validated in one week** | Before / after reports prepared so finance reviews differences only | Both |
| **R5** | **No recipes in Foodics; product data needs rebuilding** | Templates Day 1; BoM workshops Weeks 2–3; top sellers first | Tara |
| **R6** | **Foodics cannot export some data (e.g. balances)** | Gap report by 22 Oct; approach agreed early | Code-ox |
| **R7** | **Hardware, terminals or network late** | Spec 29 Oct; on site 26 Nov; pilot test | Tara |
| **R8** | **Key users unavailable in December** | Testers and calendar named by 26 Nov | Tara |
| **R9** | **ZATCA issue near go-live** | Simulation passed 26 Nov; one-time code process rehearsed | Both |
| **R10** | **Apple Pay not in Odoo's Paymob connector** | Route decided by 5 Nov (D-14) | Code-ox |
| **R11** | **Lot-tracked ingredients inside POS kits (known Odoo issue)** | Lots and expiry kept in Central Kitchen; outlet kit ingredients untracked | Code-ox |
| **R12** | **Late scope changes** | Change control; code freeze from 24 Dec | Both |
