PROJECT EXECUTION PLAN · VERSION 1.0 · 11 OCTOBER 2026

# From Kick-off to Go-live on 1 January 2027

The complete, week-by-week execution of the Odoo 18 → 19 upgrade and the Urban Eats / MYLK implementation: every task, owner, date, input and sign-off, so your team can see how each of the coming months is managed.

| KICK-OFF | UPGRADE SIGN-OFF | UAT ENVIRONMENT | GO-LIVE | SUPPORT |
|---|---|---|---|---|
| 15 Oct | 29 Oct | 1 Dec | 1 Jan | 30 Jun |
| 2026 · latest | all six companies | committed | 2027 · committed | 2027 · six months |

## SIX PHASES

| PHASE 1 | PHASE 2 | PHASE 3 | PHASE 4 | PHASE 5 | PHASE 6 |
|---|---|---|---|---|---|
| **Mobilise & design** | **Odoo 19 upgrade** | **Build Urban Eats** | **UAT & training** | **Cutover & go-live** | **Hypercare & support** |
| 11 – 29 Oct | 18 Oct – 7 Nov | 1 – 30 Nov | 1 – 24 Dec | 27 Dec – 1 Jan | 1 Jan – 30 Jun |

**122 tasks with owners and dates**
Across every workstream, each loaded into Odoo Project on your own Odoo.

**Staging first, production last**
Every department validates and finance signs off each company before production is touched.

**Weekly visibility**
Sunday steering, Thursday demo on staging and a written status report every week.

**Your inputs and decisions dated**
23 inputs and 13 decisions, each tied to the task that needs it.

| DOCUMENT | COMPANION TO | DATE | PREPARED BY |
|---|---|---|---|
| Execution Plan v1.0 | CX-TARA-2026-02 Rev. 1 | 11 October 2026 | Code-ox Technologies |

INTRODUCTION

# Purpose, Principles & Key Dates

### What this document is

- The execution plan for Financial Proposal **CX-TARA-2026-02 Rev. 1**: Part 1 (Odoo 18 → 19 upgrade) and Part 2 (Urban Eats / MYLK implementation).
- It expands the weekly plan on page 8 of the proposal into **every task, owner, date, input and sign-off** from kick-off to the end of support.
- Every task ID here is loaded into **Odoo Project on your own Odoo** by Sun 18 Oct, so your team sees status, owner and due date at any time.

### How the plan is run

- **Standard Odoo first**: standard › configuration › Studio › supported module › custom development, each custom item justified in writing and approved by you.
- **Nothing reaches production untested**: upgrade validated on staging and signed off by every department before production is touched.
- **Continuity of data**: your POs, journal entries, invoices and history continue in Odoo 19 in the same database. Nothing is re-keyed into a separate system.
- **No surprises**: weekly steering, a Thursday demo on staging and a written status report every week.

## Milestones

| # | MILESTONE | TARGET DATE | CONFIRMED BY | EVIDENCE |
|---|---|---|---|---|
| **M0** | **Agreement signed & kick-off held** | By Thu 15 Oct 2026 | Both parties | Signed agreement; kick-off minutes |
| **M1** | **Upgrade assessment & Urban Eats architecture approved** | Tue 27 Oct | Tara project owner | Approved assessment, module register and architecture document |
| **M2** | **Upgrade signed off on staging** (all six companies) | Thu 29 Oct | Tara finance, per company | Signed before / after validation per company |
| **M3** | **Production upgraded to Odoo 19** (existing companies) | Weekend 5–7 Nov | Tara finance + IT | Post-upgrade checks signed; see decision D-03 |
| **M4** | **Urban Eats foundation configured** | Thu 12 Nov | Tara project owner | Thursday demo on staging |
| **M5** | **Central kitchen flow, POS & payments ready** | Thu 26 Nov | Tara kitchen + outlets | Thursday demo; hardware test at pilot outlet |
| **M6** | **Delivery platforms connected in test** | Thu 26 Nov | Tara outlets | Test orders per connected platform, subject to platform approvals |
| **M7** | **Internal testing complete; migration data loaded** | Mon 30 Nov | Code-ox | Internal test report |
| **M8** | **Production-ready UAT environment live** | **Tue 1 Dec 2026** | Committed date | UAT environment handed over with logins and scripts |
| **M9** | **UAT acceptance** | Thu 24 Dec | Tara project owner | UAT report; no open Critical or High issues |
| **M10** | **Go / No-Go decision** | Tue 29 Dec | Steering committee | Go / No-Go checklist signed |
| **M11** | **Ready for cutover** | Thu 31 Dec | Both parties | Cutover runbook steps complete |
| **M12** | **Production go-live**: no new transactions on Foodics | **Fri 1 Jan 2027** | Committed date | POS selling, ZATCA accepted, platform orders flowing |
| **M13** | **Hypercare complete; source & documentation handed over** | Thu 14 Jan 2027 | Tara project owner + IT | Handover pack signed |
| **M14** | **Six-month support ends** | Wed 30 Jun 2027 | Both parties | Support close-out; AMC at your option |


**DATES AND CONDITIONS**

Dates assume kick-off by **Thu 15 Oct 2026**. An earlier kick-off adds buffer and leaves every date unchanged. The 1 December and 1 January commitments rely on the conditions already in the proposal: signed agreement and kick-off by 15 October, access and data on the dates in Section 15, timely UAT feedback, and delivery-platform approvals, which neither party controls. Working week: Sunday–Thursday, Riyadh time.

PLAN AT A GLANCE

# Gantt: Kick-off to Handover

One view of every workstream across the fourteen weeks. Detailed tasks for each bar follow in Sections 3–13.

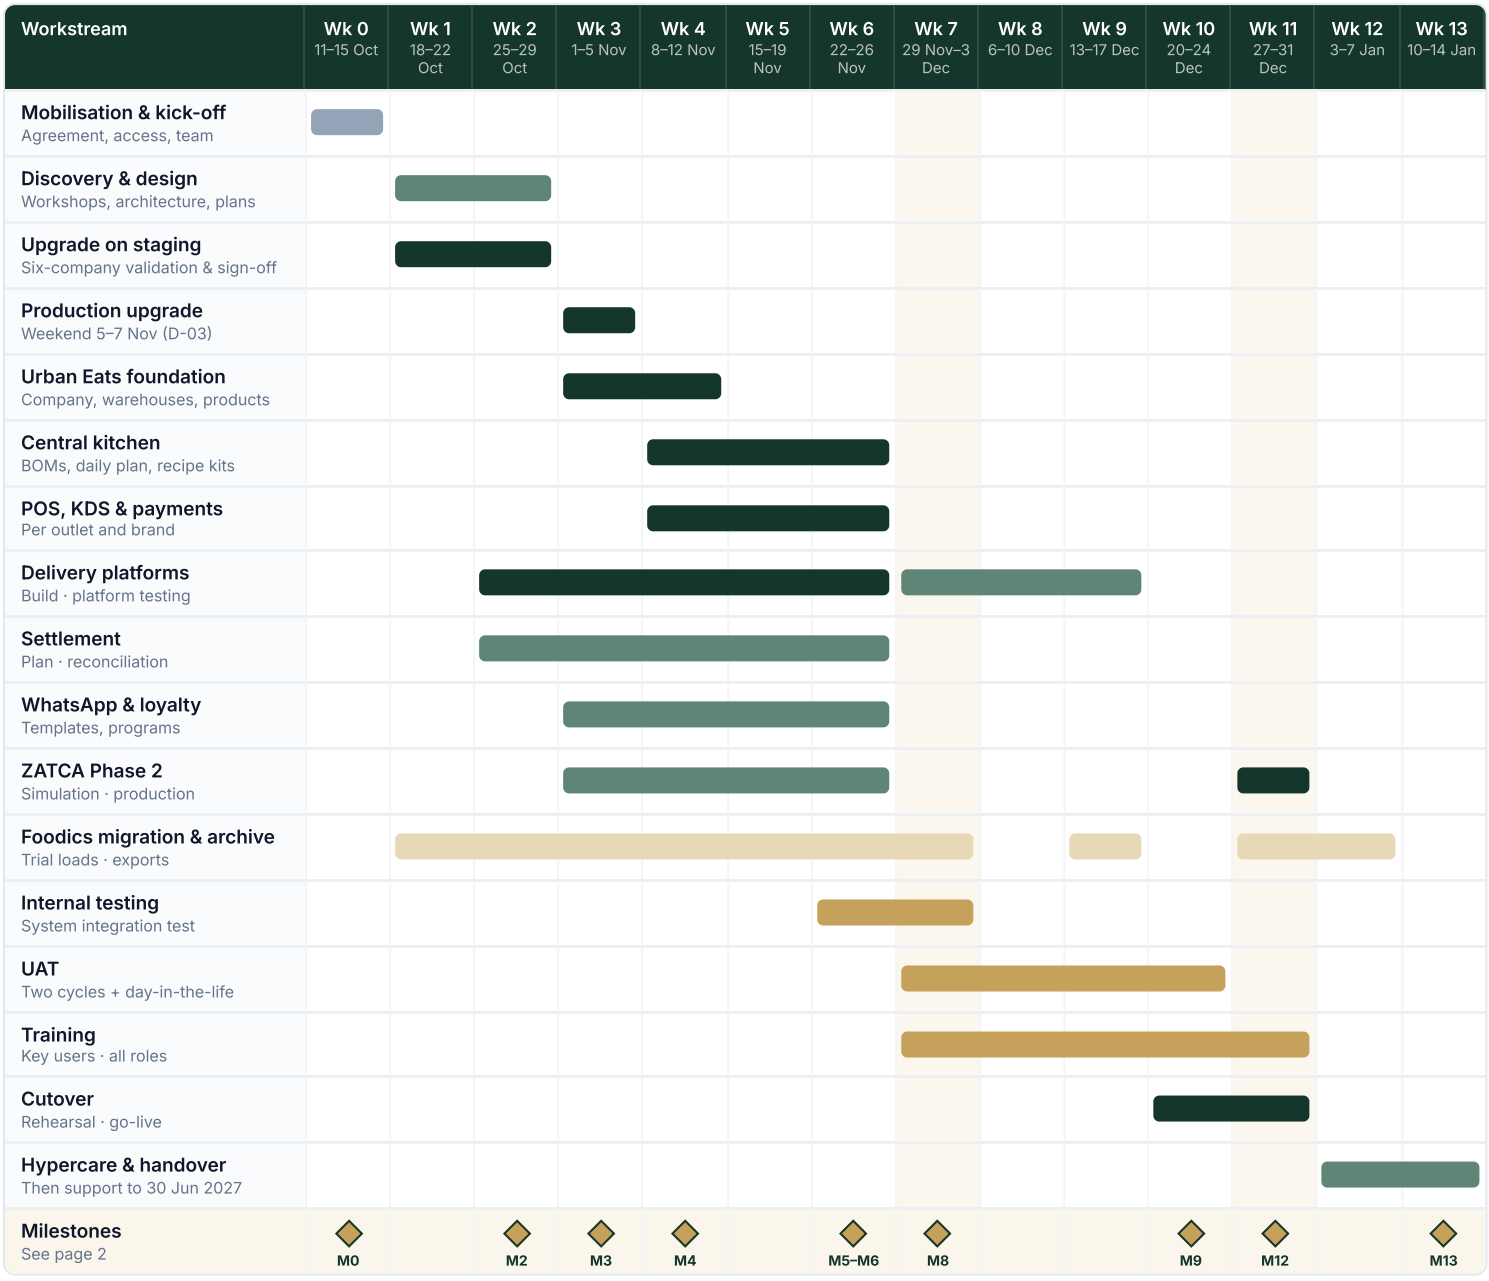


### CRITICAL PATH

Odoo.sh access at kick-off → staging upgrade (Wk 1) → finance sign-off (Wk 2) → foundation (Wk 3–4) → kitchen, POS & platforms (Wk 4–6) → UAT environment **1 Dec** → UAT sign-off **24 Dec** → go-live **1 Jan**.

### HIGHLIGHTED COLUMNS

**Wk 7**: the UAT environment goes live on Tue 1 Dec. **Wk 11**: cutover week, ending on the night of Thu 31 Dec for go-live on Fri 1 Jan 2027.

SECTION 1

# Team, Roles & Governance

### Code-ox Technologies

- **Engagement Lead**: Raghib Ali Rafeeque. Single point of contact for commercial matters and steering; owns the plan and weekly report.
- **Lead Functional Consultant (Odoo 19 Certified)**: Thayif Kabir. Business consultant across all departments; leads workshops, architecture, upgrade validation and UAT.
- **Technical Lead**: upgrade execution, module migration, deployment, code review and the repository in your name.
- **Odoo Developers**: aggregator integration, Tabby / Tamara, POS terminals, the optional tagging module.
- **QA Engineer**: test scripts, system integration test, regression, defect tracking.
- **Head of Operations**: Shabeeb K. Executive escalation and resourcing.

### Tara Holding (names confirmed at kick-off)

- **Project Owner & single point of contact**: Eng. AbdulRahman Al-Nouman (to confirm). Decisions, approvals, access.
- **Executive Sponsor**: chairs steering; final Go / No-Go.
- **Finance Lead** and a **validator for each of the six companies**: upgrade sign-off, chart of accounts, settlement.
- **Procurement & Inventory Lead**: suppliers, products, stock rules, stock count.
- **Central Kitchen Lead**: recipes, production plan, expiry and waste rules.
- **Operations / Outlets Lead** with one manager per outlet: menus, POS, KDS, training.
- **Marketing Lead**: loyalty, promotions, WhatsApp templates.
- **IT / in-house developer**: Odoo.sh, repository, hardware, network, technical handover.

## Meetings & reporting

| FORUM | WHEN | WHO | PURPOSE |
|---|---|---|---|
| **Kick-off** | By Thu 15 Oct · 2 hrs | Both teams, sponsor | Scope recap, team, this plan, access checklist, decisions D-01 to D-03 |
| **Discovery workshops** | Sun 18 – Thu 22 Oct · daily | Consultant + area leads | One workshop per area (Section 3) |
| **Steering committee** | Every Sunday · 45 min | Sponsor, owner, Code-ox leads | Progress against plan, risks, decisions due, overdue inputs |
| **Thursday demo on staging** | Every Thursday from 12 Nov · 45 min | Owner + key users | Show what was built that week; collect feedback early |
| **Weekly status report** | Every Thursday by 18:00 | Code-ox to Tara | Status per workstream (on track, at risk, late), % complete, done, next week, risks, decisions, Tara actions due |
| **Daily stand-up** | 15 min · UAT (1–24 Dec), cutover & hypercare (27 Dec – 14 Jan) | Consultant, QA, key users | Defects, blockers, plan for the day |
| **Live tracker** | Always | Everyone | Odoo Project on your Odoo: every task ID, owner, due date and status |

## Escalation

| LEVEL | CODE-OX | TARA HOLDING | RESOLUTION TARGET |
|---|---|---|---|
| 1 | Lead Functional Consultant | Area lead | Same business day |
| 2 | Engagement Lead | Project Owner | Within 2 business days |
| 3 | Head of Operations | Executive Sponsor | Next steering, or within 3 business days |

SECTION 2

# Responsibilities, Environments & Change Control

**R** does the work · **A** accountable, approves · **C** consulted · **I** informed.

| ACTIVITY | CODE-OX LEAD | CODE-OX CONSULTANT | CODE-OX TECH | CODE-OX QA | TARA OWNER | TARA FINANCE & PROCUREMENT | TARA KITCHEN & OUTLETS | TARA IT |
|---|---|---|---|---|---|---|---|---|
| Project plan, tracker, weekly report | **A/R** | C | C | I | C | I | I | I |
| Discovery workshops | **A** | R | C | I | C | R | R | C |
| Upgrade assessment & module register | **A** | R | R | I | C | C | I | C |
| Upgrade validation on staging | I | **A/R** | R | R | C | R | C | C |
| Finance sign-off per company | I | C | I | I | **A** | R | I | I |
| Architecture document | C | **A/R** | C | I | **A** | C | C | C |
| Configuration & custom development | I | **A/R** | R | C | I | I | I | C |
| Master data, menus, recipes (provide & validate) | I | C | C | I | **A** | R | R | I |
| Delivery-platform API requests | **A/R** | C | R | I | C | I | C | I |
| Hardware, terminals, network on site | I | C | C | I | **A** | I | R | R |
| UAT scripts | I | **A/R** | C | R | C | C | C | I |
| UAT execution & acceptance | I | R | C | R | **A** | R | R | C |
| Training delivery / attendance | I | **A/R** | C | I | C | R | R | R |
| Cutover runbook | **A** | R | R | C | C | C | C | C |
| Physical stock count at cutover | I | C | C | I | **A** | R | R | I |
| Go / No-Go | R | C | C | C | **A** | C | C | C |
| Hypercare & handover | **A** | R | R | C | C | C | C | R |

### Environments

- **Production** (Odoo.sh): your live six companies. Upgraded only after sign-off; Urban Eats deployed to it in cutover week.
- **Staging, upgrade validation**: copy of production upgraded to Odoo 19 for the before / after checks.
- **Staging, build & UAT**: where Urban Eats is built, demonstrated each Thursday and accepted in UAT.
- **Repository**: owned by Tara Holding; all custom modules, migration scripts and deployment notes.
- The UAT environment on 1 Dec is built from a fresh copy of production using the **same deployment package** used at go-live. The method is proven on 1 Dec and again at the 20 Dec rehearsal before production.

### Change control & defects

- **Change request**: logged in the tracker, then Code-ox gives impact on scope, cost and timeline **within 3 business days**. Work starts only on your written approval.
- **Code freeze** from Thu 24 Dec: Critical fixes only until go-live.
- **Critical**: blocks selling, payment, orders, ZATCA or a sign-off; fixed same day.
- **High**: key function impaired, workaround exists; fixed within 2 business days.
- **Normal**: minor or cosmetic; fixed before the next UAT cycle.
- Every defect has an ID, owner, severity and status visible in the tracker.

SECTION 3

# Mobilisation & Discovery (Wk 0 – Wk 2)

Starts the moment the agreement is signed. The aim of the first two weeks is to lock the design in writing so the build runs without rework.

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| **0.1** | Solution demo to your team | Mon 12 Oct | Code-ox · Consultant<br>Tara · Owner | Demo held |
| **0.2** | Financial acceptance; agreement signed; advance invoice issued | By Thu 15 Oct | Tara · Sponsor<br>Code-ox · Lead | Signed agreement |
| **0.3** | **Kick-off**: scope recap, teams, this plan, cadence, access checklist; decisions D-01 to D-03 opened | By Thu 15 Oct | Code-ox · Lead<br>Tara · Owner | Kick-off minutes · M0 |
| **0.4** | Access granted: Odoo.sh (Code-ox as collaborator), staging confirmed, Code-ox registered as partner on your Odoo subscription | At kick-off · Sun 18 Oct latest | Tara · IT | Access checklist: **critical path** |
| **0.5** | Tracker loaded in Odoo Project on your Odoo: every task ID, owner and due date | Sun 18 Oct | Code-ox · Lead | Live tracker |
| **0.6** | Kick-off pack: team list, contacts, cadence, severity definitions, templates | Sun 18 Oct | Code-ox · Lead | Kick-off pack |

## Discovery workshops

| DATE | WORKSHOP | TARA ATTENDEES | FEEDS |
|---|---|---|---|
| Sun 18 Oct | **Technical**: Odoo.sh, staging, repository, the 11 third-party modules, integrations in use | IT / in-house developer | Upgrade assessment, module register |
| Sun 18 Oct | **Structure & finance**: Urban Eats company, MYLK / Finjan brands, outlets, channels, P&L needs, shared costs | Owner, Finance | Architecture document |
| Mon 19 Oct | **Procurement & inventory**: suppliers, pack sizes, coding, warehouses, replenishment, lots & expiry | Procurement, Inventory | Product master, routes, stock rules |
| Tue 20 Oct | **Central kitchen**: products, recipes, shelf life, daily plan, transfers, waste | Kitchen Lead | Manufacturing design |
| Wed 21 Oct | **Outlets, POS & payments**: service flow per brand, modifiers, combos, receipts, KDS stations, payment methods, terminals | Operations, outlet managers | POS / KDS design, hardware spec |
| Thu 22 Oct | **Delivery platforms & settlement**: stores per outlet, menus per platform, payouts and statements | Operations, Finance | Integration plan, settlement plan |
| Thu 22 Oct | **Marketing**: WhatsApp messages, loyalty and promotion ideas (follow-up on Tue 3 Nov) | Marketing | Templates, loyalty programs |

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| **0.7** | Written **upgrade assessment** & **module-by-module register**: compatibility, treatment (retain, migrate, replace, consolidate, retire), licence or vendor cost, risk | Tue 20 Oct | Code-ox · Tech Lead | Assessment + register |
| **0.8** | **Urban Eats architecture document** (Section 5) | Thu 22 Oct | Code-ox · Consultant | Document for approval |
| **0.9** | Data migration plan, import templates & Foodics gap report | Thu 22 Oct | Code-ox · Consultant | Plan + templates |
| **0.10** | Per-platform integration plan (Option A) or UrbanPiper configuration plan (Option B) | Thu 29 Oct | Code-ox · Tech Lead | Integration plan |
| **0.11** | POS hardware & network specification per outlet | Thu 29 Oct | Code-ox · Tech Lead | Spec for ordering |
| **0.12** | **Approval** of assessment, register and architecture; decisions D-02, D-04 | Tue 27 Oct | Tara · Owner | **M1** |

SECTION 4 · PART 1

# Odoo 18 → 19 Upgrade

Performed on staging first. Production is touched only after every department has validated its own data and your finance team has signed off each company.

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| 1.1 | Full backup of production; staging copy prepared on Odoo.sh | Sun 18 Oct | Code-ox · Tech Lead | Backup reference |
| 1.2 | Upgrade of the staging copy to Odoo 19 through Odoo's upgrade service | Sun 18 – Mon 19 Oct | Code-ox · Tech Lead · Odoo | Odoo 19 staging database |
| 1.3 | **Studio customisations** checked and corrected: custom fields, views, reports, automations, server actions, access rules | Mon 19 – Wed 21 Oct | Code-ox · Consultant | Studio checklist, item by item |
| 1.4 | **Third-party modules** handled per register: simplify_access_management, advanced_web_domain_widget, auditlog, hide_menu_user, Hikvision attendance, muk_mcp, muk_mcp_access, muk_web_utils, notify_email_inbox, paymob, pos_paymob. A replacement MCP app for Odoo 19 is proposed. **No module removed without your written approval.** | Mon 19 – Thu 22 Oct | Code-ox · Developers · Tara · IT (licences) | Register status per module |
| 1.5 | Code-ox pre-validation, **each of the six companies**, before vs after: trial balance; aged receivables & payables; tax reports & fiscal configuration; stock valuation; open customer invoices & vendor bills. Every difference listed with its cause, including where Odoo 19 itself changes a calculation or presentation. | Tue 20 – Thu 22 Oct | Code-ox · Consultant · Code-ox · QA | Validation report per company |
| 1.6 | Key business flows tested against the agreed checklist: purchase → receipt → bill → payment; sale → delivery → invoice → payment; journal entries; bank reconciliation; multi-company and inter-company configuration; access rights | Wed 21 – Thu 22 Oct | Code-ox · QA | Flow checklist results |
| 1.7 | **Department validation on staging**: finance for each company, procurement, inventory and every department using Odoo. Your users work on their own POs, journals and invoices in Odoo 19. | Sun 25 – Wed 28 Oct | Tara · Finance · Tara · Departments · Code-ox · Consultant (on call) | Issue list |
| 1.8 | Fixes and re-tests for every issue raised | Sun 25 – Wed 28 Oct | Code-ox · Tech Lead | Issues closed |
| 1.9 | **Sign-off by your finance team, per company** | Thu 29 Oct | Tara · Finance | Signed forms · **M2** |
| 1.10 | Production upgrade runbook: timings, owners, checks, rollback by restore of the pre-upgrade backup | Tue 3 Nov | Code-ox · Tech Lead | Runbook shared |
| 1.11 | **Production upgrade** outside working hours: Thu 5 Nov after close of business → backup → upgrade → technical checks → finance spot checks on Sat 7 Nov → release for Sunday | Thu 5 – Sat 7 Nov | Code-ox · Tech Lead · Tara · Finance · Tara · IT | Post-upgrade checks · **M3** |
| 1.12 | First-week monitoring and priority support for all users on Odoo 19 | Sun 8 – Thu 12 Nov | Code-ox · Consultant | Daily check-in notes |

**WHAT YOUR USERS WILL SEE**

Same database, same records: every PO, journal entry, invoice and history line continues in Odoo 19, alongside its new features. No separate system for old transactions.

**DECISION D-03: PRODUCTION UPGRADE TIMING**

Planned: production upgraded in its own weekend (5–7 Nov) after sign-off, so cutover night carries only the Urban Eats switch. Alternative: upgrade on the cutover night of 31 Dec. Please confirm by Thu 29 Oct.

SECTION 5 · PART 2

# Urban Eats Foundation: Structure, Products & Inventory

## WS 2 Structure & finance

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| 2.1 | Architecture document: Urban Eats as one company (one CR, one VAT number, one set of accounts); analytic plans **Brand** (MYLK, Finjan, Shared) and **Branch**; one warehouse and one POS per outlet, each POS with its own sales journal; one POS payment method per platform with its clearing account; reporting design; access model. Odoo's "Branches" feature is not used. | Thu 22 Oct | Code-ox · Consultant | Document · approval Tue 27 Oct |
| 2.2 | Decision D-02: POS revenue tagging, Option 1 (fully standard) or Option 2 (small isolated module) | Tue 27 Oct | Tara · Owner Tara · Finance | Decision recorded |
| 2.3 | Company set-up: CR, VAT, address, fiscal year, chart of accounts, taxes, journals, bank accounts | Sun 1 – Tue 3 Nov | Code-ox · Consultant Tara · Finance (data by Sun 25 Oct) | Configured |
| 2.4 | Analytic plans and distribution models: purchases, expenses and invoices tagged to brand automatically by product, category, supplier or account | Tue 3 – Thu 5 Nov | Code-ox · Consultant | Configured |
| 2.5 | Shared finance: "Urban Eats Shared" cost tagging and optional brand allocation; B2B sales team fulfilled from Main Warehouse or Central Kitchen | Sun 8 – Tue 10 Nov | Code-ox · Consultant | Configured |
| 2.6 | Access rules: central team sees everything; outlet staff see only their own POS and warehouse | Wed 11 – Thu 12 Nov | Code-ox · Consultant | Role matrix |
| 2.7 | Option 2 module (only if chosen in D-02): Brand and Branch on POS configuration, tags copied to session revenue lines at closing | Sun 8 – Thu 19 Nov | Code-ox · Developers | Module + justification note |

## WS 3 Product master, procurement & inventory

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| 3.1 | Product types and coding scheme proposed | Tue 27 Oct | Code-ox · Consultant | Decision D-05 by Thu 29 Oct |
| 3.2 | Supplier list, vendor price lists, pack sizes and supplier barcodes completed in templates | By Sun 1 Nov | Tara · Procurement | Completed templates |
| 3.3 | Warehouses: Main Warehouse (receives all supplier deliveries), Central Kitchen, one per outlet; locations; resupply routes | Sun 1 – Thu 5 Nov | Code-ox · Consultant | Configured |
| 3.4 | Units of measure and conversions; lot and expiry tracking where needed | Tue 3 – Thu 5 Nov | Code-ox · Consultant | Configured |
| 3.5 | One generic material per ingredient; supplier products as vendor lines with code, pack size and price, **converted automatically on receipt** | Sun 8 – Tue 10 Nov | Code-ox · Consultant | Loaded; receipt test passed |
| 3.6 | Initial minimum stock levels per location | By Thu 12 Nov | Tara · Inventory | Levels sheet |
| 3.7 | Minimum stock rules at Main Warehouse, Central Kitchen and outlets; automatic replenishment tested | Sun 15 – Tue 17 Nov | Code-ox · Consultant | Rules active in test |
| 3.8 | Waste recorded with reasons; production cost from materials (labour and overhead per decision D-10) | Sun 15 – Thu 19 Nov | Code-ox · Consultant | Configured |
| 3.9 | **Foundation configured**, shown at the Thursday demo | Thu 12 Nov | Code-ox · Consultant Tara · Owner | **M4** |

SECTION 6 · PART 2

# Central Kitchen, Restaurant POS & Kitchen Display

## WS 4 Central kitchen manufacturing

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| 4.1 | Recipe / BOM template issued: ingredients, quantities, yields, shelf life, make-to-stock, make-to-order or no-carry-over | Thu 22 Oct | Code-ox · Consultant | Template |
| 4.2 | Recipes for central kitchen products and outlet recipe kits completed | By Thu 5 Nov | Tara · Kitchen Lead | Completed template |
| 4.3 | Bills of materials loaded and checked with the kitchen lead | Sun 8 – Thu 12 Nov | Code-ox · Consultant | BOMs signed by kitchen lead |
| 4.4 | Daily production plan: demand plus minimum stock → manufacturing orders → automatic ingredient consumption → stock → transfers to outlets | Sun 15 – Thu 19 Nov | Code-ox · Consultant | Flow working on staging |
| 4.5 | One simple **"what to make today"** screen for kitchen staff | Sun 15 – Thu 19 Nov | Code-ox · Consultant | Screen demonstrated |
| 4.6 | Expiry dating; leftovers listed for daily disposal; waste with reasons | Sun 22 – Tue 24 Nov | Code-ox · Consultant | Configured |
| 4.7 | Outlet recipe kits: each POS sale deducts its ingredients from that outlet's stock | Sun 22 – Thu 26 Nov | Code-ox · Consultant | Stock deduction verified |
| 4.8 | **Kitchen flow ready**: walk-through with the kitchen lead | Thu 26 Nov | Tara · Kitchen Lead | **M5** |

## WS 5 Restaurant POS & Kitchen Display

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| 5.1 | Hardware & network spec issued; Tara orders devices: POS units, receipt and kitchen printers, KDS screens, card terminals, network per outlet | Spec Thu 29 Oct · on site by Thu 26 Nov | Code-ox · Tech Lead<br>Tara · IT | Devices on site |
| 5.2 | Menus per brand validated from the Foodics export: items, prices, active status | By Thu 5 Nov | Tara · Operations | Validated menu files |
| 5.3 | POS configuration per outlet and brand: sales journal, payment methods (incl. one per delivery platform), receipt header, cash control | Sun 8 – Thu 12 Nov | Code-ox · Consultant | Configured |
| 5.4 | Menus loaded: POS categories, products, modifiers / attributes, combos, pricelists, taxes | Sun 8 – Tue 17 Nov | Code-ox · Consultant | Menus checked by outlet lead |
| 5.5 | Receipts with ZATCA QR; floor plans and tables where dine-in applies | Sun 15 – Thu 19 Nov | Code-ox · Consultant | Receipt approved |
| 5.6 | Kitchen Display per outlet, routed by station | Sun 15 – Thu 19 Nov | Code-ox · Consultant | Routing tested |
| 5.7 | Offline mode, session opening / closing and cash procedure written for outlet staff | Sun 22 – Tue 24 Nov | Code-ox · Consultant | Outlet procedure |
| 5.8 | On-site hardware test at a pilot outlet: printers, KDS, terminals, network, offline behaviour | Tue 24 – Thu 26 Nov | Code-ox · Tech Lead<br>Tara · IT<br>Tara · Outlet manager | Test record |
| 5.9 | **POS & payments ready** | Thu 26 Nov | Tara · Operations | **M5** |

SECTION 7 · PART 2

# Delivery Platforms

The list is the same under both options: **HungerStation, Jahez (incl. Noon), Keeta, The Chefz, ToYou, Ninja, Mrsool**. The structure is the same too: Brand › Branch › Platform Store › POS / Kitchen, so a new branch or brand is added by configuration. Decision D-01 (Option A or B) is due at kick-off.

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| **6.1** | Store inventory: every outlet × brand × platform with store IDs and merchant accounts | By Thu 22 Oct | Tara · Operations<br>Code-ox · Consultant | Store map |

## WS 6A Option A: Code-ox Aggregator Hub

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| **6.A1** | API access requested from each platform on Tara Holding's behalf, per entity merchant account. Requests are already sent; follow-up every week. Confirmed: HungerStation, Keeta, Jahez (incl. Noon). In progress: The Chefz, ToYou, Ninja, Mrsool. | From kick-off · weekly | Code-ox · Lead<br>Platforms | API status in weekly report |
| **6.A2** | Per-platform integration plan: endpoints, order states, menu / stock sync, cancellations and rejections as each API allows | Thu 29 Oct | Code-ox · Tech Lead | Plan shared |
| **6.A3** | Hub core in your Odoo: orders into POS and Kitchen Display; menu and price push; sold-out and stock sync; status updates back; failure and retry handling; logs and alerts; multiple branches and store IDs | Sun 1 – Thu 19 Nov | Code-ox · Developers | Core on staging |
| **6.A4** | Platform connectors for HungerStation, Jahez (incl. Noon) and Keeta | Sun 8 – Thu 26 Nov | Code-ox · Developers | Test orders end to end |
| **6.A5** | Connectors for The Chefz, ToYou, Ninja and Mrsool, each built and tested within about 10 business days of its API being issued | As each API arrives | Code-ox · Developers<br>Platforms | Test orders end to end |
| **6.A6** | Platform-side testing or certification where a platform requires it | Sun 22 Nov – Thu 17 Dec | Code-ox · Developers<br>Platforms | Platform confirmation |
| **6.A7** | A platform whose API is not issued in time keeps its own tablet at go-live and is connected when its API arrives, within the agreed scope and price | Reviewed at Go / No-Go | Code-ox · Lead | Status per platform |

## WS 6B Option B: UrbanPiper (standard connector, configuration only)

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| **6.B1** | Joint Odoo / UrbanPiper meeting outcome; UrbanPiper subscription ordered through Odoo; Saudi coverage incl. Keeta confirmed | By Thu 22 Oct | Tara · Owner<br>Odoo<br>UrbanPiper | Subscription active |
| **6.B2** | UrbanPiper stores per outlet and brand; platform linking through UrbanPiper's onboarding (timing with UrbanPiper and the platforms) | Sun 25 Oct – Thu 19 Nov | UrbanPiper<br>Code-ox · Consultant | Stores linked |
| **6.B3** | Connector configuration: menu sync, store hours, payment method per platform, routing to POS and Kitchen Display | Sun 15 – Thu 26 Nov | Code-ox · Consultant | Configured |
| **6.B4** | Connector demonstrated on staging (HungerStation orders are rejected in the HungerStation app, not in Odoo POS) | Thu 26 Nov | Code-ox · Consultant | Demo held |

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| **6.9** | **Platforms connected in test**, subject to platform approvals | Thu 26 Nov | Tara · Operations | M6 |

SECTION 8 · PART 2

# Settlement & Payments

## WS 7 Settlement & reconciliation

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| 7.1 | Payout statements, reports and files collected from each platform | Sun 25 Oct – Thu 5 Nov | Tara · Finance<br>Code-ox · Consultant | Samples per platform |
| 7.2 | Settlement plan with automation level, following Odoo's official response (decision D-09) | Thu 12 Nov | Code-ox · Consultant | Settlement plan |
| 7.3 | Clearing account per platform; reconciliation of gross sales, commission, VAT on commission, promotions, refunds, cancellations, adjustments, penalties, delivery charges, net payout | Sun 15 – Thu 26 Nov | Code-ox · Consultant | Configured |
| 7.4 | Reports by platform, brand and branch; tested in UAT with a real payout statement from each platform | Sun 22 Nov – Thu 17 Dec | Code-ox · Consultant<br>Tara · Finance | UAT result |

## WS 8 Payments

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| 8.1 | Odoo 19 availability confirmed for Geidea, NearPay and Paymob terminals **before you commit** | Thu 29 Oct | Code-ox · Tech Lead | Written confirmation → D-06 by Thu 5 Nov |
| 8.2 | Merchant accounts and API keys (test and live): Paymob, Tabby, Tamara | By Sun 1 Nov | Tara · Finance | Keys shared securely |
| 8.3 | Paymob online payments: Mada, Visa / Mastercard, Apple Pay as enabled on your account | Sun 8 – Thu 12 Nov | Code-ox · Developers | Test payments |
| 8.4 | Tabby and Tamara integration built by Code-ox | Sun 8 – Thu 19 Nov | Code-ox · Developers | Test payments + refunds |
| 8.5 | POS terminal integration for the provider(s) chosen in D-06 | Sun 15 – Thu 26 Nov | Code-ox · Developers<br>Tara · IT (devices) | Terminal tests at pilot outlet |
| 8.6 | Rules: order marked paid only on terminal or gateway confirmation; refunds to the original method where supported; failed payments retried or switched | Sun 22 – Thu 26 Nov | Code-ox · Developers | Test cases passed |

**PAYMENT TESTING**

Every payment method is tested in test mode on staging, then with small live transactions at the pilot outlet during UAT and again in the go-live smoke test. Provider fees are paid directly to each provider (proposal, page 9).

SECTION 9 · PART 2

# WhatsApp, Loyalty & ZATCA

## WS 9 WhatsApp (standard Odoo Enterprise app)

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| 9.1 | Meta Business verification, dedicated number, Business Manager access | By Thu 5 Nov | Tara · Marketing<br>Meta | Verified account |
| 9.2 | WhatsApp connected to Odoo; templates drafted: receipts, order confirmations, customer messages | Sun 8 – Thu 12 Nov | Code-ox · Consultant | Drafts for approval |
| 9.3 | Templates submitted to Meta; kitchen and delivery status messages reviewed with you case by case before anything is built (D-08) | Submit by Thu 19 Nov | Code-ox · Consultant<br>Tara · Marketing | Meta approval |
| 9.4 | Automatic sending where possible; tested in UAT | Sun 22 – Thu 26 Nov | Code-ox · Consultant | Messages received in test |

## WS 10 Loyalty, promotions & rewards (MYLK)

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| 10.1 | Session with management: loyalty and promotion ideas, each assessed as standard, configuration, supported app or custom (last option) | Tue 3 Nov | Code-ox · Consultant<br>Tara · Marketing | Ideas assessed |
| 10.2 | Programs agreed (D-07) | By Thu 12 Nov | Tara · Marketing | Program list |
| 10.3 | Configuration: points and rewards; % and fixed discounts; coupons and promo codes; Buy X Get Y; gift cards and eWallet; POS and eCommerce; validity and conditions; separate programs per brand | Sun 15 – Tue 24 Nov | Code-ox · Consultant | Configured |
| 10.4 | Demonstration to your team; loyalty and gift-card balances from Foodics as available (gap report 0.9) | Thu 26 Nov | Code-ox · Consultant | Demo held |

## WS 11 ZATCA Phase 2

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| 11.1 | Company VAT, CR and address; invoice journal per POS; one-tap default customer for walk-in sales | Sun 1 – Thu 12 Nov | Code-ox · Consultant | Configured |
| 11.2 | Fatoora portal administrator nominated, with access for simulation onboarding | By Thu 19 Nov | Tara · Finance | Access confirmed |
| 11.3 | Simulation onboarding and compliance checks for each POS journal on staging | Sun 22 – Thu 26 Nov | Code-ox · Consultant<br>ZATCA | Compliance passed |
| 11.4 | UAT: simplified and standard invoices, credit notes, B2B invoices, rejected-invoice handling | Tue 1 – Thu 17 Dec | Tara · Finance<br>Code-ox · QA | UAT result |
| 11.5 | **Production onboarding** of each POS journal (OTP generated by your Fatoora administrator) | Tue 29 – Wed 30 Dec | Code-ox · Consultant<br>Tara · Finance | Production certificates |

SECTION 10

# Foodics Migration & Historical Archive

Migrated: menus, categories, products, modifiers and customers per brand. Archived: full history in open formats under your control. Opening stock comes from a physical count at cutover. Foodics stays live until the last order on 31 December.

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| **12.1** | Foodics console and API access; data inventory; **gap report** on what Foodics can and cannot export (e.g. loyalty or gift-card balances), flagged at the start | Sun 18 – Thu 22 Oct | Code-ox · Consultant<br>Tara · IT | Gap report |
| **12.2** | Trial export 1 and field mapping per brand | Sun 25 – Thu 29 Oct | Code-ox · Consultant | Mapping sheet |
| **12.3** | Data validation and clean-up by your team: menu prices, active items, duplicate customers | Sun 1 – Thu 5 Nov | Tara · Operations<br>Tara · Marketing | Validated files |
| **12.4** | Trial load 1 into the build environment; counts and samples checked | Sun 8 – Thu 12 Nov | Code-ox · Consultant | Load report |
| **12.5** | Trial load 2 into the UAT environment | Sun 29 – Mon 30 Nov | Code-ox · Consultant | Load report |
| **12.6** | **Archive export 1**: all history to date: sales and orders, payments, products, menus, modifiers and categories, customers, discounts, promotions, refunds, cancellations, inventory history, loyalty / gift-card balances, tax and financial reports, branch and store configuration. CSV / Excel and PDF, plus a draft index and data dictionary. | Sun 13 – Thu 17 Dec | Code-ox · Consultant | Archive v1 in your storage |
| **12.7** | Rehearsal load using the cutover method, with timings recorded | Sun 20 – Mon 21 Dec | Code-ox · Consultant | Rehearsal report |
| **12.8** | Menu freeze in Foodics: any change after this date is applied in both systems by Code-ox | From Sun 27 Dec | Tara · Operations | Freeze notice |
| **12.9** | **Final export** after the last Foodics transaction | Night of Thu 31 Dec | Code-ox · Consultant | Final export |
| **12.10** | Opening stock from physical count at every outlet, Main Warehouse and Central Kitchen, posted before the first sale | Night 31 Dec – before opening 1 Jan | Tara · Inventory<br>Tara · Outlet managers<br>Code-ox · Consultant | Count sheets + inventory adjustment |
| **12.11** | Final archive with complete **index and data dictionary**: each dataset, its period and what it contains | Sun 3 Jan 2027 | Code-ox · Consultant | Archive handed over |

## Data objects

| OBJECT | SOURCE | METHOD | VALIDATED BY |
|---|---|---|---|
| Menus, categories, products, modifiers, combos | Foodics export | Import templates, per brand | Operations |
| Customers (incl. loyalty data where exported) | Foodics export | Import with de-duplication | Marketing |
| Ingredients, vendor lines, pack sizes, barcodes | Your procurement data | Templates 3.2 | Procurement |
| Recipes / BOMs and outlet recipe kits | Kitchen team | Templates 4.1 | Kitchen Lead |
| Minimum stock levels | Inventory team | Template 3.6 | Inventory |
| Users and roles (all staff incl. cashiers) | HR / Operations | User list by Thu 19 Nov | Owner |
| Opening stock | Physical count at cutover | Count sheets → inventory adjustment | Inventory + outlet managers |
| Sales history, reports, balances | Foodics | Archive only (not migrated as transactions) | Finance |

SECTION 11

# Testing, UAT & Training

Tested at every level, from build to full rehearsal, before your users accept anything, and every role trained before it uses the system.

| LEVEL | WHEN | WHO | EXIT CRITERIA |
|---|---|---|---|
| **Build testing** | Continuous, Wk 3–6 | Code-ox consultants and developers | Each item tested before the Thursday demo |
| **Thursday demos** | Weekly from Thu 12 Nov | Your key users | Feedback logged in the tracker |
| **System integration test** | Sun 22 – Mon 30 Nov | Code-ox QA | All end-to-end flows pass incl. platforms, payments, ZATCA simulation; internal test report (M7) |
| **UAT cycle 1** | Sun 6 – Thu 10 Dec | Your key users, guided by Code-ox | All scenarios executed; defects logged daily |
| **UAT cycle 2 + day-in-the-life** | Sun 13 – Thu 17 Dec | Key users with kitchen and one outlet team | Re-tests passed; a full trading day simulated end to end |
| **Cutover rehearsal** | Sun 20 – Mon 21 Dec | Code-ox, your IT and inventory leads | Deployment and data load timed and documented |
| **Regression & sign-off** | Tue 22 – Thu 24 Dec | Code-ox QA, project owner | No open Critical or High issues → UAT acceptance (M9) |

### UAT scenarios (scripts issued Thu 26 Nov)

- Purchase → receipt with pack conversion → bill → payment
- Central kitchen day: plan → MOs → consumption → transfers
- Expiry, leftovers disposal and waste with reasons
- Minimum stock replenishment to outlets
- Dine-in and takeaway with modifiers, combos and floor plan
- Delivery order per platform → KDS → status back; sold-out sync
- Card, Mada, Apple Pay, Tabby, Tamara; split payment; refund; failed payment
- Offline POS; session closing and cash control
- ZATCA simplified and standard invoices, credit notes
- B2B order, delivery and invoice
- Loyalty earn and redeem; coupon; gift card; eWallet
- WhatsApp receipt and order confirmation
- Platform payout reconciliation
- P&L by brand, branch and channel; stock value by outlet
- Access rules for each role

### Training plan

- **Key users (train-the-trainer)**: Tue 1 – Thu 3 Dec, before UAT starts
- **Finance & accounting**: Sun 13 – Mon 14 Dec (2 sessions)
- **Procurement & warehouse**: Tue 15 Dec
- **Central kitchen**: Wed 16 Dec, plus on the floor during the day-in-the-life test
- **Marketing** (loyalty, WhatsApp): Thu 17 Dec
- **Outlet managers & cashiers**: Sun 20 – Thu 24 Dec, by outlet group: POS, KDS, payments, delivery orders, ZATCA, offline mode, closing
- **IT / in-house developer**: Tue 22 Dec, covering repository, modules, deployment and integration monitoring; full handover in January
- **Refresher & go-live briefing**: Tue 29 – Wed 30 Dec
- Materials: role guides and quick-reference cards by Mon 30 Nov; attendance lists by Thu 3 Dec; attendance recorded per session

**ACCEPTANCE CRITERIA (PROPOSAL, PAGE 10)**

**Upgrade**: documented before / after validation signed off by finance for each of the six companies, and all agreed flows pass on staging, before production is touched. **UAT**: agreed scenarios pass on staging with no open Critical or High issues. **Go-live**: production live on Odoo 19, POS selling, ZATCA invoices accepted and orders flowing from the connected platforms, with any remaining Normal issues listed and scheduled.

SECTION 12

# Cutover & Go-Live

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| **15.1** | Cutover runbook (hour by hour) and rollback plan shared | Thu 17 Dec | Code-ox · Lead | Runbook |
| **15.2** | Cutover rehearsal on a fresh copy of production; timings recorded; runbook updated | Sun 20 – Mon 21 Dec | Code-ox · Tech Lead<br>Tara · IT | Rehearsal report |
| **15.3** | UAT acceptance; code freeze | Thu 24 Dec | Tara · Owner | **M9** |
| **15.4** | Stock count teams, count sheets and outlet go-live contacts confirmed; Foodics end date decided (D-12) | By Thu 24 Dec | Tara · Inventory<br>Tara · Operations | Count plan |
| **15.5** | Urban Eats deployed to production: modules from your repository, configuration, master data, users and access (no transactions yet) | Sun 27 – Mon 28 Dec | Code-ox · Tech Lead<br>Code-ox · Consultant | Deployment checklist |
| **15.6** | **Go / No-Go meeting** against the checklist below | Tue 29 Dec | Steering committee | **M10** |
| **15.7** | ZATCA production onboarding per POS journal; refresher training | Tue 29 – Wed 30 Dec | Code-ox · Consultant<br>Tara · Finance | Certificates |
| **15.8** | Final checks at every outlet: devices, printers, KDS, terminals, network, platform store mapping | Wed 30 Dec | Code-ox · Tech Lead<br>Tara · Outlet managers | Outlet checklist |

### Cutover night: Thu 31 Dec → Fri 1 Jan (T = closing of each outlet)

| TIME | STEP | OWNER |
|---|---|---|
| 31 Dec 09:00 | Command centre opens (Code-ox + your project owner); runbook review. Trading continues on Foodics as normal. | Code-ox · Lead |
| Afternoon | Central kitchen finishes the day's production; Main Warehouse and Central Kitchen counted once movement stops | Tara · Inventory |
| T | Last Foodics order at the outlet; shift closed; end-of-day report saved | Tara · Outlet manager |
| T + 15 min | Delivery platform stores switched from tablets to Odoo (Option A hub or Option B UrbanPiper) | Code-ox · Developers |
| T → T + 3 h | Physical stock count at the outlet; counts entered as opening stock and checked | Tara · Outlet team; Code-ox · Consultant |
| After last outlet | Final Foodics export started (12.9) | Code-ox · Consultant |
| Before opening | Smoke test per outlet: open session, test sale on each payment method, refund, KDS ticket, ZATCA invoice accepted, platform test order. Test documents reversed per procedure. | Code-ox · QA; Tara · Outlet manager |
| Before opening | **Go confirmation for each outlet** from outlet manager and Code-ox | Both |
| 1 Jan opening | **First live sales on Odoo**: monitoring of orders, payments, ZATCA queue and platform sync; hourly check-ins on day 1 | Code-ox · all; Tara · Owner |
| 1 Jan close | Day-1 review: issues, fixes and plan for day 2 | Both |

### Go / No-Go checklist (Tue 29 Dec)

- UAT accepted; no open Critical or High issues
- Production deployment verified (15.5)
- Hardware and terminals tested at every outlet
- Platform status known for each platform; any not ready stays on its tablet
- All roles trained; attendance recorded
- Count teams and Fatoora administrator confirmed
- Rollback plan and support rota published

### Rollback

- A Critical blocker found before opening on 1 Jan: the steering committee decides by an agreed time. The affected outlet(s) trade one more day on Foodics while it is fixed, which is why the Foodics account stays active until the archive is verified (D-12).
- The existing six companies are not affected: they have run on Odoo 19 since November (D-03).
- If D-03 is the 31 Dec upgrade instead, production is restored from the pre-upgrade backup. That restore is tested at the rehearsal.

SECTION 13

# Hypercare, Handover & Support

Two weeks of close support after go-live, a full handover so your developer owns the system, then six months of support under the SLA.

| ID | TASK | WHEN | OWNER | OUTPUT / EVIDENCE |
|---|---|---|---|---|
| **16.1** | Daily 30-minute check-in; issue log shared daily; monitoring of platform sync, payments and ZATCA submissions | Fri 1 – Thu 14 Jan | Code-ox · Consultant<br>Tara · Owner | Daily log |
| **16.2** | Floor support for outlets and kitchen in the first days, on site or remote as agreed in the runbook | Fri 1 – Sun 3 Jan | Code-ox · Consultant | Support rota |
| **16.3** | Final Foodics archive with index and data dictionary (12.11) | Sun 3 Jan | Code-ox · Consultant | Archive handed over |
| **16.4** | Go-live report: what went live, open items, platform status, next steps | Thu 7 Jan | Code-ox · Lead | Report |
| **16.5** | First weekly stock, waste and production review with kitchen and inventory leads | Thu 7 Jan | Code-ox · Consultant<br>Tara · Kitchen | Review notes |
| **16.6** | First platform payout reconciliations with finance | As payouts arrive in January | Code-ox · Consultant<br>Tara · Finance | Reconciled payouts |
| **16.7** | **Handover pack**: complete source in your repository, deployment instructions, migration scripts, technical, integration / API and configuration documentation; technical session with your developer | Thu 14 Jan | Code-ox · Tech Lead<br>Tara · IT | Signed handover · **M13** |
| **16.8** | Go-live acceptance feedback within 5 business days (proposal terms) | By Thu 7 Jan | Tara · Owner | Acceptance |
| **16.9** | First month-end close on the new system, supported with finance | Sun 31 Jan – Thu 4 Feb | Code-ox · Consultant<br>Tara · Finance | Close completed |
| **16.10** | Six months of support under the SLA; monthly support review meeting | 1 Jan – 30 Jun 2027 | Code-ox · Lead | Monthly review notes · M14 |

### Support SLA (from the proposal, page 10)

| PRIORITY | RESPONSE | FIX / WORKAROUND |
|---|---|---|
| **Critical**: POS, payment, platform, order sync or ZATCA down | 1 hour, 7 days a week, by phone or WhatsApp | 4 hours, including Friday and Saturday |
| **High** | 4 hours | 1 business day |
| **Normal** | 1 business day | 3 business days |

**AFTER THE SIX MONTHS**

Support continues under an AMC at your option, at the rate on page 7 of the proposal. New branches, brands, platforms and new requirements are quoted in writing before work starts, at the indicative rates in the proposal.

SECTION 14

# Week-by-Week Calendar

| WEEK | CODE-OX | TARA HOLDING | MEETINGS & MILESTONES |
|---|---|---|---|
| Wk 0<br>11–15 Oct | Demo (Mon 12); kick-off pack; tracker set-up | Financial acceptance; signed agreement; owner and key users named; D-01; Odoo.sh and Foodics access | Kick-off by Thu 15 · **M0** |
| Wk 1<br>18–22 Oct | Workshops daily; backup & staging upgrade; Studio and module migration; pre-validation; assessment & register (Tue 20); architecture, migration plan, gap report (Thu 22) | Attend workshops; company validators; outlet & store list; module licences; repository | Steering Sun 18; report Thu 22 |
| Wk 2<br>25–29 Oct | Support department validation; fixes; coding scheme (Tue 27); integration plan, hardware spec, terminal availability (Thu 29); Foodics trial export | Validate on staging (25–28); approve architecture, D-02, D-04 (Tue 27); D-05, D-03; **finance sign-off per company (Thu 29)**; Urban Eats CR / VAT / accounts data (Sun 25) | **M1** Tue 27 · **M2** Thu 29 |
| Wk 3<br>1–5 Nov | Company, accounts, taxes, journals, analytic plans; warehouses, routes, UoM; upgrade runbook (Tue 3); loyalty session (Tue 3); **production upgrade Thu 5 night** | Supplier data and payment keys (Sun 1); data clean-up; menus and recipes (Thu 5); Meta verification (Thu 5); D-06, D-10 (Thu 5); finance checks Sat 7 | **M3** weekend 5–7 Nov |
| Wk 4<br>8–12 Nov | Materials & vendor lines; shared ops; access; BOMs; POS configs; menus; Paymob; Tabby / Tamara; hub core or UrbanPiper stores; WhatsApp drafts; ZATCA journals; trial load 1 | Minimum stock levels; D-07, D-08, D-09 (Thu 12) | First Thursday demo · **M4** Thu 12 |
| Wk 5<br>15–19 Nov | Daily production plan; kitchen screen; stock rules; KDS; receipts; menus done; terminals; platform connectors; settlement; loyalty; waste & costing; WhatsApp templates submitted | Fatoora access; user list and roles (Thu 19) | Thursday demo |
| Wk 6<br>22–26 Nov | Expiry & leftovers; recipe kits; offline & cash procedure; payment rules; ZATCA simulation; WhatsApp automations; platform tests; system test; pilot-outlet hardware test; UAT scripts (Thu 26) | Hardware & terminals on site; Odoo subscription users / apps updated; UAT testers named (Thu 26) | **M5** · **M6** Thu 26 |
| Wk 7<br>29 Nov–3 Dec | Internal test report and trial load 2 (Mon 30); UAT environment built from production copy; materials ready; **UAT live Tue 1 Dec**; key-user training | Agree UAT scripts (Mon 30); key users trained; attendance lists (Thu 3) | **M7** Mon 30 · **M8** Tue 1 Dec |
| Wk 8<br>6–10 Dec | UAT cycle 1 support; daily fixes; platform testing | Execute scenarios; log defects daily | Daily stand-up |
| Wk 9<br>13–17 Dec | UAT cycle 2 + day-in-the-life; archive export 1; training (finance, procurement, kitchen, marketing); cutover runbook (Thu 17) | Re-test; staff the day-in-the-life; attend training | Daily stand-up |
| Wk 10<br>20–24 Dec | Cutover rehearsal (20–21); regression; outlet staff training; IT session (Tue 22); code freeze | **UAT sign-off (Thu 24)**; count teams; D-12 | **M9** Thu 24 |
| Wk 11<br>27–31 Dec | Production deployment (27–28); ZATCA production onboarding (29–30); outlet checks (30); **cutover night 31 Dec** | Menu freeze; Go / No-Go (Tue 29); Fatoora OTPs; refresher training; stock count | **M10** Tue 29 · **M11** Thu 31 |
| Fri 1 Jan | **Go-live**: command centre; hourly check-ins | Outlets open on Odoo; no new transactions on Foodics | **M12** |
| Wk 12<br>3–7 Jan | Hypercare; final archive (Sun 3); go-live report (Thu 7); first stock & waste review | Daily check-in; go-live feedback | Daily check-in |
| Wk 13<br>10–14 Jan | Hypercare; payout reconciliations; **handover pack (Thu 14)** | Technical handover with your developer | **M13** Thu 14 |

**EVERY WEEK**

Steering on Sunday · Thursday demo (from 12 Nov) · written status report on Thursday · live tracker in Odoo Project. After hypercare: first month-end close 31 Jan – 4 Feb, then monthly support reviews to 30 Jun 2027.

SECTION 15

# Your Inputs & Decisions

## Inputs from Tara Holding

| ID | INPUT | DUE | OWNER |
|---|---|---|---|
| **I-01** | Signed agreement and advance payment | Thu 15 Oct | Sponsor |
| **I-02** | Project owner and key users named per area | Thu 15 Oct | Sponsor |
| **I-03** | **Odoo.sh access**; staging confirmed; Code-ox registered as partner on the subscription **(critical path)** | Sun 18 Oct | IT |
| **I-04** | Foodics console and API access | Sun 18 Oct | IT |
| **I-05** | Platform merchant accounts / authorisation per entity for API requests (Option A) or UrbanPiper order (Option B) | Sun 18 Oct | Operations |
| **I-06** | Six companies with a finance validator each; input to the validation checklist | Tue 20 Oct | Finance |
| **I-07** | Licences and source for third-party modules as listed in the register | Tue 20 Oct | IT |
| **I-08** | Outlet list: brands, address, hours, devices, platform store IDs | Thu 22 Oct | Operations |
| **I-09** | Repository for custom code in Tara Holding's name, with Code-ox access | Thu 22 Oct | IT |
| **I-10** | Urban Eats CR, VAT number, address, chart of accounts preferences, bank accounts | Sun 25 Oct | Finance |
| **I-11** | Suppliers, vendor price lists, pack sizes, barcodes | Sun 1 Nov | Procurement |
| **I-12** | Paymob, Tabby, Tamara merchant accounts and API keys | Sun 1 Nov | Finance |
| **I-13** | Validated menus per brand and recipes / BOMs | Thu 5 Nov | Operations, Kitchen |
| **I-14** | Meta Business verification, WhatsApp number, Business Manager access | Thu 5 Nov | Marketing |
| **I-15** | Initial minimum stock levels per location | Thu 12 Nov | Inventory |
| **I-16** | Fatoora portal administrator and access | Thu 19 Nov | Finance |
| **I-17** | User list with roles (all staff incl. cashiers) | Thu 19 Nov | Operations |
| **I-18** | POS hardware, printers, KDS screens, card terminals and network on site | Thu 26 Nov | IT |
| **I-19** | Odoo subscription updated for the users and apps needed (count from Code-ox by Thu 12 Nov) | Thu 26 Nov | IT |
| **I-20** | Named UAT testers and calendar | Thu 26 Nov | Owner |
| **I-21** | Training attendance lists per session | Thu 3 Dec | Operations |
| **I-22** | Stock count teams and outlet go-live contacts | Thu 24 Dec | Inventory |
| **I-23** | Fatoora administrator available for OTPs; outlet managers on cutover night | 29–31 Dec | Finance, Operations |

## Decisions

| ID | DECISION | DUE |
|---|---|---|
| **D-01** | Part 2 delivery-platform layer: Option A (Code-ox Aggregator Hub) or Option B (UrbanPiper) | Thu 15 Oct |
| **D-02** | POS revenue tagging: Option 1 fully standard or Option 2 small isolated module | Tue 27 Oct |
| **D-03** | Production upgrade window: weekend 5–7 Nov (as planned) or cutover night 31 Dec | Thu 29 Oct |
| **D-04** | Treatment of each third-party module, incl. the replacement MCP app | Tue 27 Oct |
| **D-05** | Product types and coding scheme | Thu 29 Oct |
| **D-06** | POS terminal provider(s): Geidea, NearPay, Paymob | Thu 5 Nov |
| **D-07** | Loyalty and promotion programs for MYLK | Thu 12 Nov |
| **D-08** | Kitchen and delivery status WhatsApp messages: which, if any, to automate | Thu 12 Nov |
| **D-09** | Settlement automation level (after Odoo's official response) | Thu 12 Nov |
| **D-10** | Labour and overhead in production cost (optional) | Thu 5 Nov |
| **D-11** | Training language(s) and session format | Thu 26 Nov |
| **D-12** | Foodics account end date (kept active until the final archive is verified) | Thu 24 Dec |
| **D-13** | Go / No-Go | Tue 29 Dec |

SECTION 16

# Deliverables

Every document Code-ox delivers, with its due date. Each one is shared for review in the tracker; documents that need your approval are marked in the related task.

| ID | DELIVERABLE | DUE |
|---|---|---|
| **DL-01** | Execution plan (this document) and live tracker in Odoo Project | Sun 18 Oct |
| **DL-02** | Kick-off pack: team, contacts, cadence, severity definitions, templates | Sun 18 Oct |
| **DL-03** | Written upgrade assessment and module-by-module register | Tue 20 Oct |
| **DL-04** | Urban Eats architecture document | Thu 22 Oct |
| **DL-05** | Upgrade validation report per company (before / after) | Thu 22 Oct → sign-off Thu 29 Oct |
| **DL-06** | Data migration plan, import templates, Foodics gap report | Thu 22 Oct |
| **DL-07** | Per-platform integration plan (A) or UrbanPiper configuration plan (B) | Thu 29 Oct |
| **DL-08** | POS hardware and network specification | Thu 29 Oct |
| **DL-09** | Production upgrade runbook | Tue 3 Nov |
| **DL-10** | Settlement plan | Thu 12 Nov |
| **DL-11** | Written justification for each custom item, before it is built | As raised |
| **DL-12** | UAT scenarios, scripts and calendar | Thu 26 Nov |
| **DL-13** | Internal test report | Mon 30 Nov |
| **DL-14** | Training materials: role guides and quick-reference cards | Mon 30 Nov |
| **DL-15** | Cutover runbook and rollback plan | Thu 17 Dec |
| **DL-16** | UAT report and acceptance form | Thu 24 Dec |
| **DL-17** | Go / No-Go checklist | Tue 29 Dec |
| **DL-18** | Foodics archive v1 (Thu 17 Dec); final archive with index and data dictionary | Sun 3 Jan 2027 |
| **DL-19** | Go-live report | Thu 7 Jan 2027 |
| **DL-20** | Handover pack: source, deployment instructions, migration scripts, technical / integration / configuration documentation | Thu 14 Jan 2027 |
| **DL-21** | Weekly status report | Every Thursday |

SECTION 17

# Risks & Assumptions

Reviewed every Sunday at steering. New risks are added to the tracker with an owner and a mitigation.

| ID | RISK | MITIGATION | OWNER |
|---|---|---|---|
| **R1** | Platform APIs issued late (Option A) | Requested on Tara's behalf already; weekly follow-up; connectors built in order of arrival; a late platform keeps its tablet and is connected when ready, within scope | Code-ox |
| **R2** | UrbanPiper onboarding or coverage timing (Option B) | Coverage confirmed in the joint meeting; stores started in Wk 2; uncovered platform stays on its tablet | Tara, UrbanPiper |
| **R3** | A third-party module has no Odoo 19 version | Register by Tue 20 Oct; migrate or replace; nothing removed without approval | Code-ox |
| **R4** | Validation time for six companies in one week | Code-ox prepares before / after reports so finance reviews differences only; checklist agreed in Wk 1 | Both |
| **R5** | Recipe or menu data incomplete | Templates in Wk 1; workshop support; top-selling items first | Tara |
| **R6** | Foodics cannot export some data (e.g. balances) | Gap report in Wk 1, so the approach is agreed early | Code-ox |
| **R7** | Hardware, terminals or network not ready | Spec Thu 29 Oct; devices on site Thu 26 Nov; pilot-outlet test | Tara |
| **R8** | Key users unavailable in December | Named testers and calendar by Thu 26 Nov | Tara |
| **R9** | ZATCA onboarding issue near go-live | Simulation passed in Wk 6; OTP process rehearsed; administrator on standby | Both |
| **R10** | Late scope changes | Change control; code freeze from Thu 24 Dec | Both |

**ASSUMPTIONS**

Tara Holding stays on Odoo.sh with one staging branch available · Urban Eats goes live at all outlets on 1 Jan 2027 · Scope, prices and terms are as in Financial Proposal CX-TARA-2026-02 Rev. 1; this plan does not change them · Third-party and platform fees are as listed on page 9 of the proposal.

ACCEPTANCE

# Plan Acceptance

By signing, both parties agree this plan as the baseline for delivery. Changes to dates, owners or tasks are agreed at steering and recorded in the tracker. Changes to scope, cost or the committed dates of 1 December 2026 and 1 January 2027 follow the change control in Section 2.

**FOR & ON BEHALF OF CODE-OX TECHNOLOGIES**

AUTHORISED SIGNATORY

NAME & TITLE

DATE

**FOR & ON BEHALF OF TARA HOLDING**

AUTHORISED SIGNATORY

NAME & TITLE

DATE

**CONTACT**

Raghib Ali Rafeeque, Code-ox Technologies · raghib@code-ox.com · +966 561 765 707 · 3239 Al Zubair Bin Al Awwam St, Al Rawabi Dist., Riyadh 14215, KSA
