PROJECT EXECUTION PLAN · VERSION 1.0 · 11 OCTOBER 2026

From Kick-off to Go-live on 1 January 2027

The complete, week-by-week execution of the Odoo 18 → 19 upgrade and the Urban Eats / MYLK implementation: every task, owner, date, input and sign-off, so your team can see how each of the coming months is managed.

KICK-OFF	UPGRADE SIGN-OFF	UAT ENVIRONMENT	GO-LIVE	SUPPORT
15 Oct	29 Oct	1 Dec	1 Jan	30 Jun
2026 · latest	all six companies	committed	2027 · committed	2027 · six months

SIX PHASES

PHASE 1	PHASE 2	PHASE 3	PHASE 4	PHASE 5	PHASE 6
Mobilise & design	**Odoo 19 upgrade**	**Build Urban Eats**	**UAT & training**	**Cutover & go-live**	**Hypercare & support**
11 – 29 Oct	18 Oct – 7 Nov	1 – 30 Nov	1 – 24 Dec	27 Dec – 1 Jan	1 Jan – 30 Jun

122 tasks with owners and dates
Across every workstream, each loaded into Odoo Project on your own Odoo.

Staging first, production last
Every department validates and finance signs off each company before production is touched.

Weekly visibility
Sunday steering, Thursday demo on staging and a written status report every week.

Your inputs and decisions dated
23 inputs and 13 decisions, each tied to the task that needs it.

DOCUMENT	COMPANION TO	DATE	PREPARED BY
Execution Plan v1.0	CX-TARA-2026-02 Rev. 1	11 October 2026	Code-ox Technologies

INTRODUCTION

Purpose, Principles & Key Dates

What this document is

- The execution plan for Financial Proposal **CX-TARA-2026-02 Rev. 1**: Part 1 (Odoo 18 → 19 upgrade) and Part 2 (Urban Eats / MYLK implementation).
- It expands the weekly plan on page 8 of the proposal into **every task, owner, date, input and sign-off** from kick-off to the end of support.
- Every task ID here is loaded into **Odoo Project on your own Odoo** by Sun 18 Oct, so your team sees status, owner and due date at any time.

How the plan is run

- **Standard Odoo first**: standard › configuration › Studio › supported module › custom development, each custom item justified in writing and approved by you.
- **Nothing reaches production untested**: upgrade validated on staging and signed off by every department before production is touched.
- **Continuity of data**: your POs, journal entries, invoices and history continue in Odoo 19 in the same database. Nothing is re-keyed into a separate system.
- **No surprises**: weekly steering, a Thursday demo on staging and a written status report every week.

Milestones

#	MILESTONE	TARGET DATE	CONFIRMED BY	EVIDENCE
M0	**Agreement signed & kick-off held**	By Thu 15 Oct 2026	Both parties	Signed agreement; kick-off minutes
M1	**Upgrade assessment & Urban Eats architecture approved**	Tue 27 Oct	Tara project owner	Approved assessment, module register and architecture document
M2	**Upgrade signed off on staging** (all six companies)	Thu 29 Oct	Tara finance, per company	Signed before / after validation per company
M3	**Production upgraded to Odoo 19** (existing companies)	Weekend 5–7 Nov	Tara finance + IT	Post-upgrade checks signed; see decision D-03
M4	**Urban Eats foundation configured**	Thu 12 Nov	Tara project owner	Thursday demo on staging
M5	**Central kitchen flow, POS & payments ready**	Thu 26 Nov	Tara kitchen + outlets	Thursday demo; hardware test at pilot outlet
M6	**Delivery platforms connected in test**	Thu 26 Nov	Tara outlets	Test orders per connected platform, subject to platform approvals
M7	**Internal testing complete; migration data loaded**	Mon 30 Nov	Code-ox	Internal test report
M8	**Production-ready UAT environment live**	**Tue 1 Dec 2026**	Committed date	UAT environment handed over with logins and scripts
M9	**UAT acceptance**	Thu 24 Dec	Tara project owner	UAT report; no open Critical or High issues
M10	**Go / No-Go decision**	Tue 29 Dec	Steering committee	Go / No-Go checklist signed
M11	**Ready for cutover**	Thu 31 Dec	Both parties	Cutover runbook steps complete
M12	**Production go-live**: no new transactions on Foodics	**Fri 1 Jan 2027**	Committed date	POS selling, ZATCA accepted, platform orders flowing
M13	**Hypercare complete; source & documentation handed over**	Thu 14 Jan 2027	Tara project owner + IT	Handover pack signed
M14	**Six-month support ends**	Wed 30 Jun 2027	Both parties	Support close-out; AMC at your option


DATES AND CONDITIONS

Dates assume kick-off by **Thu 15 Oct 2026**. An earlier kick-off adds buffer and leaves every date unchanged. The 1 December and 1 January commitments rely on the conditions already in the proposal: signed agreement and kick-off by 15 October, access and data on the dates in Section 15, timely UAT feedback, and delivery-platform approvals, which neither party controls. Working week: Sunday–Thursday, Riyadh time.

PLAN AT A GLANCE

Gantt: Kick-off to Handover

One view of every workstream across the fourteen weeks. Detailed tasks for each bar follow in Sections 3–13.

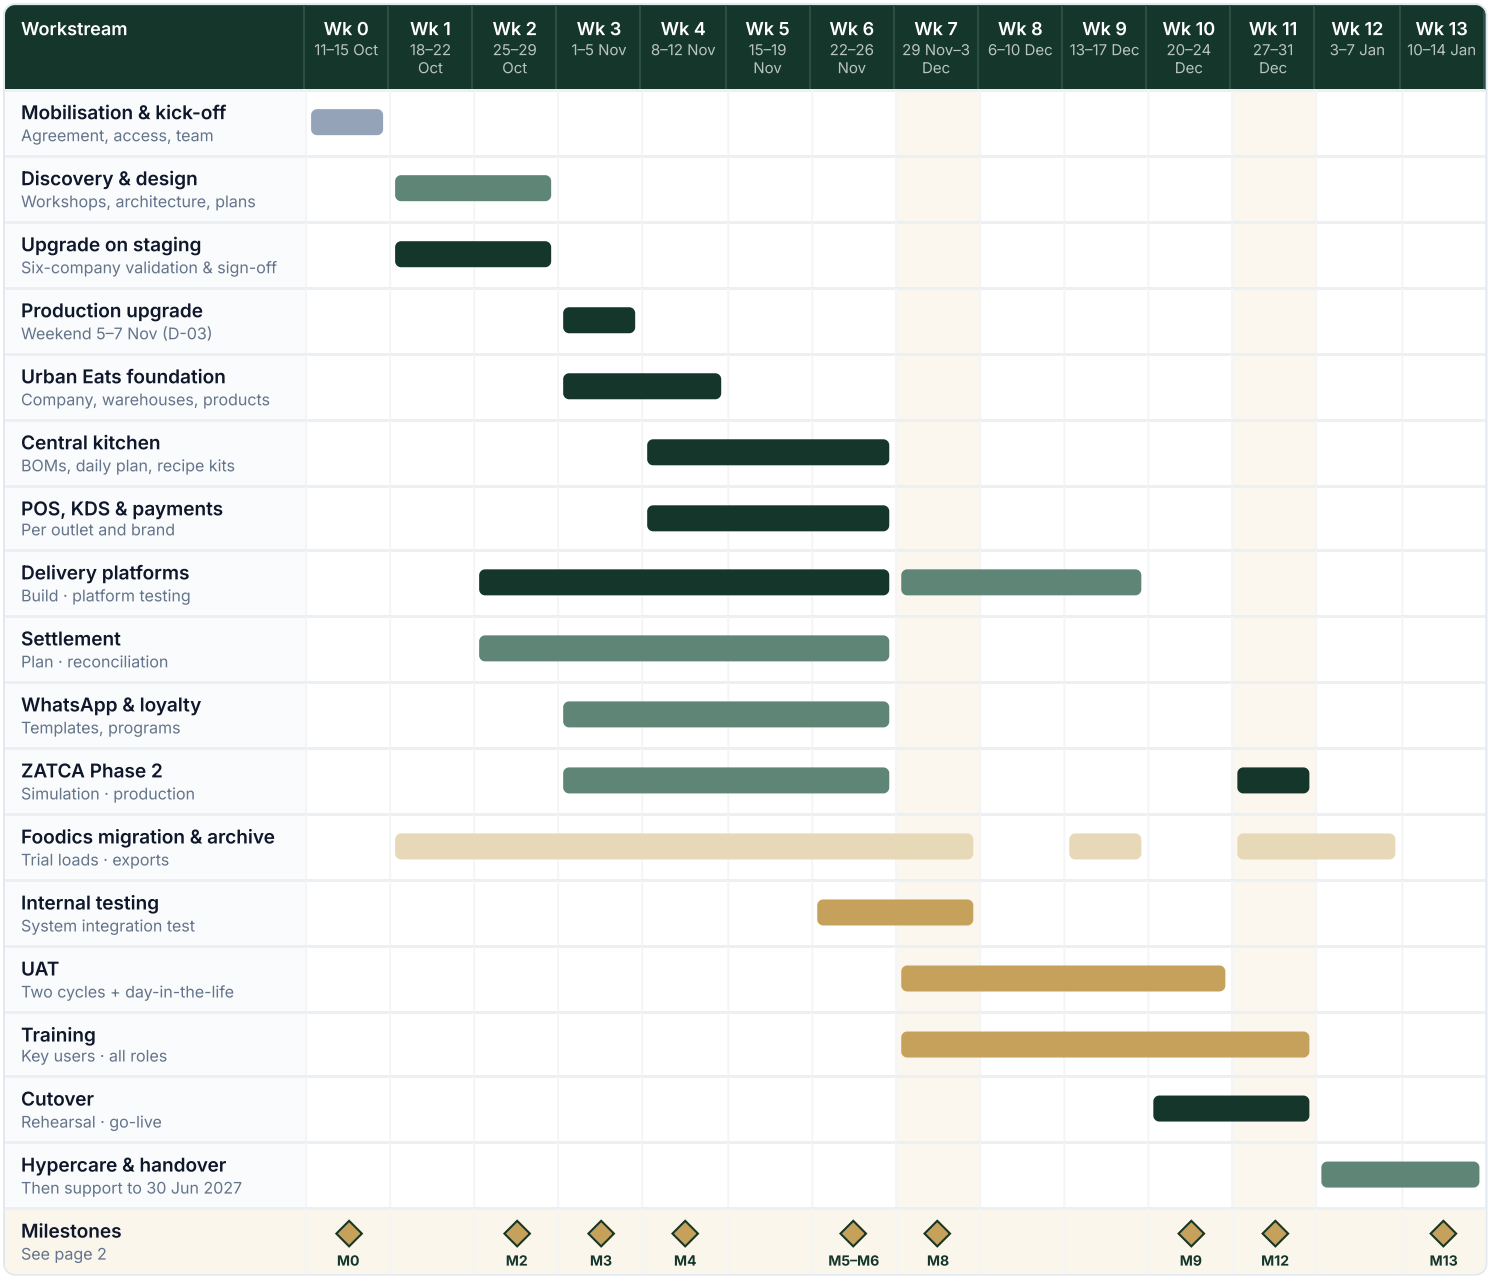

CRITICAL PATH

Odoo.sh access at kick-off → staging upgrade (Wk 1) → finance sign-off (Wk 2) → foundation (Wk 3–4) → kitchen, POS & platforms (Wk 4–6) → UAT environment **1 Dec** → UAT sign-off **24 Dec** → go-live **1 Jan**.

HIGHLIGHTED COLUMNS

Wk 7: the UAT environment goes live on Tue 1 Dec. **Wk 11**: cutover week, ending on the night of Thu 31 Dec for go-live on Fri 1 Jan 2027.

SECTION 1

Team, Roles & Governance

Code-ox Technologies

- **Engagement Lead**: Raghib Ali Rafeeque. Single point of contact for commercial matters and steering; owns the plan and weekly report.
- **Lead Functional Consultant (Odoo 19 Certified)**: Thayif Kabir. Business consultant across all departments; leads workshops, architecture, upgrade validation and UAT.
- **Technical Lead**: upgrade execution, module migration, deployment, code review and the repository in your name.
- **Odoo Developers**: aggregator integration, Tabby / Tamara, POS terminals, the optional tagging module.
- **QA Engineer**: test scripts, system integration test, regression, defect tracking.
- **Head of Operations**: Shabeeb K. Executive escalation and resourcing.

Tara Holding (names confirmed at kick-off)

- **Project Owner & single point of contact**: Eng. AbdulRahman Al-Nouman (to confirm). Decisions, approvals, access.
- **Executive Sponsor**: chairs steering; final Go / No-Go.
- **Finance Lead** and a **validator for each of the six companies**: upgrade sign-off, chart of accounts, settlement.
- **Procurement & Inventory Lead**: suppliers, products, stock rules, stock count.
- **Central Kitchen Lead**: recipes, production plan, expiry and waste rules.
- **Operations / Outlets Lead** with one manager per outlet: menus, POS, KDS, training.
- **Marketing Lead**: loyalty, promotions, WhatsApp templates.
- **IT / in-house developer**: Odoo.sh, repository, hardware, network, technical handover.

Meetings & reporting

FORUM	WHEN	WHO	PURPOSE
Kick-off	By Thu 15 Oct · 2 hrs	Both teams, sponsor	Scope recap, team, this plan, access checklist, decisions D-01 to D-03
Discovery workshops	Sun 18 – Thu 22 Oct · daily	Consultant + area leads	One workshop per area (Section 3)
Steering committee	Every Sunday · 45 min	Sponsor, owner, Code-ox leads	Progress against plan, risks, decisions due, overdue inputs
Thursday demo on staging	Every Thursday from 12 Nov · 45 min	Owner + key users	Show what was built that week; collect feedback early
Weekly status report	Every Thursday by 18:00	Code-ox to Tara	Status per workstream (on track, at risk, late), % complete, done, next week, risks, decisions, Tara actions due
Daily stand-up	15 min · UAT (1–24 Dec), cutover & hypercare (27 Dec – 14 Jan)	Consultant, QA, key users	Defects, blockers, plan for the day
Live tracker	Always	Everyone	Odoo Project on your Odoo: every task ID, owner, due date and status

Escalation

LEVEL	CODE-OX	TARA HOLDING	RESOLUTION TARGET
1	Lead Functional Consultant	Area lead	Same business day
2	Engagement Lead	Project Owner	Within 2 business days
3	Head of Operations	Executive Sponsor	Next steering, or within 3 business days

SECTION 2

Who Does What

Who does each activity, who approves it, and who gives input. Everyone else is kept informed through the weekly status report and the live tracker. Green = Code-ox team · Gold = Tara Holding team.

ACTIVITY	DOES THE WORK	APPROVES	GIVES INPUT
Project plan, tracker, weekly report	Engagement Lead	Engagement Lead	Functional Consultant, Technical Lead & Developers, Project Owner
Discovery workshops	Functional Consultant, Finance & Procurement, Kitchen & Outlets	Engagement Lead	Technical Lead & Developers, Project Owner, IT team
Upgrade assessment & module register	Functional Consultant, Technical Lead & Developers	Engagement Lead	Project Owner, Finance & Procurement, IT team
Upgrade validation on staging	Functional Consultant, Technical Lead & Developers, Testing team, Finance & Procurement	Functional Consultant	Project Owner, Kitchen & Outlets, IT team
Finance sign-off per company	Finance & Procurement	Project Owner	Functional Consultant
Architecture document	Functional Consultant	Functional Consultant, Project Owner	Engagement Lead, Technical Lead & Developers, Finance & Procurement, Kitchen & Outlets, IT team
Configuration & custom development	Functional Consultant, Technical Lead & Developers	Functional Consultant	Testing team, IT team
Master data, menus, recipes (provide & validate)	Finance & Procurement, Kitchen & Outlets	Project Owner	Functional Consultant, Technical Lead & Developers
Delivery-platform API requests	Engagement Lead, Technical Lead & Developers	Engagement Lead	Functional Consultant, Project Owner, Kitchen & Outlets
Hardware, terminals, network on site	Kitchen & Outlets, IT team	Project Owner	Functional Consultant, Technical Lead & Developers
UAT scripts	Functional Consultant, Testing team	Functional Consultant	Technical Lead & Developers, Project Owner, Finance & Procurement, Kitchen & Outlets
UAT execution & acceptance	Functional Consultant, Testing team, Finance & Procurement, Kitchen & Outlets	Project Owner	Technical Lead & Developers, IT team
Training delivery / attendance	Functional Consultant, Finance & Procurement, Kitchen & Outlets, IT team	Functional Consultant	Technical Lead & Developers, Project Owner
Cutover runbook	Functional Consultant, Technical Lead & Developers	Engagement Lead	Testing team, Project Owner, Finance & Procurement, Kitchen & Outlets, IT team
Physical stock count at cutover	Finance & Procurement, Kitchen & Outlets	Project Owner	Functional Consultant, Technical Lead & Developers
Go / No-Go	Engagement Lead	Project Owner	Functional Consultant, Technical Lead & Developers, Testing team, Finance & Procurement, Kitchen & Outlets, IT team
Hypercare & handover	Functional Consultant, Technical Lead & Developers, IT team	Engagement Lead	Testing team, Project Owner, Finance & Procurement, Kitchen & Outlets

SECTION 2 · CONTINUED

The Roles, Environments & Change Control

The roles on page 5

ROLE	TEAM	WHO	WHAT THEY DO IN THIS PROJECT
Engagement Lead	Code-ox	Raghib Ali Rafeeque	Single point of contact; owns the plan, weekly report, platform API requests and steering
Functional Consultant	Code-ox	Thayif Kabir (Odoo 19 certified)	Business consultant for every department; workshops, design, configuration, validation, UAT and training
Technical Lead & Developers	Code-ox	Named at kick-off	Upgrade, module migration, integrations, custom modules, deployment and the code repository
Testing team	Code-ox	Named at kick-off	Test scripts, end-to-end testing, re-tests and defect tracking
Project Owner	Tara Holding	Eng. AbdulRahman Al-Nouman (to confirm)	Decisions and approvals for Tara Holding; chairs the Go / No-Go with the sponsor
Finance & Procurement	Tara Holding	Finance lead + one validator per company; procurement lead	Upgrade sign-off per company, accounts, suppliers, settlement, stock count
Kitchen & Outlets	Tara Holding	Central kitchen lead; operations lead; outlet managers	Recipes, menus, POS and kitchen testing, outlet training, cutover at each outlet
IT team	Tara Holding	IT / in-house developer	Odoo.sh access, repository, devices and network; receives the technical handover

Environments

- **Production** (Odoo.sh): your live six companies. Upgraded only after sign-off; Urban Eats deployed to it in cutover week.
- **Staging, upgrade validation**: copy of production upgraded to Odoo 19 for the before / after checks.
- **Staging, build & UAT**: where Urban Eats is built, demonstrated each Thursday and accepted in UAT.
- **Repository**: owned by Tara Holding; all custom modules, migration scripts and deployment notes.
- The UAT environment on 1 Dec is built from a fresh copy of production using the **same deployment package** used at go-live. The method is proven on 1 Dec and again at the 20 Dec rehearsal before production.

Change control & defects

- **Change request**: logged in the tracker, then Code-ox gives impact on scope, cost and timeline **within 3 business days**. Work starts only on your written approval.
- **Code freeze** from Thu 24 Dec: Critical fixes only until go-live.
- **Critical**: blocks selling, payment, orders, ZATCA or a sign-off; fixed same day.
- **High**: key function impaired, workaround exists; fixed within 2 business days.
- **Normal**: minor or cosmetic; fixed before the next UAT cycle.
- Every defect has an ID, owner, severity and status visible in the tracker.

SECTION 3

Mobilisation & Discovery (Wk 0 – Wk 2)

Starts the moment the agreement is signed. The aim of the first two weeks is to lock the design in writing so the build runs without rework.

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
0.1	Solution demo to your team	Mon 12 Oct	Code-ox · Consultant Tara · Owner	Demo held
0.2	Financial acceptance; agreement signed; advance invoice issued	By Thu 15 Oct	Tara · Sponsor Code-ox · Lead	Signed agreement
0.3	**Kick-off**: scope recap, teams, this plan, cadence, access checklist; decisions D-01 to D-03 opened	By Thu 15 Oct	Code-ox · Lead Tara · Owner	Kick-off minutes · M0
0.4	Access granted: Odoo.sh (Code-ox as collaborator), staging confirmed, Code-ox registered as partner on your Odoo subscription	At kick-off · Sun 18 Oct latest	Tara · IT	Access checklist: **critical path**
0.5	Tracker loaded in Odoo Project on your Odoo: every task ID, owner and due date	Sun 18 Oct	Code-ox · Lead	Live tracker
0.6	Kick-off pack: team list, contacts, cadence, severity definitions, templates	Sun 18 Oct	Code-ox · Lead	Kick-off pack

Discovery workshops

DATE	WORKSHOP	TARA ATTENDEES	FEEDS
Sun 18 Oct	**Technical**: Odoo.sh, staging, repository, the 11 third-party modules, integrations in use	IT / in-house developer	Upgrade assessment, module register
Sun 18 Oct	**Structure & finance**: Urban Eats company, MYLK / Finjan brands, outlets, channels, P&L needs, shared costs	Owner, Finance	Architecture document
Mon 19 Oct	**Procurement & inventory**: suppliers, pack sizes, coding, warehouses, replenishment, lots & expiry	Procurement, Inventory	Product master, routes, stock rules
Tue 20 Oct	**Central kitchen**: products, recipes, shelf life, daily plan, transfers, waste	Kitchen Lead	Manufacturing design
Wed 21 Oct	**Outlets, POS & payments**: service flow per brand, modifiers, combos, receipts, KDS stations, payment methods, terminals	Operations, outlet managers	POS / KDS design, hardware spec
Thu 22 Oct	**Delivery platforms & settlement**: stores per outlet, menus per platform, payouts and statements	Operations, Finance	Integration plan, settlement plan
Thu 22 Oct	**Marketing**: WhatsApp messages, loyalty and promotion ideas (follow-up on Tue 3 Nov)	Marketing	Templates, loyalty programs

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
0.7	Written **upgrade assessment** & **module-by-module register**: compatibility, treatment (retain, migrate, replace, consolidate, retire), licence or vendor cost, risk	Tue 20 Oct	Code-ox · Tech Lead	Assessment + register
0.8	**Urban Eats architecture document** (Section 5)	Thu 22 Oct	Code-ox · Consultant	Document for approval
0.9	Data migration plan, import templates & Foodics gap report	Thu 22 Oct	Code-ox · Consultant	Plan + templates
0.10	Per-platform integration plan (Option A) or UrbanPiper configuration plan (Option B)	Thu 29 Oct	Code-ox · Tech Lead	Integration plan
0.11	POS hardware & network specification per outlet	Thu 29 Oct	Code-ox · Tech Lead	Spec for ordering
0.12	**Approval** of assessment, register and architecture; decisions D-02, D-04	Tue 27 Oct	Tara · Owner	**M1**

SECTION 4 · PART 1

Odoo 18 → 19 Upgrade

Performed on staging first. Production is touched only after every department has validated its own data and your finance team has signed off each company.

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
1.1	Full backup of production; staging copy prepared on Odoo.sh	Sun 18 Oct	Code-ox · Tech Lead	Backup reference
1.2	Upgrade of the staging copy to Odoo 19 through Odoo's upgrade service	Sun 18 – Mon 19 Oct	Code-ox · Tech Lead · Odoo	Odoo 19 staging database
1.3	**Studio customisations** checked and corrected: custom fields, views, reports, automations, server actions, access rules	Mon 19 – Wed 21 Oct	Code-ox · Consultant	Studio checklist, item by item
1.4	**Third-party modules** handled per register: simplify_access_management, advanced_web_domain_widget, auditlog, hide_menu_user, Hikvision attendance, muk_mcp, muk_mcp_access, muk_web_utils, notify_email_inbox, paymob, pos_paymob. A replacement MCP app for Odoo 19 is proposed. **No module removed without your written approval.**	Mon 19 – Thu 22 Oct	Code-ox · Developers · Tara · IT (licences)	Register status per module
1.5	Code-ox pre-validation, **each of the six companies**, before vs after: trial balance; aged receivables & payables; tax reports & fiscal configuration; stock valuation; open customer invoices & vendor bills. Every difference listed with its cause, including where Odoo 19 itself changes a calculation or presentation.	Tue 20 – Thu 22 Oct	Code-ox · Consultant · Code-ox · QA	Validation report per company
1.6	Key business flows tested against the agreed checklist: purchase → receipt → bill → payment; sale → delivery → invoice → payment; journal entries; bank reconciliation; multi-company and inter-company configuration; access rights	Wed 21 – Thu 22 Oct	Code-ox · QA	Flow checklist results
1.7	**Department validation on staging**: finance for each company, procurement, inventory and every department using Odoo. Your users work on their own POs, journals and invoices in Odoo 19.	Sun 25 – Wed 28 Oct	Tara · Finance · Tara · Departments · Code-ox · Consultant (on call)	Issue list
1.8	Fixes and re-tests for every issue raised	Sun 25 – Wed 28 Oct	Code-ox · Tech Lead	Issues closed
1.9	**Sign-off by your finance team, per company**	Thu 29 Oct	Tara · Finance	Signed forms · **M2**
1.10	Production upgrade runbook: timings, owners, checks, rollback by restore of the pre-upgrade backup	Tue 3 Nov	Code-ox · Tech Lead	Runbook shared
1.11	**Production upgrade** outside working hours: Thu 5 Nov after close of business → backup → upgrade → technical checks → finance spot checks on Sat 7 Nov → release for Sunday	Thu 5 – Sat 7 Nov	Code-ox · Tech Lead · Tara · Finance · Tara · IT	Post-upgrade checks · **M3**
1.12	First-week monitoring and priority support for all users on Odoo 19	Sun 8 – Thu 12 Nov	Code-ox · Consultant	Daily check-in notes

WHAT YOUR USERS WILL SEE

Same database, same records: every PO, journal entry, invoice and history line continues in Odoo 19, alongside its new features. No separate system for old transactions.

DECISION D-03: PRODUCTION UPGRADE TIMING

Planned: production upgraded in its own weekend (5–7 Nov) after sign-off, so cutover night carries only the Urban Eats switch. Alternative: upgrade on the cutover night of 31 Dec. Please confirm by Thu 29 Oct.

SECTION 5 · PART 2

Urban Eats Foundation: Structure, Products & Inventory

WS 2 Structure & finance

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
2.1	Architecture document: Urban Eats as one company (one CR, one VAT number, one set of accounts); analytic plans **Brand** (MYLK, Finjan, Shared) and **Branch**; one warehouse and one POS per outlet, each POS with its own sales journal; one POS payment method per platform with its clearing account; reporting design; access model. Odoo's "Branches" feature is not used.	Thu 22 Oct	Code-ox · Consultant	Document · approval Tue 27 Oct
2.2	Decision D-02: POS revenue tagging, Option 1 (fully standard) or Option 2 (small isolated module)	Tue 27 Oct	Tara · Owner Tara · Finance	Decision recorded
2.3	Company set-up: CR, VAT, address, fiscal year, chart of accounts, taxes, journals, bank accounts	Sun 1 – Tue 3 Nov	Code-ox · Consultant Tara · Finance (data by Sun 25 Oct)	Configured
2.4	Analytic plans and distribution models: purchases, expenses and invoices tagged to brand automatically by product, category, supplier or account	Tue 3 – Thu 5 Nov	Code-ox · Consultant	Configured
2.5	Shared finance: "Urban Eats Shared" cost tagging and optional brand allocation; B2B sales team fulfilled from Main Warehouse or Central Kitchen	Sun 8 – Tue 10 Nov	Code-ox · Consultant	Configured
2.6	Access rules: central team sees everything; outlet staff see only their own POS and warehouse	Wed 11 – Thu 12 Nov	Code-ox · Consultant	Role matrix
2.7	Option 2 module (only if chosen in D-02): Brand and Branch on POS configuration, tags copied to session revenue lines at closing	Sun 8 – Thu 19 Nov	Code-ox · Developers	Module + justification note

WS 3 Product master, procurement & inventory

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
3.1	Product types and coding scheme proposed	Tue 27 Oct	Code-ox · Consultant	Decision D-05 by Thu 29 Oct
3.2	Supplier list, vendor price lists, pack sizes and supplier barcodes completed in templates	By Sun 1 Nov	Tara · Procurement	Completed templates
3.3	Warehouses: Main Warehouse (receives all supplier deliveries), Central Kitchen, one per outlet; locations; resupply routes	Sun 1 – Thu 5 Nov	Code-ox · Consultant	Configured
3.4	Units of measure and conversions; lot and expiry tracking where needed	Tue 3 – Thu 5 Nov	Code-ox · Consultant	Configured
3.5	One generic material per ingredient; supplier products as vendor lines with code, pack size and price, **converted automatically on receipt**	Sun 8 – Tue 10 Nov	Code-ox · Consultant	Loaded; receipt test passed
3.6	Initial minimum stock levels per location	By Thu 12 Nov	Tara · Inventory	Levels sheet
3.7	Minimum stock rules at Main Warehouse, Central Kitchen and outlets; automatic replenishment tested	Sun 15 – Tue 17 Nov	Code-ox · Consultant	Rules active in test
3.8	Waste recorded with reasons; production cost from materials (labour and overhead per decision D-10)	Sun 15 – Thu 19 Nov	Code-ox · Consultant	Configured
3.9	**Foundation configured**, shown at the Thursday demo	Thu 12 Nov	Code-ox · Consultant Tara · Owner	**M4**

SECTION 6 · PART 2

Central Kitchen, Restaurant POS & Kitchen Display

WS 4 Central kitchen manufacturing

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
4.1	Recipe / BOM template issued: ingredients, quantities, yields, shelf life, make-to-stock, make-to-order or no-carry-over	Thu 22 Oct	Code-ox · Consultant	Template
4.2	Recipes for central kitchen products and outlet recipe kits completed	By Thu 5 Nov	Tara · Kitchen Lead	Completed template
4.3	Bills of materials loaded and checked with the kitchen lead	Sun 8 – Thu 12 Nov	Code-ox · Consultant	BOMs signed by kitchen lead
4.4	Daily production plan: demand plus minimum stock → manufacturing orders → automatic ingredient consumption → stock → transfers to outlets	Sun 15 – Thu 19 Nov	Code-ox · Consultant	Flow working on staging
4.5	One simple **"what to make today"** screen for kitchen staff	Sun 15 – Thu 19 Nov	Code-ox · Consultant	Screen demonstrated
4.6	Expiry dating; leftovers listed for daily disposal; waste with reasons	Sun 22 – Tue 24 Nov	Code-ox · Consultant	Configured
4.7	Outlet recipe kits: each POS sale deducts its ingredients from that outlet's stock	Sun 22 – Thu 26 Nov	Code-ox · Consultant	Stock deduction verified
4.8	**Kitchen flow ready**: walk-through with the kitchen lead	Thu 26 Nov	Tara · Kitchen Lead	**M5**

WS 5 Restaurant POS & Kitchen Display

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
5.1	Hardware & network spec issued; Tara orders devices: POS units, receipt and kitchen printers, KDS screens, card terminals, network per outlet	Spec Thu 29 Oct · on site by Thu 26 Nov	Code-ox · Tech Lead Tara · IT	Devices on site
5.2	Menus per brand validated from the Foodics export: items, prices, active status	By Thu 5 Nov	Tara · Operations	Validated menu files
5.3	POS configuration per outlet and brand: sales journal, payment methods (incl. one per delivery platform), receipt header, cash control	Sun 8 – Thu 12 Nov	Code-ox · Consultant	Configured
5.4	Menus loaded: POS categories, products, modifiers / attributes, combos, pricelists, taxes	Sun 8 – Tue 17 Nov	Code-ox · Consultant	Menus checked by outlet lead
5.5	Receipts with ZATCA QR; floor plans and tables where dine-in applies	Sun 15 – Thu 19 Nov	Code-ox · Consultant	Receipt approved
5.6	Kitchen Display per outlet, routed by station	Sun 15 – Thu 19 Nov	Code-ox · Consultant	Routing tested
5.7	Offline mode, session opening / closing and cash procedure written for outlet staff	Sun 22 – Tue 24 Nov	Code-ox · Consultant	Outlet procedure
5.8	On-site hardware test at a pilot outlet: printers, KDS, terminals, network, offline behaviour	Tue 24 – Thu 26 Nov	Code-ox · Tech Lead Tara · IT Tara · Outlet manager	Test record
5.9	**POS & payments ready**	Thu 26 Nov	Tara · Operations	**M5**

SECTION 7 · PART 2

Delivery Platforms

The list is the same under both options: **HungerStation, Jahez (incl. Noon), Keeta, The Chefz, ToYou, Ninja, Mrsool**. The structure is the same too: Brand › Branch › Platform Store › POS / Kitchen, so a new branch or brand is added by configuration. Decision D-01 (Option A or B) is due at kick-off.

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
6.1	Store inventory: every outlet × brand × platform with store IDs and merchant accounts	By Thu 22 Oct	Tara · Operations Code-ox · Consultant	Store map

WS 6A Option A: Code-ox Aggregator Hub

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
6.A1	API access requested from each platform on Tara Holding's behalf, per entity merchant account. Requests are already sent; follow-up every week. Confirmed: HungerStation, Keeta, Jahez (incl. Noon). In progress: The Chefz, ToYou, Ninja, Mrsool.	From kick-off · weekly	Code-ox · Lead Platforms	API status in weekly report
6.A2	Per-platform integration plan: endpoints, order states, menu / stock sync, cancellations and rejections as each API allows	Thu 29 Oct	Code-ox · Tech Lead	Plan shared
6.A3	Hub core in your Odoo: orders into POS and Kitchen Display; menu and price push; sold-out and stock sync; status updates back; failure and retry handling; logs and alerts; multiple branches and store IDs	Sun 1 – Thu 19 Nov	Code-ox · Developers	Core on staging
6.A4	Platform connectors for HungerStation, Jahez (incl. Noon) and Keeta	Sun 8 – Thu 26 Nov	Code-ox · Developers	Test orders end to end
6.A5	Connectors for The Chefz, ToYou, Ninja and Mrsool, each built and tested within about 10 business days of its API being issued	As each API arrives	Code-ox · Developers Platforms	Test orders end to end
6.A6	Platform-side testing or certification where a platform requires it	Sun 22 Nov – Thu 17 Dec	Code-ox · Developers Platforms	Platform confirmation
6.A7	A platform whose API is not issued in time keeps its own tablet at go-live and is connected when its API arrives, within the agreed scope and price	Reviewed at Go / No-Go	Code-ox · Lead	Status per platform

WS 6B Option B: UrbanPiper (standard connector, configuration only)

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
6.B1	Joint Odoo / UrbanPiper meeting outcome; UrbanPiper subscription ordered through Odoo; Saudi coverage incl. Keeta confirmed	By Thu 22 Oct	Tara · Owner Odoo UrbanPiper	Subscription active
6.B2	UrbanPiper stores per outlet and brand; platform linking through UrbanPiper's onboarding (timing with UrbanPiper and the platforms)	Sun 25 Oct – Thu 19 Nov	UrbanPiper Code-ox · Consultant	Stores linked
6.B3	Connector configuration: menu sync, store hours, payment method per platform, routing to POS and Kitchen Display	Sun 15 – Thu 26 Nov	Code-ox · Consultant	Configured
6.B4	Connector demonstrated on staging (HungerStation orders are rejected in the HungerStation app, not in Odoo POS)	Thu 26 Nov	Code-ox · Consultant	Demo held

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
6.9	**Platforms connected in test**, subject to platform approvals	Thu 26 Nov	Tara · Operations	**M6**

SECTION 8 · PART 2

Settlement & Payments

WS 7 Settlement & reconciliation

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
7.1	Payout statements, reports and files collected from each platform	Sun 25 Oct – Thu 5 Nov	Tara · Finance Code-ox · Consultant	Samples per platform
7.2	Settlement plan with automation level, following Odoo's official response (decision D-09)	Thu 12 Nov	Code-ox · Consultant	Settlement plan
7.3	Clearing account per platform; reconciliation of gross sales, commission, VAT on commission, promotions, refunds, cancellations, adjustments, penalties, delivery charges, net payout	Sun 15 – Thu 26 Nov	Code-ox · Consultant	Configured
7.4	Reports by platform, brand and branch; tested in UAT with a real payout statement from each platform	Sun 22 Nov – Thu 17 Dec	Code-ox · Consultant Tara · Finance	UAT result

WS 8 Payments

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
8.1	Odoo 19 availability confirmed for Geidea, NearPay and Paymob terminals **before you commit**	Thu 29 Oct	Code-ox · Tech Lead	Written confirmation → D-06 by Thu 5 Nov
8.2	Merchant accounts and API keys (test and live): Paymob, Tabby, Tamara	By Sun 1 Nov	Tara · Finance	Keys shared securely
8.3	Paymob online payments: Mada, Visa / Mastercard, Apple Pay as enabled on your account	Sun 8 – Thu 12 Nov	Code-ox · Developers	Test payments
8.4	Tabby and Tamara integration built by Code-ox	Sun 8 – Thu 19 Nov	Code-ox · Developers	Test payments + refunds
8.5	POS terminal integration for the provider(s) chosen in D-06	Sun 15 – Thu 26 Nov	Code-ox · Developers Tara · IT (devices)	Terminal tests at pilot outlet
8.6	Rules: order marked paid only on terminal or gateway confirmation; refunds to the original method where supported; failed payments retried or switched	Sun 22 – Thu 26 Nov	Code-ox · Developers	Test cases passed

PAYMENT TESTING

Every payment method is tested in test mode on staging, then with small live transactions at the pilot outlet during UAT and again in the go-live smoke test. Provider fees are paid directly to each provider (proposal, page 9).

SECTION 9 · PART 2

WhatsApp, Loyalty & ZATCA

WS 9 WhatsApp (standard Odoo Enterprise app)

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
9.1	Meta Business verification, dedicated number, Business Manager access	By Thu 5 Nov	Tara · Marketing Meta	Verified account
9.2	WhatsApp connected to Odoo; templates drafted: receipts, order confirmations, customer messages	Sun 8 – Thu 12 Nov	Code-ox · Consultant	Drafts for approval
9.3	Templates submitted to Meta; kitchen and delivery status messages reviewed with you case by case before anything is built (D-08)	Submit by Thu 19 Nov	Code-ox · Consultant Tara · Marketing	Meta approval
9.4	Automatic sending where possible; tested in UAT	Sun 22 – Thu 26 Nov	Code-ox · Consultant	Messages received in test

WS 10 Loyalty, promotions & rewards (MYLK)

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
10.1	Session with management: loyalty and promotion ideas, each assessed as standard, configuration, supported app or custom (last option)	Tue 3 Nov	Code-ox · Consultant Tara · Marketing	Ideas assessed
10.2	Programs agreed (D-07)	By Thu 12 Nov	Tara · Marketing	Program list
10.3	Configuration: points and rewards; % and fixed discounts; coupons and promo codes; Buy X Get Y; gift cards and eWallet; POS and eCommerce; validity and conditions; separate programs per brand	Sun 15 – Tue 24 Nov	Code-ox · Consultant	Configured
10.4	Demonstration to your team; loyalty and gift-card balances from Foodics as available (gap report 0.9)	Thu 26 Nov	Code-ox · Consultant	Demo held

WS 11 ZATCA Phase 2

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
11.1	Company VAT, CR and address; invoice journal per POS; one-tap default customer for walk-in sales	Sun 1 – Thu 12 Nov	Code-ox · Consultant	Configured
11.2	Fatoora portal administrator nominated, with access for simulation onboarding	By Thu 19 Nov	Tara · Finance	Access confirmed
11.3	Simulation onboarding and compliance checks for each POS journal on staging	Sun 22 – Thu 26 Nov	Code-ox · Consultant ZATCA	Compliance passed
11.4	UAT: simplified and standard invoices, credit notes, B2B invoices, rejected-invoice handling	Tue 1 – Thu 17 Dec	Tara · Finance Code-ox · QA	UAT result
11.5	**Production onboarding** of each POS journal (OTP generated by your Fatoora administrator)	Tue 29 – Wed 30 Dec	Code-ox · Consultant Tara · Finance	Production certificates

SECTION 10

Foodics Migration & Historical Archive

Migrated: menus, categories, products, modifiers and customers per brand. Archived: full history in open formats under your control. Opening stock comes from a physical count at cutover. Foodics stays live until the last order on 31 December.

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
12.1	Foodics console and API access; data inventory; **gap report** on what Foodics can and cannot export (e.g. loyalty or gift-card balances), flagged at the start	Sun 18 – Thu 22 Oct	Code-ox · Consultant Tara · IT	Gap report
12.2	Trial export 1 and field mapping per brand	Sun 25 – Thu 29 Oct	Code-ox · Consultant	Mapping sheet
12.3	Data validation and clean-up by your team: menu prices, active items, duplicate customers	Sun 1 – Thu 5 Nov	Tara · Operations Tara · Marketing	Validated files
12.4	Trial load 1 into the build environment; counts and samples checked	Sun 8 – Thu 12 Nov	Code-ox · Consultant	Load report
12.5	Trial load 2 into the UAT environment	Sun 29 – Mon 30 Nov	Code-ox · Consultant	Load report
12.6	**Archive export 1**: all history to date: sales and orders, payments, products, menus, modifiers and categories, customers, discounts, promotions, refunds, cancellations, inventory history, loyalty / gift-card balances, tax and financial reports, branch and store configuration. CSV / Excel and PDF, plus a draft index and data dictionary.	Sun 13 – Thu 17 Dec	Code-ox · Consultant	Archive v1 in your storage
12.7	Rehearsal load using the cutover method, with timings recorded	Sun 20 – Mon 21 Dec	Code-ox · Consultant	Rehearsal report
12.8	Menu freeze in Foodics: any change after this date is applied in both systems by Code-ox	From Sun 27 Dec	Tara · Operations	Freeze notice
12.9	**Final export** after the last Foodics transaction	Night of Thu 31 Dec	Code-ox · Consultant	Final export
12.10	Opening stock from physical count at every outlet, Main Warehouse and Central Kitchen, posted before the first sale	Night 31 Dec – before opening 1 Jan	Tara · Inventory Tara · Outlet managers Code-ox · Consultant	Count sheets + inventory adjustment
12.11	Final archive with complete **index and data dictionary**: each dataset, its period and what it contains	Sun 3 Jan 2027	Code-ox · Consultant	Archive handed over

Data objects

OBJECT	SOURCE	METHOD	VALIDATED BY
Menus, categories, products, modifiers, combos	Foodics export	Import templates, per brand	Operations
Customers (incl. loyalty data where exported)	Foodics export	Import with de-duplication	Marketing
Ingredients, vendor lines, pack sizes, barcodes	Your procurement data	Templates 3.2	Procurement
Recipes / BOMs and outlet recipe kits	Kitchen team	Templates 4.1	Kitchen Lead
Minimum stock levels	Inventory team	Template 3.6	Inventory
Users and roles (all staff incl. cashiers)	HR / Operations	User list by Thu 19 Nov	Owner
Opening stock	Physical count at cutover	Count sheets → inventory adjustment	Inventory + outlet managers
Sales history, reports, balances	Foodics	Archive only (not migrated as transactions)	Finance

SECTION 11

Testing, UAT & Training

Tested at every level, from build to full rehearsal, before your users accept anything, and every role trained before it uses the system.

LEVEL	WHEN	WHO	EXIT CRITERIA
Build testing	Continuous, Wk 3–6	Code-ox consultants and developers	Each item tested before the Thursday demo
Thursday demos	Weekly from Thu 12 Nov	Your key users	Feedback logged in the tracker
System integration test	Sun 22 – Mon 30 Nov	Code-ox QA	All end-to-end flows pass incl. platforms, payments, ZATCA simulation; internal test report (M7)
UAT cycle 1	Sun 6 – Thu 10 Dec	Your key users, guided by Code-ox	All scenarios executed; defects logged daily
UAT cycle 2 + day-in-the-life	Sun 13 – Thu 17 Dec	Key users with kitchen and one outlet team	Re-tests passed; a full trading day simulated end to end
Cutover rehearsal	Sun 20 – Mon 21 Dec	Code-ox, your IT and inventory leads	Deployment and data load timed and documented
Regression & sign-off	Tue 22 – Thu 24 Dec	Code-ox QA, project owner	No open Critical or High issues → UAT acceptance (M9)

UAT scenarios (scripts issued Thu 26 Nov)

- Purchase → receipt with pack conversion → bill → payment
- Central kitchen day: plan → MOs → consumption → transfers
- Expiry, leftovers disposal and waste with reasons
- Minimum stock replenishment to outlets
- Dine-in and takeaway with modifiers, combos and floor plan
- Delivery order per platform → KDS → status back; sold-out sync
- Card, Mada, Apple Pay, Tabby, Tamara; split payment; refund; failed payment
- Offline POS; session closing and cash control
- ZATCA simplified and standard invoices, credit notes
- B2B order, delivery and invoice
- Loyalty earn and redeem; coupon; gift card; eWallet
- WhatsApp receipt and order confirmation
- Platform payout reconciliation
- P&L by brand, branch and channel; stock value by outlet
- Access rules for each role

Training plan

- **Key users (train-the-trainer)**: Tue 1 – Thu 3 Dec, before UAT starts
- **Finance & accounting**: Sun 13 – Mon 14 Dec (2 sessions)
- **Procurement & warehouse**: Tue 15 Dec
- **Central kitchen**: Wed 16 Dec, plus on the floor during the day-in-the-life test
- **Marketing** (loyalty, WhatsApp): Thu 17 Dec
- **Outlet managers & cashiers**: Sun 20 – Thu 24 Dec, by outlet group: POS, KDS, payments, delivery orders, ZATCA, offline mode, closing
- **IT / in-house developer**: Tue 22 Dec, covering repository, modules, deployment and integration monitoring; full handover in January
- **Refresher & go-live briefing**: Tue 29 – Wed 30 Dec
- Materials: role guides and quick-reference cards by Mon 30 Nov; attendance lists by Thu 3 Dec; attendance recorded per session

ACCEPTANCE CRITERIA (PROPOSAL, PAGE 10)

Upgrade: documented before / after validation signed off by finance for each of the six companies, and all agreed flows pass on staging, before production is touched. **UAT**: agreed scenarios pass on staging with no open Critical or High issues. **Go-live**: production live on Odoo 19, POS selling, ZATCA invoices accepted and orders flowing from the connected platforms, with any remaining Normal issues listed and scheduled.

SECTION 12

Cutover & Go-Live

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
15.1	Cutover runbook (hour by hour) and rollback plan shared	Thu 17 Dec	Code-ox · Lead	Runbook
15.2	Cutover rehearsal on a fresh copy of production; timings recorded; runbook updated	Sun 20 – Mon 21 Dec	Code-ox · Tech Lead Tara · IT	Rehearsal report
15.3	UAT acceptance; code freeze	Thu 24 Dec	Tara · Owner	**M9**
15.4	Stock count teams, count sheets and outlet go-live contacts confirmed; Foodics end date decided (D-12)	By Thu 24 Dec	Tara · Inventory Tara · Operations	Count plan
15.5	Urban Eats deployed to production: modules from your repository, configuration, master data, users and access (no transactions yet)	Sun 27 – Mon 28 Dec	Code-ox · Tech Lead Code-ox · Consultant	Deployment checklist
15.6	**Go / No-Go meeting** against the checklist below	Tue 29 Dec	Steering committee	**M10**
15.7	ZATCA production onboarding per POS journal; refresher training	Tue 29 – Wed 30 Dec	Code-ox · Consultant Tara · Finance	Certificates
15.8	Final checks at every outlet: devices, printers, KDS, terminals, network, platform store mapping	Wed 30 Dec	Code-ox · Tech Lead Tara · Outlet managers	Outlet checklist

Cutover night: Thu 31 Dec → Fri 1 Jan (T = closing of each outlet)

TIME	STEP	OWNER
31 Dec 09:00	Command centre opens (Code-ox + your project owner); runbook review. Trading continues on Foodics as normal.	Code-ox · Lead
Afternoon	Central kitchen finishes the day's production; Main Warehouse and Central Kitchen counted once movement stops	Tara · Inventory
T	Last Foodics order at the outlet; shift closed; end-of-day report saved	Tara · Outlet manager
T + 15 min	Delivery platform stores switched from tablets to Odoo (Option A hub or Option B UrbanPiper)	Code-ox · Developers
T → T + 3 h	Physical stock count at the outlet; counts entered as opening stock and checked	Tara · Outlet team; Code-ox · Consultant
After last outlet	Final Foodics export started (12.9)	Code-ox · Consultant
Before opening	Smoke test per outlet: open session, test sale on each payment method, refund, KDS ticket, ZATCA invoice accepted, platform test order. Test documents reversed per procedure.	Code-ox · QA; Tara · Outlet manager
Before opening	**Go confirmation for each outlet** from outlet manager and Code-ox	Both
1 Jan opening	**First live sales on Odoo**: monitoring of orders, payments, ZATCA queue and platform sync; hourly check-ins on day 1	Code-ox · all; Tara · Owner
1 Jan close	Day-1 review: issues, fixes and plan for day 2	Both

Go / No-Go checklist (Tue 29 Dec)

- UAT accepted; no open Critical or High issues
- Production deployment verified (15.5)
- Hardware and terminals tested at every outlet
- Platform status known for each platform; any not ready stays on its tablet
- All roles trained; attendance recorded
- Count teams and Fatoora administrator confirmed
- Rollback plan and support rota published

Rollback

- A Critical blocker found before opening on 1 Jan: the steering committee decides by an agreed time. The affected outlet(s) trade one more day on Foodics while it is fixed, which is why the Foodics account stays active until the archive is verified (D-12).
- The existing six companies are not affected: they have run on Odoo 19 since November (D-03).
- If D-03 is the 31 Dec upgrade instead, production is restored from the pre-upgrade backup. That restore is tested at the rehearsal.

SECTION 13

Hypercare, Handover & Support

Two weeks of close support after go-live, a full handover so your developer owns the system, then six months of support under the SLA.

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
16.1	Daily 30-minute check-in; issue log shared daily; monitoring of platform sync, payments and ZATCA submissions	Fri 1 – Thu 14 Jan	Code-ox · Consultant Tara · Owner	Daily log
16.2	Floor support for outlets and kitchen in the first days, on site or remote as agreed in the runbook	Fri 1 – Sun 3 Jan	Code-ox · Consultant	Support rota
16.3	Final Foodics archive with index and data dictionary (12.11)	Sun 3 Jan	Code-ox · Consultant	Archive handed over
16.4	Go-live report: what went live, open items, platform status, next steps	Thu 7 Jan	Code-ox · Lead	Report
16.5	First weekly stock, waste and production review with kitchen and inventory leads	Thu 7 Jan	Code-ox · Consultant Tara · Kitchen	Review notes
16.6	First platform payout reconciliations with finance	As payouts arrive in January	Code-ox · Consultant Tara · Finance	Reconciled payouts
16.7	**Handover pack**: complete source in your repository, deployment instructions, migration scripts, technical, integration / API and configuration documentation; technical session with your developer	Thu 14 Jan	Code-ox · Tech Lead Tara · IT	Signed handover · **M13**
16.8	Go-live acceptance feedback within 5 business days (proposal terms)	By Thu 7 Jan	Tara · Owner	Acceptance
16.9	First month-end close on the new system, supported with finance	Sun 31 Jan – Thu 4 Feb	Code-ox · Consultant Tara · Finance	Close completed
16.10	Six months of support under the SLA; monthly support review meeting	1 Jan – 30 Jun 2027	Code-ox · Lead	Monthly review notes · M14

Support SLA (from the proposal, page 10)

PRIORITY	RESPONSE	FIX / WORKAROUND
Critical: POS, payment, platform, order sync or ZATCA down	1 hour, 7 days a week, by phone or WhatsApp	4 hours, including Friday and Saturday
High	4 hours	1 business day
Normal	1 business day	3 business days

AFTER THE SIX MONTHS

Support continues under an AMC at your option, at the rate on page 7 of the proposal. New branches, brands, platforms and new requirements are quoted in writing before work starts, at the indicative rates in the proposal.

SECTION 14

Week-by-Week Calendar

WEEK	CODE-OX	TARA HOLDING	MEETINGS & MILESTONES
Wk 0 11–15 Oct	Demo (Mon 12); kick-off pack; tracker set-up	Financial acceptance; signed agreement; owner and key users named; D-01; Odoo.sh and Foodics access	Kick-off by Thu 15 · **M0**
Wk 1 18–22 Oct	Workshops daily; backup & staging upgrade; Studio and module migration; pre-validation; assessment & register (Tue 20); architecture, migration plan, gap report (Thu 22)	Attend workshops; company validators; outlet & store list; module licences; repository	Steering Sun 18; report Thu 22
Wk 2 25–29 Oct	Support department validation; fixes; coding scheme (Tue 27); integration plan, hardware spec, terminal availability (Thu 29); Foodics trial export	Validate on staging (25–28); approve architecture, D-02, D-04 (Tue 27); D-05, D-03; **finance sign-off per company (Thu 29)**; Urban Eats CR / VAT / accounts data (Sun 25)	**M1** Tue 27 · **M2** Thu 29
Wk 3 1–5 Nov	Company, accounts, taxes, journals, analytic plans; warehouses, routes, UoM; upgrade runbook (Tue 3); loyalty session (Tue 3); **production upgrade Thu 5 night**	Supplier data and payment keys (Sun 1); data clean-up; menus and recipes (Thu 5); Meta verification (Thu 5); D-06, D-10 (Thu 5); finance checks Sat 7	**M3** weekend 5–7 Nov
Wk 4 8–12 Nov	Materials & vendor lines; shared ops; access; BOMs; POS configs; menus; Paymob; Tabby / Tamara; hub core or UrbanPiper stores; WhatsApp drafts; ZATCA journals; trial load 1	Minimum stock levels; D-07, D-08, D-09 (Thu 12)	First Thursday demo · **M4** Thu 12
Wk 5 15–19 Nov	Daily production plan; kitchen screen; stock rules; KDS; receipts; menus done; terminals; platform connectors; settlement; loyalty; waste & costing; WhatsApp templates submitted	Fatoora access; user list and roles (Thu 19)	Thursday demo
Wk 6 22–26 Nov	Expiry & leftovers; recipe kits; offline & cash procedure; payment rules; ZATCA simulation; WhatsApp automations; platform tests; system test; pilot-outlet hardware test; UAT scripts (Thu 26)	Hardware & terminals on site; Odoo subscription users / apps updated; UAT testers named (Thu 26)	**M5** · **M6** Thu 26
Wk 7 29 Nov–3 Dec	Internal test report and trial load 2 (Mon 30); UAT environment built from production copy; materials ready; **UAT live Tue 1 Dec**; key-user training	Agree UAT scripts (Mon 30); key users trained; attendance lists (Thu 3)	**M7** Mon 30 · **M8** Tue 1 Dec
Wk 8 6–10 Dec	UAT cycle 1 support; daily fixes; platform testing	Execute scenarios; log defects daily	Daily stand-up
Wk 9 13–17 Dec	UAT cycle 2 + day-in-the-life; archive export 1; training (finance, procurement, kitchen, marketing); cutover runbook (Thu 17)	Re-test; staff the day-in-the-life; attend training	Daily stand-up
Wk 10 20–24 Dec	Cutover rehearsal (20–21); regression; outlet staff training; IT session (Tue 22); code freeze	**UAT sign-off (Thu 24)**; count teams; D-12	**M9** Thu 24
Wk 11 27–31 Dec	Production deployment (27–28); ZATCA production onboarding (29–30); outlet checks (30); **cutover night 31 Dec**	Menu freeze; Go / No-Go (Tue 29); Fatoora OTPs; refresher training; stock count	**M10** Tue 29 · **M11** Thu 31
Fri 1 Jan	**Go-live**: command centre; hourly check-ins	Outlets open on Odoo; no new transactions on Foodics	**M12**
Wk 12 3–7 Jan	Hypercare; final archive (Sun 3); go-live report (Thu 7); first stock & waste review	Daily check-in; go-live feedback	Daily check-in
Wk 13 10–14 Jan	Hypercare; payout reconciliations; **handover pack (Thu 14)**	Technical handover with your developer	**M13** Thu 14

EVERY WEEK

Steering on Sunday · Thursday demo (from 12 Nov) · written status report on Thursday · live tracker in Odoo Project. After hypercare: first month-end close 31 Jan – 4 Feb, then monthly support reviews to 30 Jun 2027.

SECTION 15

Your Inputs & Decisions

Inputs from Tara Holding

ID	INPUT	DUE	OWNER
I-01	Signed agreement and advance payment	Thu 15 Oct	Sponsor
I-02	Project owner and key users named per area	Thu 15 Oct	Sponsor
I-03	**Odoo.sh access**; staging confirmed; Code-ox registered as partner on the subscription **(critical path)**	Sun 18 Oct	IT
I-04	Foodics console and API access	Sun 18 Oct	IT
I-05	Platform merchant accounts / authorisation per entity for API requests (Option A) or UrbanPiper order (Option B)	Sun 18 Oct	Operations
I-06	Six companies with a finance validator each; input to the validation checklist	Tue 20 Oct	Finance
I-07	Licences and source for third-party modules as listed in the register	Tue 20 Oct	IT
I-08	Outlet list: brands, address, hours, devices, platform store IDs	Thu 22 Oct	Operations
I-09	Repository for custom code in Tara Holding's name, with Code-ox access	Thu 22 Oct	IT
I-10	Urban Eats CR, VAT number, address, chart of accounts preferences, bank accounts	Sun 25 Oct	Finance
I-11	Suppliers, vendor price lists, pack sizes, barcodes	Sun 1 Nov	Procurement
I-12	Paymob, Tabby, Tamara merchant accounts and API keys	Sun 1 Nov	Finance
I-13	Validated menus per brand and recipes / BOMs	Thu 5 Nov	Operations, Kitchen
I-14	Meta Business verification, WhatsApp number, Business Manager access	Thu 5 Nov	Marketing
I-15	Initial minimum stock levels per location	Thu 12 Nov	Inventory
I-16	Fatoora portal administrator and access	Thu 19 Nov	Finance
I-17	User list with roles (all staff incl. cashiers)	Thu 19 Nov	Operations
I-18	POS hardware, printers, KDS screens, card terminals and network on site	Thu 26 Nov	IT
I-19	Odoo subscription updated for the users and apps needed (count from Code-ox by Thu 12 Nov)	Thu 26 Nov	IT
I-20	Named UAT testers and calendar	Thu 26 Nov	Owner
I-21	Training attendance lists per session	Thu 3 Dec	Operations
I-22	Stock count teams and outlet go-live contacts	Thu 24 Dec	Inventory
I-23	Fatoora administrator available for OTPs; outlet managers on cutover night	29–31 Dec	Finance, Operations

Decisions

ID	DECISION	DUE
D-01	Part 2 delivery-platform layer: Option A (Code-ox Aggregator Hub) or Option B (UrbanPiper)	Thu 15 Oct
D-02	POS revenue tagging: Option 1 fully standard or Option 2 small isolated module	Tue 27 Oct
D-03	Production upgrade window: weekend 5–7 Nov (as planned) or cutover night 31 Dec	Thu 29 Oct
D-04	Treatment of each third-party module, incl. the replacement MCP app	Tue 27 Oct
D-05	Product types and coding scheme	Thu 29 Oct
D-06	POS terminal provider(s): Geidea, NearPay, Paymob	Thu 5 Nov
D-07	Loyalty and promotion programs for MYLK	Thu 12 Nov
D-08	Kitchen and delivery status WhatsApp messages: which, if any, to automate	Thu 12 Nov
D-09	Settlement automation level (after Odoo's official response)	Thu 12 Nov
D-10	Labour and overhead in production cost (optional)	Thu 5 Nov
D-11	Training language(s) and session format	Thu 26 Nov
D-12	Foodics account end date (kept active until the final archive is verified)	Thu 24 Dec
D-13	Go / No-Go	Tue 29 Dec

SECTION 16

Deliverables

Every document Code-ox delivers, with its due date. Each one is shared for review in the tracker; documents that need your approval are marked in the related task.

ID	DELIVERABLE	DUE
DL-01	Execution plan (this document) and live tracker in Odoo Project	Sun 18 Oct
DL-02	Kick-off pack: team, contacts, cadence, severity definitions, templates	Sun 18 Oct
DL-03	Written upgrade assessment and module-by-module register	Tue 20 Oct
DL-04	Urban Eats architecture document	Thu 22 Oct
DL-05	Upgrade validation report per company (before / after)	Thu 22 Oct → sign-off Thu 29 Oct
DL-06	Data migration plan, import templates, Foodics gap report	Thu 22 Oct
DL-07	Per-platform integration plan (A) or UrbanPiper configuration plan (B)	Thu 29 Oct
DL-08	POS hardware and network specification	Thu 29 Oct
DL-09	Production upgrade runbook	Tue 3 Nov
DL-10	Settlement plan	Thu 12 Nov
DL-11	Written justification for each custom item, before it is built	As raised
DL-12	UAT scenarios, scripts and calendar	Thu 26 Nov
DL-13	Internal test report	Mon 30 Nov
DL-14	Training materials: role guides and quick-reference cards	Mon 30 Nov
DL-15	Cutover runbook and rollback plan	Thu 17 Dec
DL-16	UAT report and acceptance form	Thu 24 Dec
DL-17	Go / No-Go checklist	Tue 29 Dec
DL-18	Foodics archive v1 (Thu 17 Dec); final archive with index and data dictionary	Sun 3 Jan 2027
DL-19	Go-live report	Thu 7 Jan 2027
DL-20	Handover pack: source, deployment instructions, migration scripts, technical / integration / configuration documentation	Thu 14 Jan 2027
DL-21	Weekly status report	Every Thursday

SECTION 17

Risks & Assumptions

Reviewed every Sunday at steering. New risks are added to the tracker with an owner and a mitigation.

ID	RISK	MITIGATION	OWNER
R1	Platform APIs issued late (Option A)	Requested on Tara's behalf already; weekly follow-up; connectors built in order of arrival; a late platform keeps its tablet and is connected when ready, within scope	Code-ox
R2	UrbanPiper onboarding or coverage timing (Option B)	Coverage confirmed in the joint meeting; stores started in Wk 2; uncovered platform stays on its tablet	Tara, UrbanPiper
R3	A third-party module has no Odoo 19 version	Register by Tue 20 Oct; migrate or replace; nothing removed without approval	Code-ox
R4	Validation time for six companies in one week	Code-ox prepares before / after reports so finance reviews differences only; checklist agreed in Wk 1	Both
R5	Recipe or menu data incomplete	Templates in Wk 1; workshop support; top-selling items first	Tara
R6	Foodics cannot export some data (e.g. balances)	Gap report in Wk 1, so the approach is agreed early	Code-ox
R7	Hardware, terminals or network not ready	Spec Thu 29 Oct; devices on site Thu 26 Nov; pilot-outlet test	Tara
R8	Key users unavailable in December	Named testers and calendar by Thu 26 Nov	Tara
R9	ZATCA onboarding issue near go-live	Simulation passed in Wk 6; OTP process rehearsed; administrator on standby	Both
R10	Late scope changes	Change control; code freeze from Thu 24 Dec	Both

ASSUMPTIONS

Tara Holding stays on Odoo.sh with one staging branch available · Urban Eats goes live at all outlets on 1 Jan 2027 · Scope, prices and terms are as in Financial Proposal CX-TARA-2026-02 Rev. 1; this plan does not change them · Third-party and platform fees are as listed on page 9 of the proposal.

ACCEPTANCE

Plan Acceptance

By signing, both parties agree this plan as the baseline for delivery. Changes to dates, owners or tasks are agreed at steering and recorded in the tracker. Changes to scope, cost or the committed dates of 1 December 2026 and 1 January 2027 follow the change control in Section 2.

FOR & ON BEHALF OF CODE-OX TECHNOLOGIES

AUTHORISED SIGNATORY

NAME & TITLE

DATE

FOR & ON BEHALF OF TARA HOLDING

AUTHORISED SIGNATORY

NAME & TITLE

DATE

CONTACT

Raghib Ali Rafeeque, Code-ox Technologies · raghib@code-ox.com · +966 561 765 707 · 3239 Al Zubair Bin Al Awwam St, Al Rawabi Dist., Riyadh 14215, KSA
