PROJECT EXECUTION PLAN · VERSION 1.1 · 12 OCTOBER 2026

From Kick-off to Go-live on 1 January 2027

The complete, week-by-week execution of the Odoo 18 → 19 upgrade and the Urban Eats / MYLK implementation: every task, owner, target week, input and sign-off, so your team can see how each of the coming months is managed.

WORK STARTS	UPGRADE SIGN-OFF	UAT ENVIRONMENT	GO-LIVE	SUPPORT
15 Oct	Week 2	1 Dec	1 Jan	30 Jun
2026 · Week 1	all six companies	committed	2027 · committed	2027 · six months

FIVE PHASES

PHASE 1	PHASE 2	PHASE 3	PHASE 4	PHASE 5
Discovery, design & upgrade	**Build Urban Eats**	**UAT & training**	**Cutover & go-live**	**Support under SLA**
Weeks 1–3 · in parallel	Weeks 3–7	Weeks 7–10	Week 11 · 1 Jan	1 Jan – 30 Jun

118 tasks with owners and target weeks
Across every workstream, each loaded into Odoo Project on your own Odoo.

Staging first, production last
Every department validates and finance signs off each company before production is touched.

Weekly visibility
Sunday steering, Thursday demo and a weekly status report until UAT sign-off; SLA support from go-live.

Your inputs and decisions planned
23 inputs and 13 decisions, each with a target week tied to the task that needs it.

DOCUMENT	COMPANION TO	DATE	PREPARED BY
Execution Plan v1.1	CX-TARA-2026-02 Rev. 1	12 October 2026	Code-ox Technologies

INTRODUCTION

Purpose, Principles & Key Dates

What this document is

- The execution plan for Financial Proposal **CX-TARA-2026-02 Rev. 1**: Part 1 (Odoo 18 → 19 upgrade) and Part 2 (Urban Eats / MYLK implementation).
- It expands the weekly plan on page 8 of the proposal into **every task, owner, target week, input and sign-off** from kick-off to the end of support.
- Every task ID here is loaded into **Odoo Project on your own Odoo** by end of Week 1, so your team sees status, owner and due date at any time.

How the plan is run

- **Standard Odoo first**: standard › configuration › Studio › supported module › custom development, each custom item justified in writing and approved by you.
- **Nothing reaches production untested**: upgrade validated on staging and signed off by every department before production is touched.
- **Continuity of data**: your POs, journal entries, invoices and history continue in Odoo 19 in the same database. Nothing is re-keyed into a separate system.
- **No surprises**: until UAT sign-off we meet once or twice a week and send a written status report every week; from go-live, support runs under the SLA.

Milestones

#	MILESTONE	TARGET DATE	CONFIRMED BY	EVIDENCE
M0	**Agreement signed & kick-off held**	Thu 15 Oct 2026	Both parties	Signed agreement; kick-off minutes
M1	**Upgrade assessment & Urban Eats architecture approved**	Week 2	Tara project owner	Approved assessment, module register and architecture document
M2	**Upgrade signed off on staging** (all six companies)	Week 2	Tara finance, per company	Signed before / after validation per company
M3	**Production upgraded to Odoo 19** (existing companies)	End of Week 3	Tara finance + IT	Post-upgrade checks signed; see decision D-03
M4	**Urban Eats foundation configured**	Week 4	Tara project owner	Thursday demo on staging
M5	**Central kitchen flow, POS & payments ready**	Week 6	Tara kitchen + outlets	Thursday demo; hardware test at pilot outlet
M6	**Delivery platforms connected in test**	Week 6	Tara outlets	Test orders per connected platform, subject to platform approvals
M7	**Internal testing complete; migration data loaded**	Week 7	Code-ox	Internal test report
M8	**Production-ready UAT environment live**	**Tue 1 Dec 2026**	Committed date	UAT environment handed over with logins and scripts
M9	**UAT acceptance**	Week 10	Tara project owner	UAT report; no open Critical or High issues
M10	**Go / No-Go decision**	Week 11	Steering committee	Go / No-Go checklist signed
M11	**Ready for cutover**	Thu 31 Dec	Both parties	Cutover runbook steps complete
M12	**Production go-live**: no new transactions on Foodics	**Fri 1 Jan 2027**	Committed date	POS selling, ZATCA accepted, platform orders flowing
M13	**Source & documentation handed over**	Week 13	Tara project owner + IT	Handover pack signed
M14	**Six-month support ends**	Wed 30 Jun 2027	Both parties	Support close-out; AMC at your option


DATES AND CONDITIONS

Work starts on **Thu 15 Oct 2026**, the first day of Week 1; each later week runs Sunday to Thursday. Activities are planned by target week; exact days within a week are agreed at the Sunday steering meeting. The 1 December and 1 January commitments rely on the conditions already in the proposal: signed agreement and kick-off by 15 October, access and data on the dates in Section 15, timely UAT feedback, and delivery-platform approvals, which neither party controls.

PLAN AT A GLANCE

Gantt: Kick-off to Handover

One view of every workstream across the thirteen weeks. Detailed tasks for each bar follow in Sections 3–13.

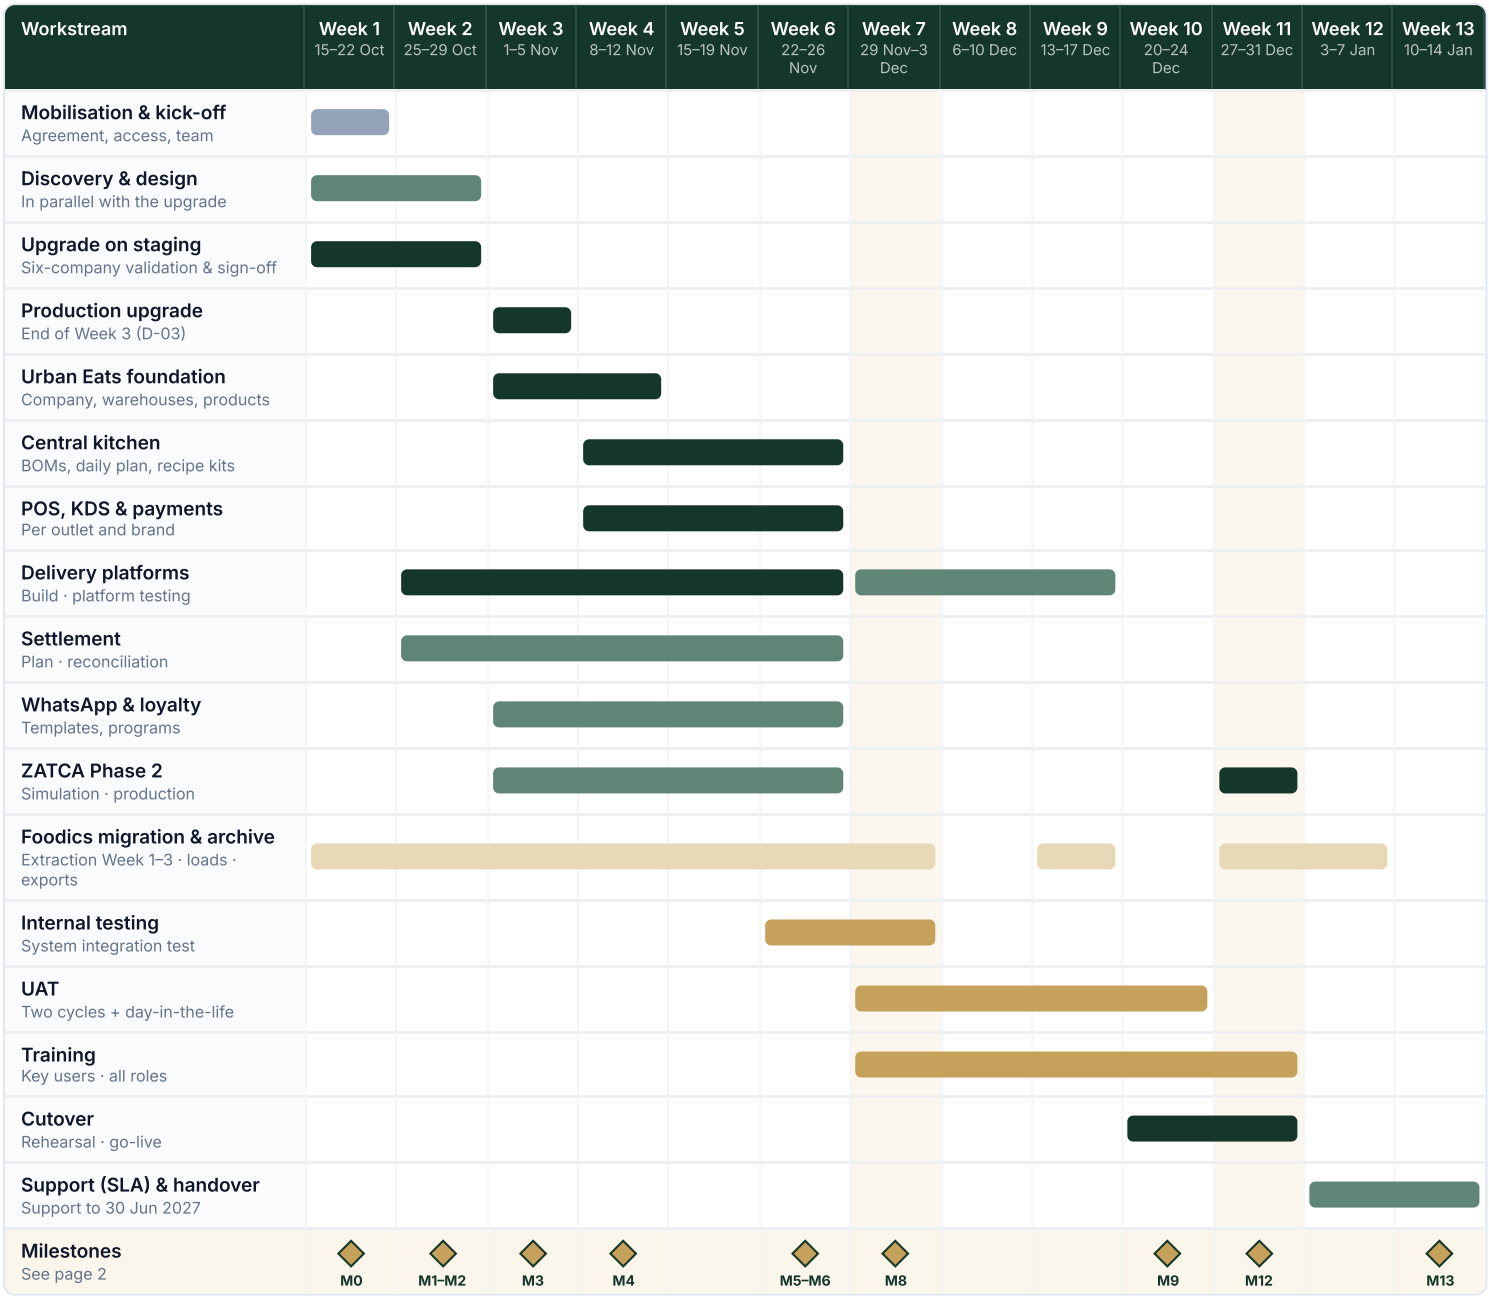

Build & go-live · Design, integration & support · Testing, UAT & training · Data migration · Mobilisation · Milestone

CRITICAL PATH

Odoo.sh access at kick-off → staging upgrade (Week 1) → finance sign-off (Week 2) → foundation (Week 3–4) → kitchen, POS & platforms (Week 4–6) → UAT environment **1 Dec** → UAT sign-off **Week 10** → go-live **1 Jan**.

HIGHLIGHTED COLUMNS

Week 7: the UAT environment goes live on Tue 1 Dec. **Week 11**: cutover week, ending on the night of 31 Dec for go-live on Fri 1 Jan 2027.

SECTION 1

Team, Roles & Governance

Code-ox Technologies

- **Engagement Lead**: Raghib Ali Rafeeque. Single point of contact for commercial matters and steering; owns the plan and weekly report.
- **Project Lead**: Mohammed Shajir. Leads delivery across every workstream: discovery and design, upgrade validation, build, UAT, training and go-live.
- **Delivery team**: functional, technical and testing specialists assigned and managed by Code-ox under the Project Lead.
- **Head of Operations**: Shabeeb K. Executive escalation and resourcing.

Tara Holding (names confirmed at kick-off)

- **Project Owner & single point of contact**: Eng. AbdulRahman Al-Nouman (to confirm). Decisions, approvals, access.
- **Executive Sponsor**: chairs steering; final Go / No-Go.
- **Finance Lead** and a **validator for each of the six companies**: upgrade sign-off, chart of accounts, settlement.
- **Procurement & Inventory Lead**: suppliers, products, stock rules, stock count.
- **Central Kitchen Lead**: recipes, production plan, expiry and waste rules.
- **Operations / Outlets Lead** with one manager per outlet: menus, POS, KDS, training.
- **Marketing Lead**: loyalty, promotions, WhatsApp templates.
- **IT / in-house developer**: Odoo.sh, repository, hardware, network, technical handover.

Meetings & reporting

FORUM	WHEN	WHO	PURPOSE
Kick-off	Thu 15 Oct · 2 hrs	Both teams, sponsor	Scope recap, team, this plan, access checklist, decisions D-01 to D-03
Steering committee	Every Sunday until UAT sign-off · 45 min	Sponsor, owner, Code-ox leads	Progress against plan, risks, decisions due, overdue inputs
Thursday demo / review	Every Thursday, Weeks 4–10 · 45 min	Owner + key users	Show what was built that week; during UAT, review open issues
Weekly status report	Every Thursday until go-live	Code-ox to Tara	Status per workstream (on track, at risk, late), % complete, done, next week, risks, decisions, Tara actions due
Live tracker	Always	Everyone	Odoo Project on your Odoo: every task ID, owner, due date and status

MEETING RHYTHM

We meet **once or twice a week until UAT sign-off** (Week 10): Sunday steering and the Thursday demo / review. After UAT the project moves to go-live, and from go-live every issue is raised through the support channel and handled **under the SLA**. A meeting is held only when a specific matter needs one.

Escalation

LEVEL	CODE-OX	TARA HOLDING	RESOLUTION TARGET
1	Project Lead	Area lead	Same business day
2	Engagement Lead	Project Owner	Within 2 business days
3	Head of Operations	Executive Sponsor	Next steering, or within 3 business days

SECTION 2

Who Does What

Who does each activity, who approves it, and who gives input. Everyone else is kept informed through the weekly status report and the live tracker. Green = Code-ox team · Gold = Tara Holding team.

ACTIVITY	DOES THE WORK	APPROVES	GIVES INPUT
Project plan, tracker, weekly report	Engagement Lead	Engagement Lead	Project Lead, Delivery team, Project Owner
Discovery & design	Project Lead, Finance & Procurement, Kitchen & Outlets	Engagement Lead	Delivery team, Project Owner, IT team
Upgrade assessment & module register	Project Lead, Delivery team	Engagement Lead	Project Owner, Finance & Procurement, IT team
Upgrade validation on staging	Project Lead, Delivery team, Finance & Procurement	Project Lead	Project Owner, Kitchen & Outlets, IT team
Finance sign-off per company	Finance & Procurement	Project Owner	Project Lead
Architecture document	Project Lead	Project Lead, Project Owner	Engagement Lead, Delivery team, Finance & Procurement, Kitchen & Outlets, IT team
Configuration & custom development	Project Lead, Delivery team	Project Lead	IT team
Master data, menus, recipes (provide & validate)	Finance & Procurement, Kitchen & Outlets	Project Owner	Project Lead, Delivery team
Delivery-platform API requests	Engagement Lead, Delivery team	Engagement Lead	Project Lead, Project Owner, Kitchen & Outlets
Hardware, terminals, network on site	Kitchen & Outlets, IT team	Project Owner	Project Lead, Delivery team
UAT scripts	Project Lead, Delivery team	Project Lead	Project Owner, Finance & Procurement, Kitchen & Outlets
UAT execution & acceptance	Project Lead, Delivery team, Finance & Procurement, Kitchen & Outlets	Project Owner	IT team
Training delivery / attendance	Project Lead, Finance & Procurement, Kitchen & Outlets, IT team	Project Lead	Delivery team, Project Owner
Cutover runbook	Project Lead, Delivery team	Engagement Lead	Project Owner, Finance & Procurement, Kitchen & Outlets, IT team
Physical stock count at cutover	Finance & Procurement, Kitchen & Outlets	Project Owner	Project Lead, Delivery team
Go / No-Go	Engagement Lead	Project Owner	Project Lead, Delivery team, Finance & Procurement, Kitchen & Outlets, IT team
Handover & support	Project Lead, Delivery team, IT team	Engagement Lead	Project Owner, Finance & Procurement, Kitchen & Outlets

SECTION 2 · CONTINUED

The Roles, Environments & Change Control

The roles on page 5

ROLE	TEAM	WHO	WHAT THEY DO IN THIS PROJECT
Engagement Lead	Code-ox	Raghib Ali Rafeeque	Single point of contact; owns the plan, weekly report, platform API requests and steering
Project Lead	Code-ox	Mohammed Shajir	Leads delivery across every workstream: design, upgrade validation, configuration, UAT, training and go-live
Delivery team	Code-ox	Assigned by Code-ox	Functional, technical and testing work under the Project Lead: configuration, integrations, custom modules, deployment and testing
Project Owner	Tara Holding	Eng. AbdulRahman Al-Nouman (to confirm)	Decisions and approvals for Tara Holding; chairs the Go / No-Go with the sponsor
Finance & Procurement	Tara Holding	Finance lead + one validator per company; procurement lead	Upgrade sign-off per company, accounts, suppliers, settlement, stock count
Kitchen & Outlets	Tara Holding	Central kitchen lead; operations lead; outlet managers	Recipes, menus, POS and kitchen testing, outlet training, cutover at each outlet
IT team	Tara Holding	IT / in-house developer	Odoo.sh access, repository, devices and network; receives the technical handover

Environments

- **Production** (Odoo.sh): your live six companies. Upgraded only after sign-off; Urban Eats deployed to it in cutover week.
- **Staging, upgrade validation**: copy of production upgraded to Odoo 19 for the before / after checks.
- **Staging, build & UAT**: where Urban Eats is built, demonstrated each Thursday and accepted in UAT.
- **Repository**: owned by Tara Holding; all custom modules, migration scripts and deployment notes.
- The UAT environment on 1 Dec is built from a fresh copy of production using the **same deployment package** used at go-live. The method is proven on 1 Dec and again at the Week 10 rehearsal before production.

Change control & defects

- **Change request**: logged in the tracker, then Code-ox gives impact on scope, cost and timeline **before any work starts**. Work starts only on your written approval.
- **Code freeze** from Week 10: Critical fixes only until go-live.
- **Critical**: blocks selling, payment, orders, ZATCA or a sign-off; handled first.
- **High**: key function impaired, workaround exists; handled next.
- **Normal**: minor or cosmetic; planned into the next UAT cycle.
- Every defect has an ID, owner, severity and status visible in the tracker.

SECTION 3

Phase 1: Discovery, Design & Upgrade in Parallel

Starts on 15 October. Discovery, design and the Odoo 19 upgrade run side by side, so the design is approved in writing before the build starts.

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
0.1	Financial acceptance; agreement signed; advance invoice issued	Thu 15 Oct	Tara · Sponsor Code-ox · Engagement Lead	Signed agreement
0.2	**Kick-off**: scope recap, teams, this plan, cadence, access checklist; decisions D-01 to D-03 opened	Thu 15 Oct	Code-ox · Engagement Lead Tara · Owner	Kick-off minutes · M0
0.3	Access granted: Odoo.sh (Code-ox as collaborator), staging confirmed, Code-ox registered as partner on your Odoo subscription	At kick-off · Week 1 latest	Tara · IT	Access checklist: **critical path**
0.4	Tracker loaded in Odoo Project on your Odoo: every task ID, owner and due date	Week 1	Code-ox · Engagement Lead	Live tracker
0.5	Kick-off pack: team list, contacts, cadence, severity definitions, templates	Week 1	Code-ox · Engagement Lead	Kick-off pack

DISCOVERY AND DESIGN RUN IN PARALLEL WITH THE UPGRADE

While the Odoo 19 upgrade is performed on staging (Section 4), Code-ox gathers the requirements for each area — structure & finance, procurement & inventory, central kitchen, outlets & POS, delivery platforms & settlement, marketing — and turns them into the documents below for your approval.

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
0.6	Written **upgrade assessment** & **module-by-module register**: compatibility, treatment (retain, migrate, replace, consolidate, retire), licence or vendor cost, risk	Week 1	Code-ox · Delivery team	Assessment + register
0.7	**Urban Eats architecture document** (Section 5)	Week 1	Code-ox · Project Lead	Document for approval
0.8	Data migration plan, import templates & Foodics gap report	Week 1	Code-ox · Project Lead	Plan + templates
0.9	Per-platform integration plan (Option A) or UrbanPiper configuration plan (Option B)	Week 2	Code-ox · Delivery team	Integration plan
0.10	POS hardware & network specification per outlet	Week 2	Code-ox · Delivery team	Spec for ordering
0.11	**Approval** of assessment, register and architecture; decisions D-02, D-04	Week 2	Tara · Owner	**M1**

SECTION 4 · PART 1

Odoo 18 → 19 Upgrade

Performed on staging first. Production is touched only after every department has validated its own data and your finance team has signed off each company. Foodics data is extracted in parallel during these weeks (Section 10).

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
1.1	Full backup of production; staging copy prepared on Odoo.sh	Week 1	Code-ox · Delivery team	Backup reference
1.2	Upgrade of the staging copy to Odoo 19 through Odoo's upgrade service	Week 1	Code-ox · Delivery team Odoo	Odoo 19 staging database
1.3	**Studio customisations** checked and corrected: custom fields, views, reports, automations, server actions, access rules	Week 1	Code-ox · Project Lead	Studio checklist, item by item
1.4	**Third-party modules** handled per register: simplify_access_management, advanced_web_domain_widget, auditlog, hide_menu_user, Hikvision attendance, muk_mcp, muk_mcp_access, muk_web_utils, notify_email_inbox, paymob, pos_paymob. A replacement MCP app for Odoo 19 is proposed. **No module removed without your written approval.**	Week 1	Code-ox · Delivery team Tara · IT (licences)	Register status per module
1.5	Code-ox pre-validation, **each of the six companies**, before vs after: trial balance; aged receivables & payables; tax reports & fiscal configuration; stock valuation; open customer invoices & vendor bills. Every difference listed with its cause, including where Odoo 19 itself changes a calculation or presentation.	Week 1	Code-ox · Project Lead Code-ox · Delivery team	Validation report per company
1.6	Key business flows tested against the agreed checklist: purchase → receipt → bill → payment; sale → delivery → invoice → payment; journal entries; bank reconciliation; multi-company and inter-company configuration; access rights	Week 1	Code-ox · Delivery team	Flow checklist results
1.7	**Department validation on staging**: finance for each company, procurement, inventory and every department using Odoo. Your users work on their own POs, journals and invoices in Odoo 19.	Week 2	Tara · Finance Tara · Departments Code-ox · Project Lead (on call)	Issue list
1.8	Fixes and re-tests for every issue raised	Week 2	Code-ox · Delivery team	Issues closed
1.9	**Sign-off by your finance team, per company**	Week 2	Tara · Finance	Signed forms · **M2**
1.10	Production upgrade runbook: timings, owners, checks, rollback by restore of the pre-upgrade backup	Week 3	Code-ox · Delivery team	Runbook shared
1.11	**Production upgrade** outside working hours at the end of Week 3: backup → upgrade → technical checks → finance spot checks → released before the next working day	Week 3	Code-ox · Delivery team Tara · Finance Tara · IT	Post-upgrade checks · **M3**
1.12	First-week monitoring and priority support for all users on Odoo 19	Week 4	Code-ox · Project Lead	Issue log

WHAT YOUR USERS WILL SEE

Same database, same records: every PO, journal entry, invoice and history line continues in Odoo 19, alongside its new features. No separate system for old transactions.

DECISION D-03: PRODUCTION UPGRADE TIMING

Planned: production upgraded in its own weekend (end of Week 3) after sign-off, so cutover night carries only the Urban Eats switch. Alternative: upgrade on the cutover night of 31 Dec. Please confirm by end of Week 2.

SECTION 5 · PART 2

Urban Eats Foundation: Structure, Products & Inventory

WS 2 Structure & finance

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
2.1	Architecture document: Urban Eats as one company (one CR, one VAT number, one set of accounts); analytic plans **Brand** (MYLK, Finjan, Shared) and **Branch**; one warehouse and one POS per outlet, each POS with its own sales journal; one POS payment method per platform with its clearing account; reporting design; access model. Odoo's "Branches" feature is not used.	Week 1	Code-ox · Project Lead	Document · approval Week 2
2.2	Decision D-02: POS revenue tagging, Option 1 (fully standard) or Option 2 (small isolated module)	Week 2	Tara · Owner Tara · Finance	Decision recorded
2.3	Company set-up: CR, VAT, address, fiscal year, chart of accounts, taxes, journals, bank accounts	Week 3	Code-ox · Project Lead Tara · Finance (data by end of Week 2)	Configured
2.4	Analytic plans and distribution models: purchases, expenses and invoices tagged to brand automatically by product, category, supplier or account	Week 3	Code-ox · Project Lead	Configured
2.5	Shared finance: "Urban Eats Shared" cost tagging and optional brand allocation; B2B sales team fulfilled from Main Warehouse or Central Kitchen	Week 4	Code-ox · Project Lead	Configured
2.6	Access rules: central team sees everything; outlet staff see only their own POS and warehouse	Week 4	Code-ox · Project Lead	Role matrix
2.7	Option 2 module (only if chosen in D-02): Brand and Branch on POS configuration, tags copied to session revenue lines at closing	Weeks 4–5	Code-ox · Delivery team	Module + justification note

WS 3 Product master, procurement & inventory

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
3.1	Product types and coding scheme proposed	Week 2	Code-ox · Project Lead	Decision D-05 by end of Week 2
3.2	Supplier list, vendor price lists, pack sizes and supplier barcodes completed in templates	By end of Week 3	Tara · Procurement	Completed templates
3.3	Warehouses: Main Warehouse (receives all supplier deliveries), Central Kitchen, one per outlet; locations; resupply routes	Week 3	Code-ox · Project Lead	Configured
3.4	Units of measure and conversions; lot and expiry tracking where needed	Week 3	Code-ox · Project Lead	Configured
3.5	One generic material per ingredient; supplier products as vendor lines with code, pack size and price, **converted automatically on receipt**	Week 4	Code-ox · Project Lead	Loaded; receipt test passed
3.6	Initial minimum stock levels per location	By end of Week 4	Tara · Inventory	Levels sheet
3.7	Minimum stock rules at Main Warehouse, Central Kitchen and outlets; automatic replenishment tested	Week 5	Code-ox · Project Lead	Rules active in test
3.8	Waste recorded with reasons; production cost from materials (labour and overhead per decision D-10)	Week 5	Code-ox · Project Lead	Configured
3.9	**Foundation configured**, shown at the Thursday demo	Week 4	Code-ox · Project Lead Tara · Owner	**M4**

SECTION 6 · PART 2

Central Kitchen, Restaurant POS & Kitchen Display

WS 4 Central kitchen manufacturing

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
4.1	Recipe / BOM template issued: ingredients, quantities, yields, shelf life, make-to-stock, make-to-order or no-carry-over	Week 1	Code-ox · Project Lead	Template
4.2	Recipes for central kitchen products and outlet recipe kits completed	By end of Week 3	Tara · Kitchen Lead	Completed template
4.3	Bills of materials loaded and checked with the kitchen lead	Week 4	Code-ox · Project Lead	BOMs signed by kitchen lead
4.4	Daily production plan: demand plus minimum stock → manufacturing orders → automatic ingredient consumption → stock → transfers to outlets	Week 5	Code-ox · Project Lead	Flow working on staging
4.5	One simple **"what to make today"** screen for kitchen staff	Week 5	Code-ox · Project Lead	Screen demonstrated
4.6	Expiry dating; leftovers listed for daily disposal; waste with reasons	Week 6	Code-ox · Project Lead	Configured
4.7	Outlet recipe kits: each POS sale deducts its ingredients from that outlet's stock	Week 6	Code-ox · Project Lead	Stock deduction verified
4.8	**Kitchen flow ready**: walk-through with the kitchen lead	Week 6	Tara · Kitchen Lead	**M5**

WS 5 Restaurant POS & Kitchen Display

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
5.1	Hardware & network spec issued; Tara orders devices: POS units, receipt and kitchen printers, KDS screens, card terminals, network per outlet	Spec Week 2 · on site by end of Week 6	Code-ox · Delivery team Tara · IT	Devices on site
5.2	Menus per brand validated from the Foodics export: items, prices, active status	By end of Week 3	Tara · Operations	Validated menu files
5.3	POS configuration per outlet and brand: sales journal, payment methods (incl. one per delivery platform), receipt header, cash control	Week 4	Code-ox · Project Lead	Configured
5.4	Menus loaded: POS categories, products, modifiers / attributes, combos, pricelists, taxes	Weeks 4–5	Code-ox · Project Lead	Menus checked by outlet lead
5.5	Receipts with ZATCA QR; floor plans and tables where dine-in applies	Week 5	Code-ox · Project Lead	Receipt approved
5.6	Kitchen Display per outlet, routed by station	Week 5	Code-ox · Project Lead	Routing tested
5.7	Offline mode, session opening / closing and cash procedure written for outlet staff	Week 6	Code-ox · Project Lead	Outlet procedure
5.8	On-site hardware test at a pilot outlet: printers, KDS, terminals, network, offline behaviour	Week 6	Code-ox · Delivery team Tara · IT Tara · Outlet manager	Test record
5.9	**POS & payments ready**	Week 6	Tara · Operations	**M5**

SECTION 7 · PART 2

Delivery Platforms

The list is the same under both options: **HungerStation, Jahez (incl. Noon), Keeta, The Chefz, ToYou, Ninja, Mrsool**. The structure is the same too: Brand › Branch › Platform Store › POS / Kitchen, so a new branch or brand is added by configuration. Decision D-01 (Option A or B) is due at kick-off.

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
6.1	Store inventory: every outlet × brand × platform with store IDs and merchant accounts	By end of Week 1	Tara · Operations Code-ox · Project Lead	Store map

WS 6A Option A: Code-ox Aggregator Hub

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
6.A1	API access requested from each platform on Tara Holding's behalf, per entity merchant account. Requests are already sent; follow-up every week. Confirmed: HungerStation, Keeta, Jahez (incl. Noon). In progress: The Chefz, ToYou, Ninja, Mrsool.	From kick-off · weekly	Code-ox · Engagement Lead Platforms	API status in weekly report
6.A2	Per-platform integration plan: endpoints, order states, menu / stock sync, cancellations and rejections as each API allows	Week 2	Code-ox · Delivery team	Plan shared
6.A3	Hub core in your Odoo: orders into POS and Kitchen Display; menu and price push; sold-out and stock sync; status updates back; failure and retry handling; logs and alerts; multiple branches and store IDs	Weeks 3–5	Code-ox · Delivery team	Core on staging
6.A4	Platform connectors for HungerStation, Jahez (incl. Noon) and Keeta	Weeks 4–6	Code-ox · Delivery team	Test orders end to end
6.A5	Connectors for The Chefz, ToYou, Ninja and Mrsool, each built and tested once its API is issued	As each API arrives	Code-ox · Delivery team Platforms	Test orders end to end
6.A6	Platform-side testing or certification where a platform requires it	Weeks 6–9	Code-ox · Delivery team Platforms	Platform confirmation
6.A7	A platform whose API is not issued in time keeps its own tablet at go-live and is connected when its API arrives, within the agreed scope and price	Reviewed at Go / No-Go	Code-ox · Engagement Lead	Status per platform

WS 6B Option B: UrbanPiper (standard connector, configuration only)

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
6.B1	Joint Odoo / UrbanPiper meeting outcome; UrbanPiper subscription ordered through Odoo; Saudi coverage incl. Keeta confirmed	By end of Week 1	Tara · Owner Odoo UrbanPiper	Subscription active
6.B2	UrbanPiper stores per outlet and brand; platform linking through UrbanPiper's onboarding (timing with UrbanPiper and the platforms)	Weeks 2–5	UrbanPiper Code-ox · Project Lead	Stores linked
6.B3	Connector configuration: menu sync, store hours, payment method per platform, routing to POS and Kitchen Display	Weeks 5–6	Code-ox · Project Lead	Configured
6.B4	Connector demonstrated on staging (HungerStation orders are rejected in the HungerStation app, not in Odoo POS)	Week 6	Code-ox · Project Lead	Demo held

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
6.9	**Platforms connected in test**, subject to platform approvals	Week 6	Tara · Operations	**M6**

SECTION 8 · PART 2

Settlement & Payments

WS 7 Settlement & reconciliation

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
7.1	Payout statements, reports and files collected from each platform	Weeks 2–3	Tara · Finance Code-ox · Project Lead	Samples per platform
7.2	Settlement plan with automation level, following Odoo's official response (decision D-09)	Week 4	Code-ox · Project Lead	Settlement plan
7.3	Clearing account per platform; reconciliation of gross sales, commission, VAT on commission, promotions, refunds, cancellations, adjustments, penalties, delivery charges, net payout	Weeks 5–6	Code-ox · Project Lead	Configured
7.4	Reports by platform, brand and branch; tested in UAT with a real payout statement from each platform	Weeks 6–9	Code-ox · Project Lead Tara · Finance	UAT result

WS 8 Payments

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
8.1	Odoo 19 availability confirmed for Geidea, NearPay and Paymob terminals **before you commit**	Week 2	Code-ox · Delivery team	Written confirmation → D-06 by end of Week 3
8.2	Merchant accounts and API keys (test and live): Paymob, Tabby, Tamara	By end of Week 3	Tara · Finance	Keys shared securely
8.3	Paymob online payments: Mada, Visa / Mastercard, Apple Pay as enabled on your account	Week 4	Code-ox · Delivery team	Test payments
8.4	Tabby and Tamara integration built by Code-ox	Weeks 4–5	Code-ox · Delivery team	Test payments + refunds
8.5	POS terminal integration for the provider(s) chosen in D-06	Weeks 5–6	Code-ox · Delivery team Tara · IT (devices)	Terminal tests at pilot outlet
8.6	Rules: order marked paid only on terminal or gateway confirmation; refunds to the original method where supported; failed payments retried or switched	Week 6	Code-ox · Delivery team	Test cases passed

PAYMENT TESTING

Every payment method is tested in test mode on staging, then with small live transactions at the pilot outlet during UAT and again in the go-live smoke test. Provider fees are paid directly to each provider (proposal, page 9).

SECTION 9 · PART 2

WhatsApp, Loyalty & ZATCA

WS 9 WhatsApp (standard Odoo Enterprise app)

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
9.1	Meta Business verification, dedicated number, Business Manager access	By end of Week 3	Tara · Marketing Meta	Verified account
9.2	WhatsApp connected to Odoo; templates drafted: receipts, order confirmations, customer messages	Week 4	Code-ox · Project Lead	Drafts for approval
9.3	Templates submitted to Meta; kitchen and delivery status messages reviewed with you case by case before anything is built (D-08)	Submit by end of Week 5	Code-ox · Project Lead Tara · Marketing	Meta approval
9.4	Automatic sending where possible; tested in UAT	Week 6	Code-ox · Project Lead	Messages received in test

WS 10 Loyalty, promotions & rewards (MYLK)

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
10.1	Session with management: loyalty and promotion ideas, each assessed as standard, configuration, supported app or custom (last option)	Week 3	Code-ox · Project Lead Tara · Marketing	Ideas assessed
10.2	Programs agreed (D-07)	By end of Week 4	Tara · Marketing	Program list
10.3	Configuration: points and rewards; % and fixed discounts; coupons and promo codes; Buy X Get Y; gift cards and eWallet; POS and eCommerce; validity and conditions; separate programs per brand	Weeks 5–6	Code-ox · Project Lead	Configured
10.4	Demonstration to your team; loyalty and gift-card balances from Foodics as available (gap report 0.8)	Week 6	Code-ox · Project Lead	Demo held

WS 11 ZATCA Phase 2

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
11.1	Company VAT, CR and address; invoice journal per POS; one-tap default customer for walk-in sales	Weeks 3–4	Code-ox · Project Lead	Configured
11.2	Fatoora portal administrator nominated, with access for simulation onboarding	By end of Week 5	Tara · Finance	Access confirmed
11.3	Simulation onboarding and compliance checks for each POS journal on staging	Week 6	Code-ox · Project Lead ZATCA	Compliance passed
11.4	UAT: simplified and standard invoices, credit notes, B2B invoices, rejected-invoice handling	Weeks 7–9	Tara · Finance Code-ox · Delivery team	UAT result
11.5	**Production onboarding** of each POS journal (OTP generated by your Fatoora administrator)	Week 11	Code-ox · Project Lead Tara · Finance	Production certificates

SECTION 10

Foodics Migration & Historical Archive

Migrated: menus, categories, products, modifiers and customers per brand. Archived: full history in open formats. Opening stock from a physical count at cutover; Foodics stays live until 31 December.

FOODICS DATA IS COLLECTED DURING THE UPGRADE

Full extraction runs in Weeks 1–3, in parallel with the Odoo 19 upgrade, so all Foodics data is in hand before the build starts. Later exports add only new transactions.

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
12.1	Foodics console and API access; data inventory; **gap report** on what Foodics can and cannot export (e.g. loyalty or gift-card balances), flagged at the start	Week 1	Code-ox · Project Lead Tara · IT	Gap report
12.2	**Full Foodics data extraction, in parallel with the Odoo 19 upgrade**: master data (menus, categories, products, modifiers, customers) and all history to date: sales and orders, payments, discounts, promotions, refunds, cancellations, inventory history, loyalty / gift-card balances, tax and financial reports, branch and store configuration, in CSV / Excel and PDF.	Weeks 1–3	Code-ox · Project Lead Tara · IT	Foodics data set v1 in your storage
12.3	Field mapping per brand from the extracted data	Weeks 2–3	Code-ox · Project Lead	Mapping sheet
12.4	Data validation and clean-up by your team: menu prices, active items, duplicate customers	Week 3	Tara · Operations Tara · Marketing	Validated files
12.5	Trial load 1 into the build environment; counts and samples checked	Week 4	Code-ox · Project Lead	Load report
12.6	Trial load 2 into the UAT environment	Week 7	Code-ox · Project Lead	Load report
12.7	**Top-up export**: Foodics transactions since the first extraction added to the archive	Week 9	Code-ox · Project Lead	Archive updated
12.8	Rehearsal load using the cutover method, with timings recorded	Week 10	Code-ox · Project Lead	Rehearsal report
12.9	Menu freeze in Foodics: any change after this date is applied in both systems by Code-ox	From Week 11	Tara · Operations	Freeze notice
12.10	**Final export** after the last Foodics transaction	Night of Thu 31 Dec	Code-ox · Project Lead	Final export
12.11	Opening stock from physical count at every outlet, Main Warehouse and Central Kitchen, posted before the first sale	Night 31 Dec – before opening 1 Jan	Tara · Inventory Tara · Outlet managers Code-ox · Project Lead	Count sheets + inventory adjustment
12.12	Final archive with complete **index and data dictionary**: each dataset, its period and what it contains	Week 12	Code-ox · Project Lead	Archive handed over

Data objects

OBJECT	SOURCE	METHOD	VALIDATED BY
Menus, categories, products, modifiers, combos	Foodics export	Import templates, per brand	Operations
Customers (incl. loyalty data where exported)	Foodics export	Import with de-duplication	Marketing
Ingredients, vendor lines, pack sizes, barcodes	Your procurement data	Templates 3.2	Procurement
Recipes / BOMs and outlet recipe kits	Kitchen team	Templates 4.1	Kitchen Lead
Users and roles (all staff incl. cashiers)	HR / Operations	User list by end of Week 5	Owner
Opening stock	Physical count at cutover	Count sheets → inventory adjustment	Inventory + outlet managers
Sales history, reports, balances	Foodics	Archive only (not migrated as transactions)	Finance

SECTION 11

Testing, UAT & Training

Tested at every level, from build to full rehearsal, before your users accept anything, and every role trained before it uses the system.

LEVEL	WHEN	WHO	EXIT CRITERIA
Build testing	Continuous, Weeks 3–6	Code-ox delivery team	Each item tested before the Thursday demo
Thursday demos	Weekly from Week 4	Your key users	Feedback logged in the tracker
System integration test	Weeks 6–7	Code-ox delivery team	All end-to-end flows pass incl. platforms, payments, ZATCA simulation; internal test report (M7)
UAT cycle 1	Week 8	Your key users, guided by Code-ox	All scenarios executed; defects logged in the tracker
UAT cycle 2 + day-in-the-life	Week 9	Key users with kitchen and one outlet team	Re-tests passed; a full trading day simulated end to end
Cutover rehearsal	Week 10	Code-ox, your IT and inventory leads	Deployment and data load timed and documented
Regression & sign-off	Week 10	Code-ox delivery team, project owner	No open Critical or High issues → UAT acceptance (M9)

UAT scenarios (scripts issued Week 6)

- Purchase → receipt with pack conversion → bill → payment
- Central kitchen day: plan → MOs → consumption → transfers
- Expiry, leftovers disposal and waste with reasons
- Minimum stock replenishment to outlets
- Dine-in and takeaway with modifiers, combos and floor plan
- Delivery order per platform → KDS → status back; sold-out sync
- Card, Mada, Apple Pay, Tabby, Tamara; split payment; refund; failed payment
- Offline POS; session closing and cash control
- ZATCA simplified and standard invoices, credit notes
- B2B order, delivery and invoice
- Loyalty earn and redeem; coupon; gift card; eWallet
- WhatsApp receipt and order confirmation
- Platform payout reconciliation
- P&L by brand, branch and channel; stock value by outlet
- Access rules for each role

Training plan

- **Key users (train-the-trainer)**: Week 7, before UAT starts
- **Finance & accounting**: Week 9 (2 sessions)
- **Procurement & warehouse**: Week 9
- **Central kitchen**: Week 9, plus on the floor during the day-in-the-life test
- **Marketing** (loyalty, WhatsApp): Week 9
- **Outlet managers & cashiers**: Week 10, by outlet group: POS, KDS, payments, delivery orders, ZATCA, offline mode, closing
- **IT / in-house developer**: Week 10, covering repository, modules, deployment and integration monitoring; full handover in January
- **Refresher & go-live briefing**: Week 11
- Materials: role guides and quick-reference cards by end of Week 7; attendance lists by end of Week 7; attendance recorded per session

ACCEPTANCE CRITERIA (PROPOSAL, PAGE 10)

Upgrade: documented before / after validation signed off by finance for each of the six companies, and all agreed flows pass on staging, before production is touched. **UAT**: agreed scenarios pass on staging with no open Critical or High issues. **Go-live**: production live on Odoo 19, POS selling, ZATCA invoices accepted and orders flowing from the connected platforms, with any remaining Normal issues listed and scheduled.

SECTION 12

Cutover & Go-Live

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
15.1	Cutover runbook and rollback plan shared	Week 9	Code-ox · Engagement Lead	Runbook
15.2	Cutover rehearsal on a fresh copy of production; timings recorded; runbook updated	Week 10	Code-ox · Delivery team Tara · IT	Rehearsal report
15.3	UAT acceptance; code freeze	Week 10	Tara · Owner	**M9**
15.4	Stock count teams, count sheets and outlet go-live contacts confirmed; Foodics end date decided (D-12)	By end of Week 10	Tara · Inventory Tara · Operations	Count plan
15.5	Urban Eats deployed to production: modules from your repository, configuration, master data, users and access (no transactions yet)	Week 11	Code-ox · Delivery team Code-ox · Project Lead	Deployment checklist
15.6	**Go / No-Go meeting** against the checklist below	Week 11	Steering committee	**M10**
15.7	ZATCA production onboarding per POS journal; refresher training	Week 11	Code-ox · Project Lead Tara · Finance	Certificates
15.8	Final checks at every outlet: devices, printers, KDS, terminals, network, platform store mapping	Week 11	Code-ox · Delivery team Tara · Outlet managers	Outlet checklist

Cutover sequence: 31 December → 1 January

STEP	WHAT HAPPENS	OWNER
1	Cutover starts as per the runbook agreed with your project owner. Trading continues on Foodics as normal.	Code-ox · Engagement Lead
2	Central kitchen finishes the day's production; Main Warehouse and Central Kitchen counted once movement stops	Tara · Inventory
3	At each outlet's closing: last Foodics order; shift closed; end-of-day report saved	Tara · Outlet manager
4	Delivery platform stores switched from tablets to Odoo (Option A hub or Option B UrbanPiper)	Code-ox · Delivery team
5	Physical stock count at the outlet; counts entered as opening stock and checked	Tara · Outlet team; Code-ox · Project Lead
6	Final Foodics export after the last outlet closes (12.10)	Code-ox · Project Lead
7	Before opening, smoke test per outlet: open session, test sale on each payment method, refund, KDS ticket, ZATCA invoice accepted, platform test order. Test documents reversed per procedure.	Code-ox · Delivery team; Tara · Outlet manager
8	**Go confirmation for each outlet** from outlet manager and Code-ox	Both
9	**First live sales on Odoo** on 1 January: close monitoring of orders, payments, ZATCA submissions and platform sync	Code-ox · all; Tara · Owner
10	End of day 1: review of issues, fixes and plan for day 2	Both

Go / No-Go checklist (Week 11)

- UAT accepted; no open Critical or High issues
- Production deployment verified (15.5)
- Hardware and terminals tested at every outlet
- Platform status known for each platform; any not ready stays on its tablet
- All roles trained; attendance recorded
- Count teams and Fatoora administrator confirmed
- Rollback plan and support rota published

Rollback

- A Critical blocker found before opening on 1 Jan: the steering committee decides by an agreed time. The affected outlet(s) trade one more day on Foodics while it is fixed, which is why the Foodics account stays active until the archive is verified (D-12).
- The existing six companies are not affected: they have run on Odoo 19 since November (D-03).
- If D-03 is the 31 Dec upgrade instead, production is restored from the pre-upgrade backup. That restore is tested at the rehearsal.

SECTION 13

Go-Live Support, Handover & SLA

After UAT the project goes live. From go-live, support follows the SLA: your team raises an issue through the support channel and Code-ox resolves it within the times below. No scheduled meetings are needed.

ID	TASK	WHEN	OWNER	OUTPUT / EVIDENCE
16.1	From go-live, issues raised by your team through the support channel (phone, WhatsApp or the tracker) are handled under the SLA below, including platform sync, payments and ZATCA	From 1 Jan 2027	Code-ox · Engagement Lead Tara · Owner	Issue log
16.2	Final Foodics archive with index and data dictionary (12.12)	Week 12	Code-ox · Project Lead	Archive handed over
16.3	Go-live report: what went live, open items, platform status, next steps	Week 12	Code-ox · Engagement Lead	Report
16.4	Go-live acceptance feedback within 5 business days (proposal terms)	By end of Week 12	Tara · Owner	Acceptance
16.5	**Handover pack**: complete source in your repository, deployment instructions, migration scripts, technical, integration / API and configuration documentation, walked through with your developer	Week 13	Code-ox · Delivery team Tara · IT	Signed handover · **M13**
16.6	Six months of support under the SLA	1 Jan – 30 Jun 2027	Code-ox · Engagement Lead	**M14**

Support SLA (from the proposal, page 10)

PRIORITY	RESPONSE	FIX / WORKAROUND
Critical: POS, payment, platform, order sync or ZATCA down	1 hour, 7 days a week, by phone or WhatsApp	4 hours, including Friday and Saturday
High	4 hours	1 business day
Normal	1 business day	3 business days

AFTER THE SIX MONTHS

Support continues under an AMC at your option, at the rate on page 7 of the proposal. New branches, brands, platforms and new requirements are quoted in writing before work starts, at the indicative rates in the proposal.

SECTION 14

Week-by-Week Calendar

WEEK	CODE-OX	TARA HOLDING	MEETINGS & MILESTONES
Week 1 15–22 Oct	Kick-off; tracker set-up; discovery & design in parallel with the upgrade; backup & staging upgrade; Studio and module migration; pre-validation; upgrade assessment & module register; architecture document; migration plan; Foodics gap report; **Foodics data extraction starts**	Signed agreement; owner and key users named; D-01; Odoo.sh and Foodics access; requirements input per area; company validators; outlet & store list; module licences; repository	Kick-off 15 Oct · **M0**
Week 2 25–29 Oct	Support department validation; fixes; coding scheme; integration plan; hardware spec; terminal availability; Foodics data extraction and field mapping	Validate on staging; approve architecture; D-02 to D-05; **finance sign-off per company**; Urban Eats CR / VAT / accounts data	**M1 · M2**
Week 3 1–5 Nov	Company, accounts, taxes, journals, analytic plans; warehouses, routes, UoM; upgrade runbook; loyalty session; **Foodics extraction complete**; **production upgrade at the end of the week**	Supplier data and payment keys; data clean-up; menus and recipes; Meta verification; D-06, D-10; finance checks after upgrade	**M3**
Week 4 8–12 Nov	Materials & vendor lines; shared operations; access; BOMs; POS configurations; menus; Paymob; Tabby / Tamara; hub core or UrbanPiper stores; WhatsApp drafts; ZATCA journals; trial load 1	Minimum stock levels; D-07, D-08, D-09	First Thursday demo · **M4**
Week 5 15–19 Nov	Daily production plan; kitchen screen; stock rules; KDS; receipts; menus complete; terminals; platform connectors; settlement; loyalty; waste & costing; WhatsApp templates submitted	Fatoora access; user list and roles	Thursday demo
Week 6 22–26 Nov	Expiry & leftovers; recipe kits; offline & cash procedure; payment rules; ZATCA simulation; WhatsApp automations; platform tests; system test; pilot-outlet hardware test; UAT scripts	Hardware & terminals on site; Odoo subscription updated; UAT testers named	**M5 · M6**
Week 7 29 Nov–3 Dec	Internal test report; trial load 2; UAT environment built from production copy; training materials; **UAT environment live on 1 Dec**; key-user training	Agree UAT scripts; key users trained; attendance lists	**M7 · M8** (1 Dec)
Week 8 6–10 Dec	UAT cycle 1 support; fixes; platform testing	Execute scenarios; log defects	Steering · Thursday review
Week 9 13–17 Dec	UAT cycle 2 + day-in-the-life; Foodics top-up export; training (finance, procurement, kitchen, marketing); cutover runbook	Re-test; staff the day-in-the-life; attend training	Steering · Thursday review
Week 10 20–24 Dec	Cutover rehearsal; regression; outlet staff training; IT session; code freeze	**UAT sign-off**; count teams; D-12	**M9**
Week 11 27–31 Dec	Production deployment; ZATCA production onboarding; outlet checks; **cutover on the night of 31 Dec**	Menu freeze; Go / No-Go; Fatoora OTPs; refresher training; stock count	**M10 · M11**
1 Jan 2027	**Go-live**: monitoring of orders, payments, ZATCA and platform sync	Outlets open on Odoo; no new transactions on Foodics	**M12**
Week 12 3–7 Jan	Support under SLA; final Foodics archive; go-live report	Raise issues through the support channel; go-live feedback	SLA support
Week 13 10–14 Jan	Support under SLA; **handover pack**	Technical handover with your developer	**M13**

EVERY WEEK

Until UAT sign-off: steering on Sunday · Thursday demo / review (from Week 4) · written status report on Thursday · live tracker in Odoo Project. From go-live: support under the SLA to 30 Jun 2027; meetings only when a specific matter needs one.

SECTION 15

Your Inputs & Decisions

Inputs from Tara Holding

ID	INPUT	DUE	OWNER
I-01	Signed agreement and advance payment	Thu 15 Oct	Sponsor
I-02	Project owner and key users named per area	Thu 15 Oct	Sponsor
I-03	**Odoo.sh access**; staging confirmed; Code-ox registered as partner on the subscription **(critical path)**	Week 1	IT
I-04	Foodics console and API access	Week 1	IT
I-05	Platform merchant accounts / authorisation per entity for API requests (Option A) or UrbanPiper order (Option B)	Week 1	Operations
I-06	Six companies with a finance validator each; input to the validation checklist	Week 1	Finance
I-07	Licences and source for third-party modules as listed in the register	Week 1	IT
I-08	Outlet list: brands, address, hours, devices, platform store IDs	Week 1	Operations
I-09	Repository for custom code in Tara Holding's name, with Code-ox access	Week 1	IT
I-10	Urban Eats CR, VAT number, address, chart of accounts preferences, bank accounts	Week 2	Finance
I-11	Suppliers, vendor price lists, pack sizes, barcodes	Week 3	Procurement
I-12	Paymob, Tabby, Tamara merchant accounts and API keys	Week 3	Finance
I-13	Validated menus per brand and recipes / BOMs	Week 3	Operations, Kitchen
I-14	Meta Business verification, WhatsApp number, Business Manager access	Week 3	Marketing
I-15	Initial minimum stock levels per location	Week 4	Inventory
I-16	Fatoora portal administrator and access	Week 5	Finance
I-17	User list with roles (all staff incl. cashiers)	Week 5	Operations
I-18	POS hardware, printers, KDS screens, card terminals and network on site	Week 6	IT
I-19	Odoo subscription updated for the users and apps needed (count from Code-ox by end of Week 4)	Week 6	IT
I-20	Named UAT testers and calendar	Week 6	Owner
I-21	Training attendance lists per session	Week 7	Operations
I-22	Stock count teams and outlet go-live contacts	Week 10	Inventory
I-23	Fatoora administrator available for OTPs; outlet managers on cutover night	Week 11	Finance, Operations

Decisions

ID	DECISION	DUE
D-01	Part 2 delivery-platform layer: Option A (Code-ox Aggregator Hub) or Option B (UrbanPiper)	Thu 15 Oct
D-02	POS revenue tagging: Option 1 fully standard or Option 2 small isolated module	Week 2
D-03	Production upgrade window: weekend at the end of Week 3 (as planned) or cutover night 31 Dec	Week 2
D-04	Treatment of each third-party module, incl. the replacement MCP app	Week 2
D-05	Product types and coding scheme	Week 2
D-06	POS terminal provider(s): Geidea, NearPay, Paymob	Week 3
D-07	Loyalty and promotion programs for MYLK	Week 4
D-08	Kitchen and delivery status WhatsApp messages: which, if any, to automate	Week 4
D-09	Settlement automation level (after Odoo's official response)	Week 4
D-10	Labour and overhead in production cost (optional)	Week 3
D-11	Training language(s) and session format	Week 6
D-12	Foodics account end date (kept active until the final archive is verified)	Week 10
D-13	Go / No-Go	Week 11

SECTION 16

Deliverables

Every document Code-ox delivers, with its due date. Each one is shared for review in the tracker; documents that need your approval are marked in the related task.

ID	DELIVERABLE	DUE
DL-01	Execution plan (this document) and live tracker in Odoo Project	Week 1
DL-02	Kick-off pack: team, contacts, cadence, severity definitions, templates	Week 1
DL-03	Written upgrade assessment and module-by-module register	Week 1
DL-04	Urban Eats architecture document	Week 1
DL-05	Upgrade validation report per company (before / after)	Week 1 → sign-off Week 2
DL-06	Data migration plan, import templates, Foodics gap report	Week 1
DL-07	Per-platform integration plan (A) or UrbanPiper configuration plan (B)	Week 2
DL-08	POS hardware and network specification	Week 2
DL-09	Production upgrade runbook	Week 3
DL-10	Settlement plan	Week 4
DL-11	Written justification for each custom item, before it is built	As raised
DL-12	UAT scenarios, scripts and calendar	Week 6
DL-13	Internal test report	Week 7
DL-14	Training materials: role guides and quick-reference cards	Week 7
DL-15	Cutover runbook and rollback plan	Week 9
DL-16	UAT report and acceptance form	Week 10
DL-17	Go / No-Go checklist	Week 11
DL-18	Foodics data set v1 (Week 3); final archive with index and data dictionary	Week 12
DL-19	Go-live report	Week 12
DL-20	Handover pack: source, deployment instructions, migration scripts, technical / integration / configuration documentation	Week 13
DL-21	Weekly status report	Every Thursday

SECTION 17

Risks & Assumptions

Reviewed every Sunday at steering. New risks are added to the tracker with an owner and a mitigation.

ID	RISK	MITIGATION	OWNER
R1	Platform APIs issued late (Option A)	Requested on Tara's behalf already; weekly follow-up; connectors built in order of arrival; a late platform keeps its tablet and is connected when ready, within scope	Code-ox
R2	UrbanPiper onboarding or coverage timing (Option B)	Coverage confirmed in the joint meeting; stores started in Week 2; uncovered platform stays on its tablet	Tara, UrbanPiper
R3	A third-party module has no Odoo 19 version	Register by end of Week 1; migrate or replace; nothing removed without approval	Code-ox
R4	Validation time for six companies in one week	Code-ox prepares before / after reports so finance reviews differences only; checklist agreed in Week 1	Both
R5	Recipe or menu data incomplete	Templates in Week 1; Code-ox support; top-selling items first	Tara
R6	Foodics cannot export some data (e.g. balances)	Gap report in Week 1, so the approach is agreed early	Code-ox
R7	Hardware, terminals or network not ready	Spec Week 2; devices on site Week 6; pilot-outlet test	Tara
R8	Key users unavailable in December	Named testers and calendar by end of Week 6	Tara
R9	ZATCA onboarding issue near go-live	Simulation passed in Week 6; OTP process rehearsed; administrator on standby	Both
R10	Late scope changes	Change control; code freeze from Week 10	Both

ASSUMPTIONS

Tara Holding stays on Odoo.sh with one staging branch available · Urban Eats goes live at all outlets on 1 Jan 2027 · Scope, prices and terms are as in Financial Proposal CX-TARA-2026-02 Rev. 1; this plan does not change them · Third-party and platform fees are as listed on page 9 of the proposal.

ACCEPTANCE

Plan Acceptance

By signing, both parties agree this plan as the baseline for delivery. Changes to dates, owners or tasks are agreed at steering and recorded in the tracker. Changes to scope, cost or the committed dates of 1 December 2026 and 1 January 2027 follow the change control in Section 2.

FOR & ON BEHALF OF CODE-OX TECHNOLOGIES

AUTHORISED SIGNATORY

NAME & TITLE

DATE

FOR & ON BEHALF OF TARA HOLDING

AUTHORISED SIGNATORY

NAME & TITLE

DATE

CONTACT

Raghib Ali Rafeeque, Code-ox Technologies · raghib@code-ox.com · +966 561 765 707 · 3239 Al Zubair Bin Al Awwam St, Al Rawabi Dist., Riyadh 14215, KSA
