Tara Holding *with* CODE OX

Project kick-off, Thursday 15 October 2026

Odoo 19 Upgrade & Urban Eats Implementation

15 Oct 2026
Work starts today

1 Jan 2027
Every outlet live on Odoo POS

Prepared by Code-ox Technologies, Odoo Silver Partner. Purchase Order TH P00008.

Today’s agenda

01 Why we are here today

02 What we are delivering

03 The road to 1 January

04 Phases, timeline and milestones

05 The first two weeks

06 Our team and how to reach us

07 How we work together

08 What we need from Tara Holding

09 Decisions, risks and go-live

10 Next steps

01

Why we are here today

The goal: Tara Holding upgraded to Odoo 19 and Urban Eats running on Odoo from 1 January 2027, on a platform your own team can run with confidence.

Start the project

Officially begin the work, with the agreement signed and the advance invoiced.

Align on the plan

Walk through the phases, dates and milestones so both teams share one picture.

Confirm who does what

Name the people, owners and escalation path on both sides.

Agree the first inputs

Access, information and decisions Tara Holding provides in the first two weeks.

02

What we are delivering

Part 1

Odoo 18 to 19 upgrade

All six companies move to Odoo 19 in the same database, with history intact.

- ✓ Assessment and module-by-module register
- ✓ Upgrade validated on staging first
- ✓ Finance sign-off for each company
- ✓ Production upgraded outside working hours

Part 2

Urban Eats / MYLK on Odoo 19

- Urban Eats as one company, with Brand, Branch and Channel reporting
- Main Warehouse, Central Kitchen and outlet stock
- Products, recipes and central kitchen production
- Restaurant POS and Kitchen Display per branch and brand
- Delivery platforms through UrbanPiper (Option B)
- Settlement and platform reconciliation
- Paymob, Tabby, Tamara and POS terminals
- ZATCA Phase 2
- WhatsApp, loyalty and promotions
- Foodics exit with a full data archive

Included after go-live: two weeks of hypercare, the Foodics archive, source and documentation handover, and support until 30 June 2027.

03

The road to 1 January

15 Oct
Kick-off
Today

29 Oct
SRS signed
Upgrade signed off on staging

6–7 Nov
Production upgrade
Six companies on Odoo 19

1 Dec
UAT environment
Committed date

24 Dec
UAT accepted
Code freeze starts

1 Jan
Go-live
Committed date

30 Jun
Support ends
Six months under SLA

The two committed dates hold if access, inputs and UAT feedback arrive on time and the delivery platforms approve their connections.

04

Five phases

1

Mobilise, design & upgrade

15 Oct – 12 Nov

Agreement and access, requirement workshops, staging upgrade, finance sign-off and the production upgrade.

2

Build Urban Eats

1–30 Nov

Foundation, central kitchen, POS and Kitchen Display, platforms, payments, ZATCA, data loads and internal testing.

3

UAT & training

1–24 Dec

Two UAT cycles, role-based training, cutover rehearsal and UAT acceptance.

4

Cutover & go-live

27 Dec – 1 Jan

Production deployment, Go / No-Go, cutover night on 31 December and go-live on 1 January.

5

Hypercare & SLA support


1 Jan – 30 Jun

Weekend cover, two weeks of hypercare, handover on 14 January, then support to 30 June 2027.

05

Timeline

Seventeen workstreams across thirteen weeks, 15 October 2026 to 14 January 2027.

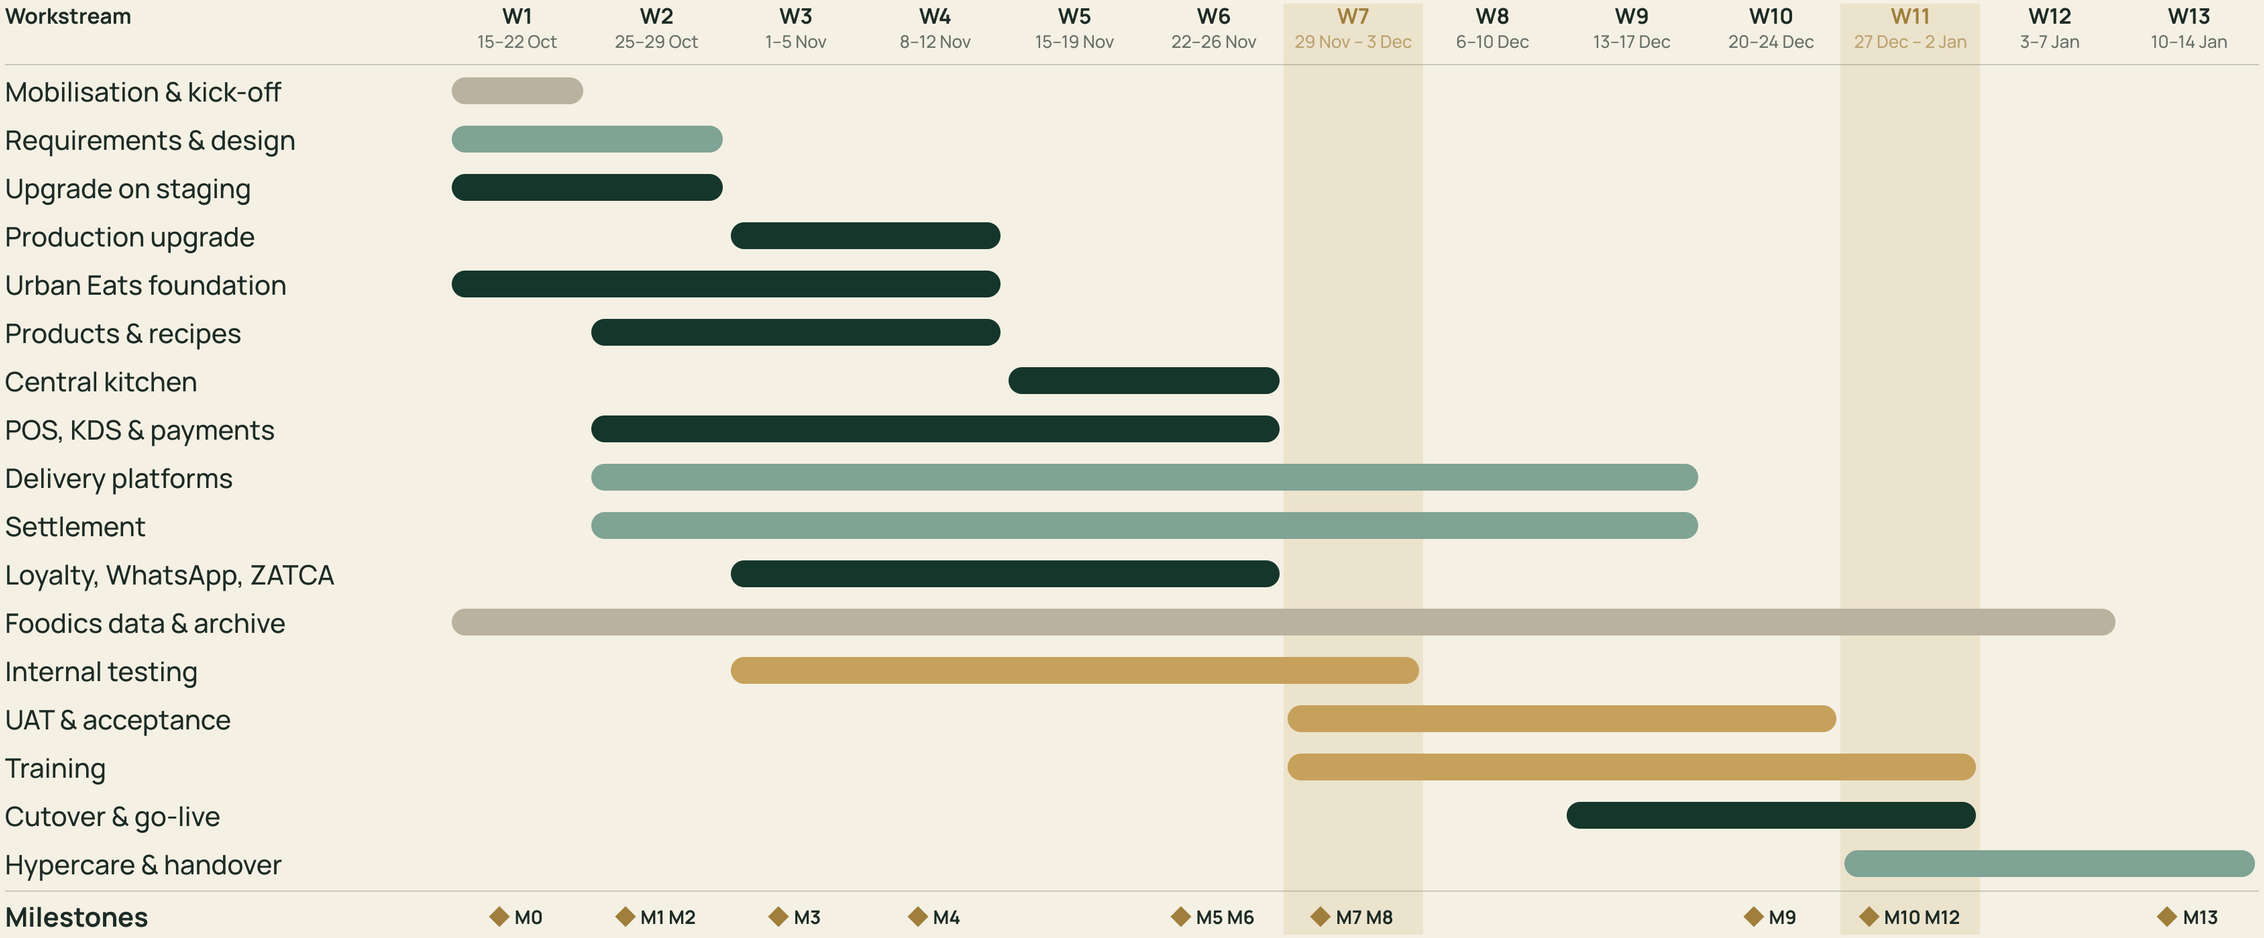

06

Fifteen milestones

M0	Thu 15 Oct 2026	Agreement signed & kick-off held
M1	Thu 29 Oct	SRS signed; assessment, module register & architecture approved
M2	Thu 29 Oct	Upgrade signed off on staging (six companies)
M3	Weekend 6–7 Nov	Production upgraded to Odoo 19
M4	Thu 12 Nov	Urban Eats foundation configured
M5	Thu 26 Nov	Central kitchen, POS & payments ready
M6	Thu 26 Nov	Delivery platforms connected in test
M7	Mon 30 Nov	Internal testing complete; data loaded
M8	Tue 1 Dec 2026	**Production-ready UAT environment live**
M9	Thu 24 Dec	UAT acceptance
M10	Tue 29 Dec	Go / No-Go
M11	Thu 31 Dec (night)	Cutover complete: Foodics closed for transactions
M12	Fri 1 Jan 2027	**Production go-live: all outlets on Odoo POS**
M13	Thu 14 Jan	Source & documentation handed over
M14	Wed 30 Jun 2027	Six-month support ends

Gold marks the two committed dates.

07

The first two weeks


15 to 29 October: access, staging upgrade, workshops and the signed SRS.

When	Task	Owner
Thu 15 Oct	Agreement signed, advance invoiced, kick-off held	Both teams
Thu 15 Oct	Odoo.sh, staging and GitHub access	Tara IT
Thu 15 Oct	Full production backup; staging branch created	Code-ox
15–18 Oct	Staging copy upgraded to Odoo 19	Code-ox with Odoo
15–22 Oct	Upgrade assessment and module register	Code-ox
15–22 Oct	Foodics console and API access; data inventory	Tara IT, Code-ox
18–21 Oct	Studio customisations and third-party modules checked	Code-ox
18–26 Oct	Requirement workshops, two hours each	Both teams
by 22 Oct	Joint Odoo and UrbanPiper meeting on platform coverage	Tara Holding
21–27 Oct	Validation of every company and department on staging	Tara Finance, departments
25–27 Oct	Software Requirements Specification prepared	Code-ox
Thu 29 Oct	SRS signed; finance sign-off for each company	Tara Holding

08

Our team

One point of contact for Tara Holding, a project manager with three developers, and founder-level oversight.

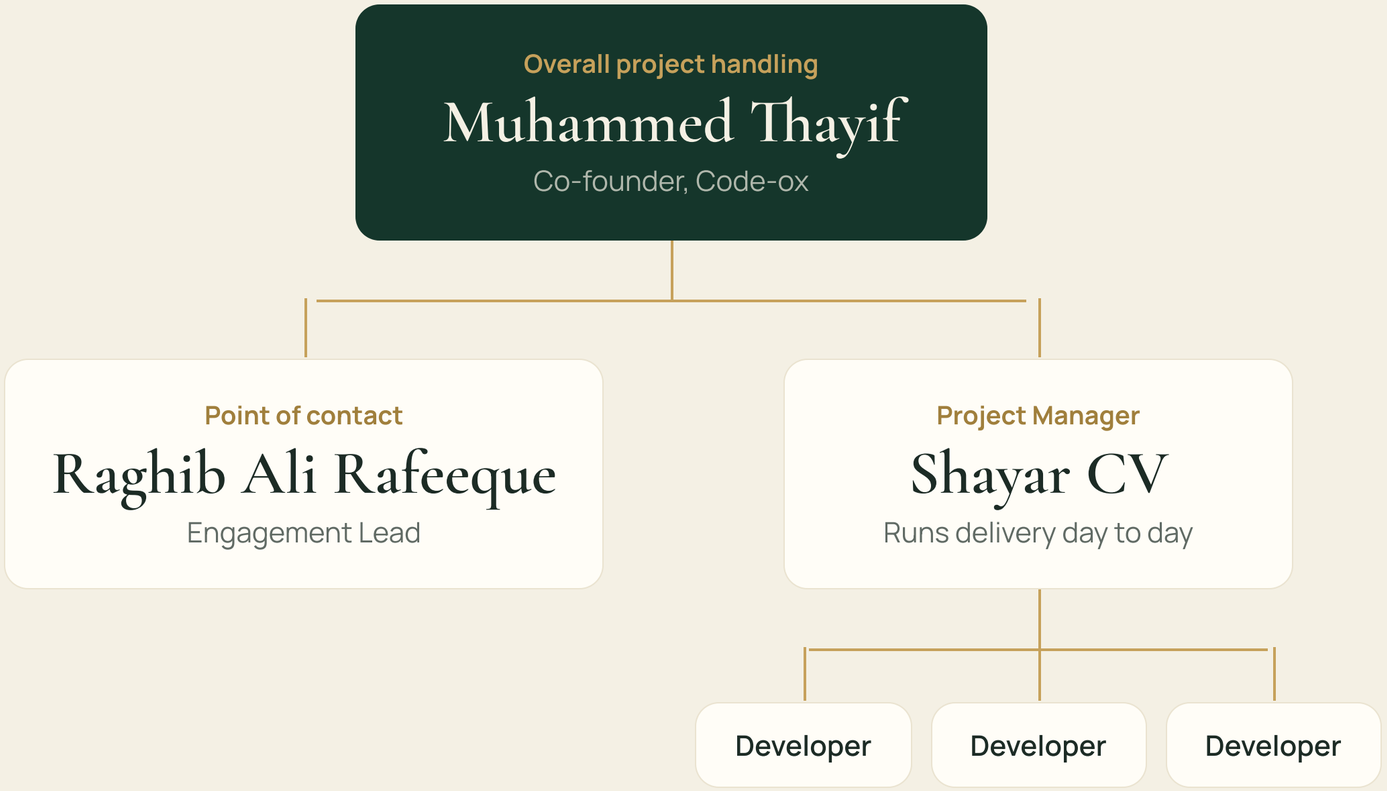

Tara Holding

Project Owner

Eng. AbdulRahman Al-Nouman

Executive Sponsor

Named at kick-off

Area leads

Finance (one validator per company), Procurement and Inventory, Central Kitchen, Operations and outlet managers, Marketing, IT

09

How to reach us

Initial contact

Raghib Ali Rafeeque

Engagement Lead

raghib@code-ox.com
+966 561 765 707

Escalation 1

Shabeeb K

Head of Operations

shabeeb.k@code-ox.com
+966 535 716 437

Escalation 2

Muhammed Thayif

Co-founder

Final escalation

Start with Raghib for anything at all. If something needs more weight, it moves up one step at a time.

10

How we work together

Status report

Every Thursday

Per workstream: on track, at risk or late; done, next, risks, Tara actions due

Steering review

29 Oct, 12 Nov, 26 Nov, 10 Dec, 24 Dec

Milestones, risks, decisions, change requests

Live tracker

Always

Code-ox Odoo Project: tasks, dates, dependencies, Gantt; Helpdesk for UAT defects and support tickets

Requirements and changes

SRS signed 29 October

The signed SRS is the agreed scope. Every change is assessed for scope, cost and dates, approved in writing and recorded as a new SRS revision. Code freeze starts on 24 December.

11

What we need first

Inputs due by 29 October. There are 25 in total, all listed in the Project Plan; a late input moves the tasks that depend on it.

Due	Input from Tara Holding	Owner
Thu 15 Oct	Signed agreement and advance payment	Sponsor
Thu 15 Oct	Executive sponsor, project owner and key users named per area	Sponsor
Thu 15 Oct	Odoo.sh, staging and GitHub access for Code-ox	IT
Thu 15 Oct	Licences and source of third-party modules	IT
15–22 Oct	Foodics items F1–F9	IT, Operations
Thu 22 Oct	Requirement questionnaires answered per area	All leads
Thu 22 Oct	UrbanPiper order and platform merchant accounts; payout samples	Operations
Thu 22 Oct	Finance validator per company; validation checklist input	Finance
Thu 22 Oct	Outlet list: brand, address, hours, devices, platform store IDs	Operations
Thu 22 Oct	Repository for custom code in Tara’s name	IT
Thu 29 Oct	Urban Eats CR, VAT, address, accounts, banks	Finance
Thu 29 Oct	SRS reviewed and signed by the Project Owner	Owner

12

Decisions calendar

Fifteen decisions, each due before the work that depends on it.

Thu 15 Oct

- ✓ **D-01 Delivery layer confirmed: Option B, UrbanPiper**

Thu 29 Oct

- **D-02** POS revenue tagging: Option 1 standard or Option 2 module
- **D-03** Production upgrade window: 6–7 Nov or 31 Dec
- **D-04** Treatment of each third-party module, incl. MCP replacement
- **D-05** Product categories, naming and coding
- **D-15** Go-live on Fri 1 Jan confirmed, with outlet and support cover named for Fri 1–Sat 2 Jan

Thu 5 Nov

- **D-06** POS terminal provider: Geidea, NearPay, Paymob
- **D-10** Labour and overhead in production cost
- **D-14** Apple Pay route on the website

Thu 12 Nov

- **D-07** Loyalty and promotion programs
- **D-08** Kitchen / delivery status messages on WhatsApp
- **D-09** Settlement automation level

Thu 26 Nov

- **D-11** Training languages and format

Thu 24 Dec

- **D-12** Foodics end date

Tue 29 Dec

- **D-13** Go / No-Go

13

Risks we are watching

Reviewed every week, so nothing surprises either team.

Delivery platform coverage

Odoo's UrbanPiper list does not include ToYou or The Chefz today. Coverage is confirmed in the joint meeting by 22 October; any platform not covered stays on its tablet or gets a direct connector.

Tara Holding and UrbanPiper

Six companies validated in one week

Before-and-after reports are prepared in advance, so finance reviews only the differences.

Both teams

Recipes rebuilt from the start

Foodics holds no recipes. Templates arrive on day one, recipe workshops run in weeks two and three, top sellers first.

Tara Holding

Data Foodics cannot export

A gap report by 22 October, so the approach for anything missing is agreed early.

Code-ox

Devices or network late

Specification on 29 October, devices on site by 19 November, pilot test from 24 to 26 November.

Tara Holding

Late scope changes

Every change goes through change control against the signed SRS. Code freeze starts on 24 December.

Both teams

14

Go-live and support

1
29 Dec
Go / No-Go
Checklist signed by both sides

2
31 Dec
Cutover night
Final Foodics export and stock count

3
1 Jan
Go-live
Every outlet on Odoo POS

4
1–2 Jan
Weekend cover
Code-ox team on call

5
3–14 Jan
Hypercare
Two weeks of close support

6
14 Jan
Handover
Source code and documents

Critical
Response in 1 hour, 7 days a week
Fix in 4 hours

High
Response in 4 hours
Fix in 1 business day

Normal
Response in 1 business day
Fix in 3 business days

From 1 January all outlets use Odoo POS only. Foodics stays read-only until the archive is verified. Support runs until 30 June 2027.

15

Next steps

01	Today	Agreement signed and kick-off held	Both teams
02	Today	Odoo.sh, staging and GitHub access granted	Tara IT
03	Today	Executive sponsor, project owner and key users named	Tara Holding
04	15–18 Oct	Backup and staging upgrade to Odoo 19	Code-ox
05	From 18 Oct	Requirement workshops begin	Both teams
06	By 22 Oct	Questionnaires, Foodics items, outlet list and merchant accounts	Tara Holding
07	29 Oct	SRS signed; upgrade signed off on staging	Tara Holding

Thank you

Let’s begin.

Questions, now or at any point: Raghib is your first call.

Raghib Ali Rafeeque

Engagement Lead
raghib@code-ox.com
+966 561 765 707

Shabeeb K

Head of Operations
shabeeb.k@code-ox.com
+966 535 716 437
