EXPECTED PROJECT PLAN · 12 OCTOBER 2026

From Kick-off on 15 October to Go-live on 1 January

The Odoo 19 upgrade for six companies and Urban Eats on Odoo POS, planned task by task. Dates are expected dates from Execution Plan v1.2 of 12 October 2026. Handover follows on 14 January, then support to 30 June 2027.

KICK-OFF	UPGRADE SIGN-OFF	UAT ENVIRONMENT	GO-LIVE	SUPPORT
15 Oct	29 Oct	1 Dec	1 Jan	30 Jun
Thu · 2026	six companies	Tue · committed	Fri · all outlets on Odoo POS	2027 · six months

FIVE PHASES

PHASE 1	PHASE 2	PHASE 3	PHASE 4	PHASE 5
Mobilise, design & upgrade	**Build Urban Eats**	**UAT & training**	**Cutover & go-live**	**Hypercare & SLA support**
15 Oct–8 Nov	1–30 Nov	1–24 Dec	27 Dec–1 Jan	1 Jan–30 Jun

Standard Odoo first
Standard, then configuration, Studio, a supported module, and custom development last. Each custom item is justified in writing and approved before it is built.

Staging first, production last
Every department validates on staging, and finance signs off each company before production is touched.

Dated and linked
Every task has a start, an end, an owner and the task or input it depends on, tracked live in Odoo Project.

Scope unchanged
Scope, prices and terms are as in proposal CX-TARA-2026-02 Rev. 1. This plan does not change them.

DOCUMENT	BASED ON	COMPANION TO	DATE
Expected Project Plan	Execution Plan v1.2	CX-TARA-2026-02 Rev. 1	12 October 2026

OVERVIEW

The Plan at a Glance

Work starts on Thursday 15 October 2026. The UAT environment opens on Tuesday 1 December and every outlet goes live on Odoo POS on Friday 1 January 2027, with six months of support after that.

Part 1: Odoo 18 to 19 upgrade

- All six existing companies move to **Odoo 19 in the same database**, with history intact.
- Everything is validated on staging first, and **finance signs off each company** before production is touched.

Part 2: Urban Eats on Odoo 19

- Structure and finance, central kitchen, **POS and Kitchen Display**, delivery platforms, payments, ZATCA, WhatsApp, loyalty, and the **exit from Foodics**.
- Scope, prices and terms are as in proposal **CX-TARA-2026-02 Rev. 1**.

Milestones


Fifteen milestones from kick-off to the end of support. The two committed dates are the UAT environment on 1 December and go-live on 1 January.

#	MILESTONE	DATE	NEEDS	CONFIRMED BY	EVIDENCE
M0	**Agreement signed & kick-off held**	Thu 15 Oct 2026	I-01, I-02	Both parties	Signed agreement; kick-off minutes
M1	**Assessment, module register & architecture approved**	Thu 29 Oct	0.6, 0.7	Tara Owner	Approved documents
M2	**Upgrade signed off on staging (six companies)**	Thu 29 Oct	1.5–1.8	Tara Finance, per company	Signed before / after report per company
M3	**Production upgraded to Odoo 19**	Weekend 6–7 Nov	M2, D-03	Tara Finance + IT	Post-upgrade checks signed
M4	**Urban Eats foundation configured**	Thu 12 Nov	M1, I-11, I-12	Tara Owner	Shown on staging
M5	**Central kitchen, POS & payments ready**	Thu 26 Nov	M4, I-14, I-19	Kitchen + Operations	Staging walk-through; pilot-outlet test
M6	**Delivery platforms connected in test**	Thu 26 Nov	D-01, platform approvals	Tara Operations	Test order per connected platform
M7	**Internal testing complete; data loaded**	Mon 30 Nov	M5, M6, 12.6	Code-ox	Internal test report
M8	**Production-ready UAT environment live**	Tue 1 Dec 2026	M7	Committed date	Logins, scripts, data handed over
M9	**UAT acceptance**	Thu 24 Dec	13.5, 13.6	Tara Owner	No open Critical or High issue
M10	**Go / No-Go**	Tue 29 Dec	M9, 14.5	Sponsor + Co-founder	Signed checklist
M11	**Cutover complete: Foodics closed for transactions**	Thu 31 Dec (night)	M10	Both parties	Runbook steps complete
M12	**Production go-live: all outlets on Odoo POS**	Fri 1 Jan 2027	M11	Committed date	POS selling, ZATCA accepted, orders flowing
M13	**Source & documentation handed over**	Thu 14 Jan	M12	Tara Owner + IT	Signed handover pack
M14	**Six-month support ends**	Wed 30 Jun 2027	M12	Both parties	Close-out; AMC optional

TIMELINE

Gantt: Kick-off to Handover

Seventeen workstreams across thirteen weeks, Thursday 15 October 2026 to Thursday 14 January 2027. Weeks run Sunday to Thursday.

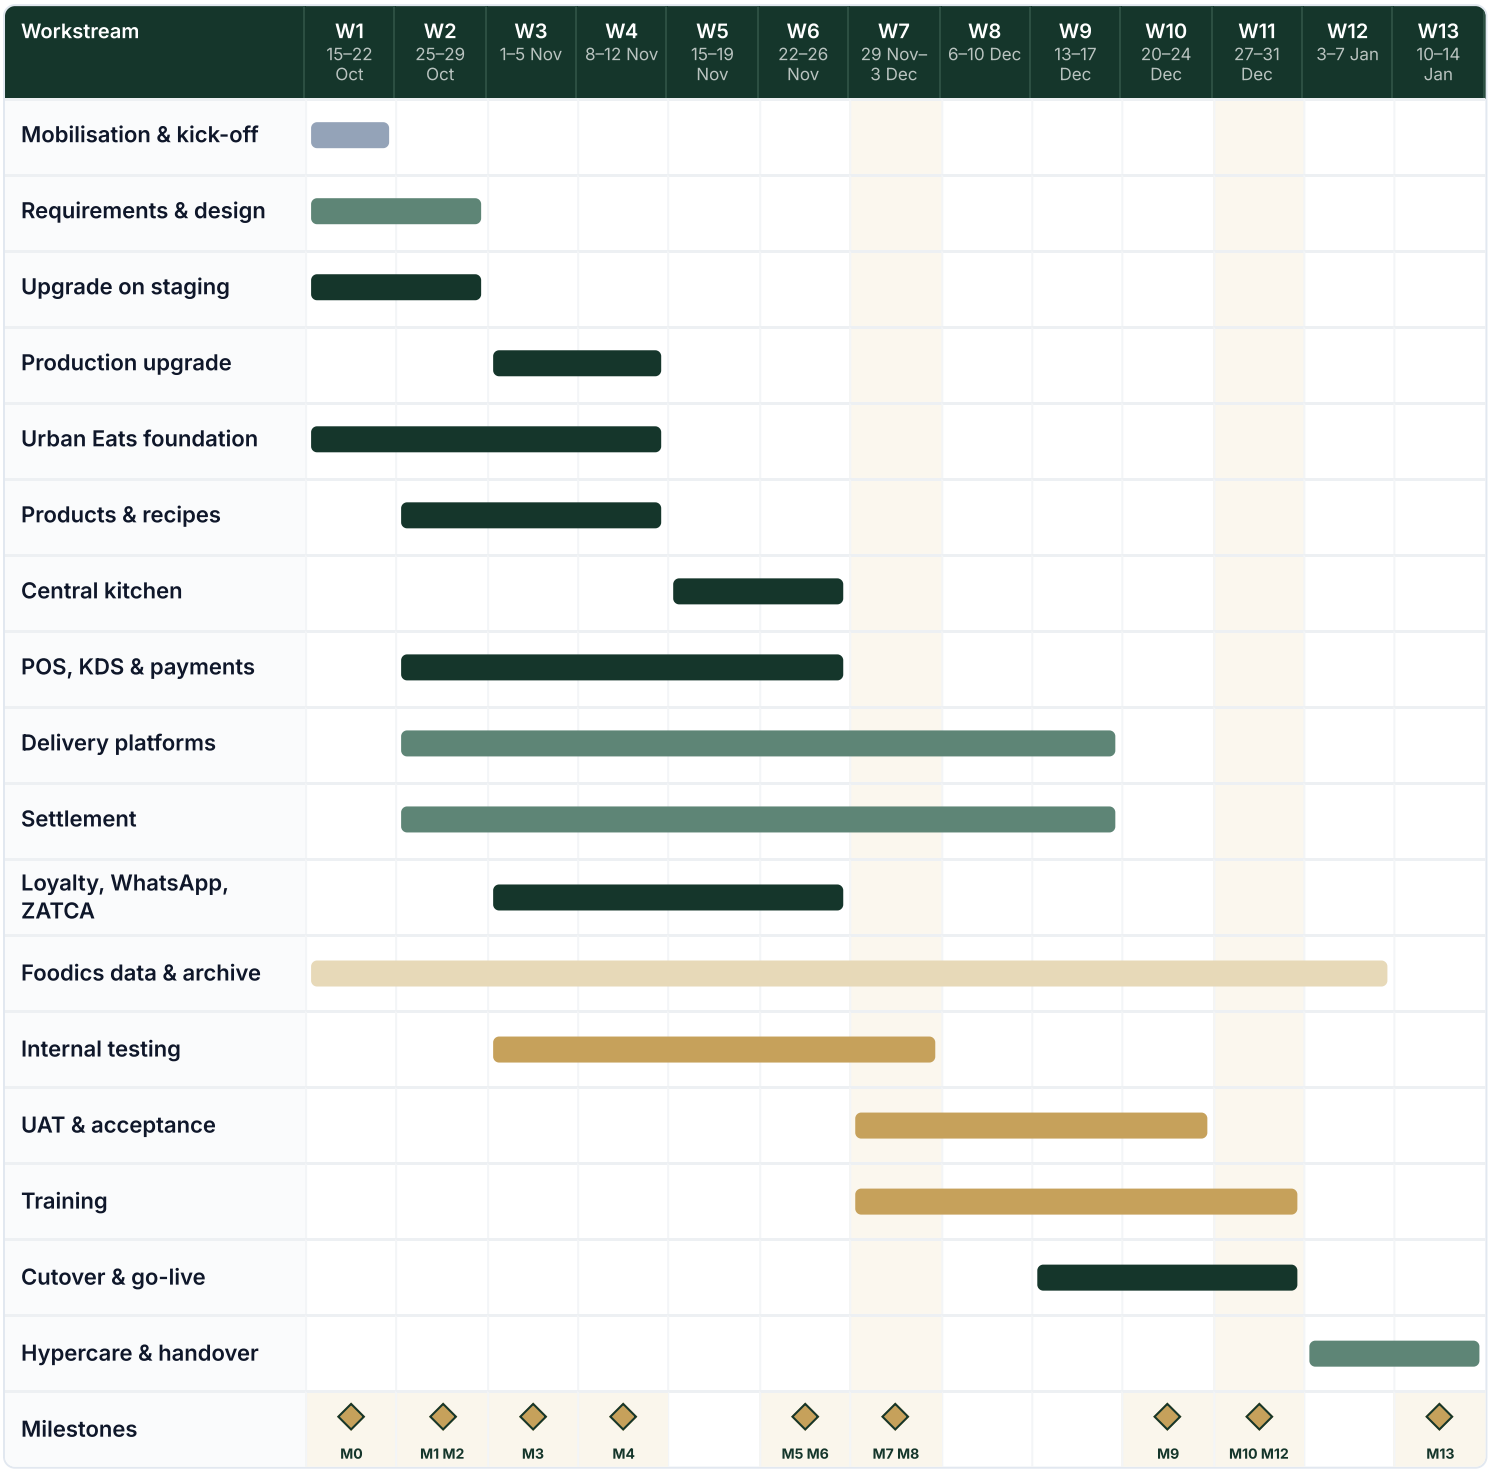

UPGRADE BEFORE CUTOVER

The upgrade is signed off by **29 October** and production is upgraded on the weekend of **6–7 November**, so cutover night carries only the Urban Eats switch.

HIGHLIGHTED WEEKS

W7: the UAT environment goes live on Tue 1 Dec. **W11**: cutover week, ending on the night of 31 Dec for go-live on Fri 1 Jan 2027. M11 (cutover night) sits between M10 and M12.

TASK LIST

Tasks by Workstream

Every task with its expected dates, owner, dependency and output. Green tags are Code-ox roles; gold tags are Tara Holding; grey tags are third parties. Gold rows are milestones.

WS 0 Mobilisation

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
P.1	Solution demo on Odoo 19: Brand / Branch / Channel as standard objects, brand POS and product visibility, central kitchen loop, 3 L bottle → litres conversion	12–13 Oct	Co-founder, Project Manager	—	Demo held
0.1	Financial acceptance; agreement signed; advance invoice	by Thu 15 Oct	Engagement Lead, Sponsor	—	Signed agreement
0.2	Kick-off: scope, team, this plan, cadence, access checklist; D-01 confirmed M0	Thu 15 Oct	Engagement Lead, Project Manager, Owner	0.1	Minutes · M0
0.3	Access: Odoo.sh collaborator, staging URL + admin login, GitHub read access, Foodics console + API; Code-ox registered as partner on the subscription	15–18 Oct	IT	0.2	Access checklist · critical path
0.4	Tracker live in Code-ox Odoo Project: tasks, sub-tasks, dates, dependencies; portal users for Tara; Helpdesk team for UAT and support	15–20 Oct	Project Manager	0.2	Portal access sent
0.5	Kick-off pack: contacts, cadence, severity definitions, requirement questionnaires per area, data templates	Thu 15 Oct	Project Manager	—	Pack issued

WS 0 Requirements & design

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
0.6	Upgrade assessment & module register: each module's function, Odoo 19 version, treatment (retain, migrate, replace, consolidate, retire), licence cost, risk	15–22 Oct	Technical, Project Manager	0.3	Assessment + register
0.7	Urban Eats architecture document (Section 5): company, analytic plans, warehouses and routes, POS and journals, presets, payment methods, access model	18–22 Oct	Project Manager, Co-founder	0.2	Document for approval
0.8	Data migration plan, import templates, Foodics gap report	15–22 Oct	Project Manager, Functional	0.3	Plan + templates
0.9	Requirement workshops (2 hrs each): finance & ZATCA · procurement & inventory · central kitchen · outlets & POS · platforms & settlement · marketing	18–29 Oct	Project Manager, Functional, Finance, Procurement, Kitchen Lead, Operations, Marketing	0.5	Signed workshop notes
0.10	Integration plan per platform (Option A) or UrbanPiper plan (Option B)	25–29 Oct	Technical, Engagement Lead	D-01, 6.1	Integration plan
0.11	POS hardware & network specification per outlet	25–29 Oct	Technical	I-09	Spec for ordering
0.12	Approval of assessment, register and architecture; decisions D-02, D-04, D-05 M1	Thu 29 Oct	Co-founder, Owner	0.6, 0.7	M1

TASK LIST

Tasks by Workstream

WS 1 Odoo 18 → 19 upgrade

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
1.1	Full backup of production; staging branch from the latest backup	Thu 15 Oct	Technical	0.3	Backup reference
1.2	Staging copy upgraded to Odoo 19 through Odoo's upgrade service	15–18 Oct	Technical Odoo	1.1	Odoo 19 staging
1.3	Studio customisations checked item by item: fields, views, reports, automations, server actions, access rules	18–21 Oct	Functional Technical	1.2	Studio checklist
1.4	Third-party modules per register: simplify_access_management advanced_web_domain_widget auditlog hide_menu_user Hikvision attendance muk_web_utils notify_email_inbox muk_mcp muk_mcp_access paymob pos_paymob, and any found in the environment scan. paymob → Odoo 19 standard Paymob provider; MCP replacement proposed (D-04). Nothing removed without approval.	18–22 Oct	Technical IT	1.2, I-04	Status per module
1.5	Pre-validation per company (six), before vs after: trial balance, aged AR/AP, tax reports, fiscal positions, stock valuation, open invoices and bills; every difference explained	20–22 Oct	Project Manager QA	1.3, 1.4	Report per company
1.6	Key flows on the agreed checklist: purchase → receipt → bill → payment sale → delivery → invoice → payment journals; bank reconciliation; inter-company; access rights	20–22 Oct	QA Functional	1.3, 1.4	Checklist results
1.7	Department validation: finance per company, procurement, inventory and every department on their own POs, journals and invoices	25–28 Oct	Finance Departments	1.5, 1.6	Issue list
1.8	Fixes and re-tests for every issue raised	25–29 Oct	Technical	1.7	Issues closed
1.9	Finance sign-off, per company M2	Thu 29 Oct	Finance	1.8	Signed forms · M2
1.10	Production runbook: timings, owners, checks, rollback by restore of the pre-upgrade backup	1–3 Nov	Technical	M2	Runbook
1.11	Production upgrade outside working hours: backup → upgrade → technical checks → finance spot checks → released before Sunday M3	Fri–Sat 6–7 Nov	Technical Finance IT	1.10, D-03	Post-upgrade checks · M3
1.12	First-week monitoring; priority support for all Odoo 19 users	8–12 Nov	Project Manager	M3	Issue log

TASK LIST

Tasks by Workstream

WS 2 Structure, finance & access

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
2.1	Architecture: one company Urban Eats (one CR, VAT, chart of accounts); analytic plans Brand (MYLK, Finjan, Shared) and Branch (one per outlet + Central Kitchen); warehouse + POS per outlet; Odoo “Branches” not used	18–22 Oct	Project Manager Co-founder	0.9	Approved 29 Oct
2.2	D-02 POS revenue tagging: Option 1 standard (journal per POS) or Option 2 module (existing community module tested first)	by 29 Oct	Owner Finance	2.1	Decision
2.3	Company: CR, VAT, ZATCA address fields, fiscal year, Saudi chart of accounts, taxes, banks, one sales + invoice journal per POS	1–3 Nov	Functional	M1, I-11	Configured
2.4	Analytic plans and accounts; applicability mandatory on income and expense; distribution models by product category, supplier and account	3–5 Nov	Functional	2.3	Configured
2.5	Shared finance: “Urban Eats – Shared” tagging and allocation rule; B2B sales team, pricelist, payment terms	8–10 Nov	Functional	2.4	Configured
2.6	Access & brand visibility: user groups per role; POS employee PIN; POS restricted categories per brand; backend access rule per brand group; outlet staff on own POS and warehouse only	8–12 Nov	Functional Technical	2.1, I-18	Role matrix
2.7	Option 2 module (if chosen): Brand / Branch on POS configuration, stamped on session revenue lines and POS invoices; built on an upgrade-safe hook	8–19 Nov	Technical	D-02	Module + note

WS 3 Product master, procurement & inventory

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
3.1	Product structure: categories (Purchased · Semi-finished BASE · Finished per brand · Shared), naming rule, internal references, AVCO costing	25–29 Oct	Project Manager Functional	0.9	D-05 · 29 Oct
3.2	Templates completed: suppliers, vendor prices, pack sizes, supplier barcodes	by Thu 5 Nov	Procurement	0.8	Templates
3.3	Warehouses: Main (buy), Central Kitchen (manufacture, resupplied from Main), one per outlet incl. portable units (resupplied from Main and Central Kitchen); routes	1–5 Nov	Functional	M1	Configured
3.4	Units & packagings (Odoo 19): e.g. Bottle 3 L = 3 L, Carton 12 × 1 L, ml; lots and expiry where needed	1–5 Nov	Functional	3.1	Configured
3.5	One generic material per ingredient; supplier products as vendor lines (code, purchase unit, price); packaging barcodes. Test: 4 bottles received = 12 L	8–12 Nov	Functional	3.2, 3.4	Receipt test passed
3.6	Initial min / max levels per location	by Thu 12 Nov	Inventory	3.3	Levels sheet
3.7	Reordering rules at Main, Central Kitchen and outlets; Replenishment report tested	15–19 Nov	Functional	3.5, 3.6	Rules active

TASK LIST

Tasks by Workstream

WS 3 Product master, procurement & inventory

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
3.8	Scrap reasons; production cost from materials (labour and overhead per D-10)	15–19 Nov	Functional	3.5	Configured
3.9	Foundation configured, shown on staging M4	Thu 12 Nov	Project Manager Owner	2.3–3.5	M4

WS 4 Central kitchen manufacturing

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
4.1	Recipe / BoM template: ingredients, quantities, yield, shelf life, make-to-stock, make-to-order or no-carry-over	Thu 15 Oct	Project Manager	—	Template
4.2	BoM workshops with the kitchen lead: recipes built from scratch (Foodics holds none), top sellers first	25 Oct–5 Nov	Functional Kitchen Lead	4.1, 3.1	Completed templates
4.3	BoMs loaded: manufacture BoMs (multi-level for BASE items) and kit BoMs for outlet menu items	8–12 Nov	Functional	4.2, 3.5	Signed by kitchen lead
4.4	Daily plan: Master Production Schedule + reordering rules → manufacturing orders in Central Kitchen → automatic consumption → transfers to outlets	15–19 Nov	Functional	4.3, 3.7	Flow on staging
4.5	“What to make today” on the Shop Floor screen: produce, record quantity, scrap	15–19 Nov	Functional	4.4	Screen shown
4.6	Expiry dating (first-expiry-first-out); end-of-day disposal list for no-carry-over items; waste with reasons	22–24 Nov	Functional	4.4	Configured
4.7	Kits at outlets: each POS sale deducts ingredients from that outlet’s stock	22–26 Nov	Functional	4.3, 5.4	Stock deduction verified
4.8	Kitchen flow ready: walk-through with the kitchen lead M5	Thu 26 Nov	Kitchen Lead	4.4–4.7	M5

WS 5 Restaurant POS & Kitchen Display

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
5.1	Hardware & network spec issued; devices ordered: POS units, receipt and kitchen printers, KDS screens, terminals	Spec 29 Oct · on site 26 Nov	Technical IT	0.11	Devices on site
5.2	Menus per brand validated from the Foodics export: items, prices, active status	by Thu 5 Nov	Operations	12.2	Validated files
5.3	POS per outlet × brand: restaurant mode, outlet warehouse, own journals, restricted categories, pricelist, presets (dine-in, takeaway, delivery), payment methods incl. one per platform, receipt header, cash control	8–12 Nov	Functional	2.3, 3.3	Configured

TASK LIST

Tasks by Workstream

WS 5 Restaurant POS & Kitchen Display

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
5.4	Menus loaded: POS categories, products, attributes (modifiers), combos, pricelists, taxes	8–19 Nov	Functional	5.2, 5.3	Checked by outlet lead
5.5	Receipts with ZATCA QR; floor plans and tables for dine-in outlets	15–19 Nov	Functional	5.3	Receipt approved
5.6	Kitchen Display per outlet: stations by POS category, stages	15–19 Nov	Functional	5.4	Routing tested
5.7	Outlet procedure: network loss, session open / close, cash	22–24 Nov	Project Manager	5.3	Procedure
5.8	Pilot-outlet hardware test: printers, KDS, terminals, network	24–26 Nov	Technical IT Operations	5.1, 8.5	Test record
5.9	POS & payments ready M5	Thu 26 Nov	Operations	5.3–5.8	M5

WS 6 Delivery platforms (both options)

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
6.1	Store map: every outlet × brand × platform with store IDs and merchant accounts	by Thu 22 Oct	Project Manager Operations	I-09	Store map

WS 6A Delivery platforms: Option A hub

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
6.A1	API access per merchant account, requested on Tara's behalf; weekly follow-up. Confirmed: HungerStation, Keeta, Jahez (incl. Noon). In progress: The Chefz, ToYou, Ninja, Mrsool	From 15 Oct · weekly	Engagement Lead Platforms	6.1	API status weekly
6.A2	Integration plan per platform: endpoints, order states, menu / stock sync, cancellations	25–29 Oct	Technical	6.A1	Plan
6.A3	Hub core in Tara's repository: Brand › Branch › Platform store › POS mapping secure webhooks; orders into POS + KDS; menu and price push; sold-out sync; status write-back; retry queue, logs, alerts	1–19 Nov	Technical	6.A2, 5.3	Core on staging
6.A4	Connectors: HungerStation, Jahez (incl. Noon), Keeta	8–26 Nov	Technical	6.A3	Test orders end to end
6.A5	The Chefz, ToYou, Ninja, Mrsool: each built and tested once its API is issued	As APIs arrive	Technical Platforms	6.A3	Test orders
6.A6	Platform testing or certification where required	22 Nov–17 Dec	Technical Platforms	6.A4	Platform confirmation
6.A7	A platform without API by go-live keeps its tablet; connected when ready, within scope	Go / No-Go	Engagement Lead	6.A5	Status per platform

TASK LIST

Tasks by Workstream

WS 6B Delivery platforms: Option B UrbanPiper

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
6.B1	Joint Odoo / UrbanPiper meeting: confirm Saudi coverage (Keeta, ToYou, The Chefz, Ninja), fees, onboarding time; subscription ordered via Odoo	by Thu 22 Oct	Owner Odoo UrbanPiper	I-07	Coverage in writing
6.B2	UrbanPiper store per outlet × brand created from POS; platforms linked and "go live" requested per store	25 Oct–19 Nov	Project Manager UrbanPiper	6.B1, 5.3	Stores linked
6.B3	Food Delivery Connector: products flagged for delivery, menu sync, store timings, payment method per platform, routing to POS + KDS; combos mapped to attributes (not supported by UrbanPiper)	15–26 Nov	Functional	6.B2, 5.4	Configured
6.B4	Connector shown on staging; HungerStation orders are rejected in the HungerStation app, not in Odoo	Thu 26 Nov	Project Manager	6.B3	Demo held

WS 6 Delivery platforms (both options)

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
6.9	Platforms connected in test (either option), subject to platform approvals M6	Thu 26 Nov	Operations	6.A4 / 6.B4	M6

WS 7 Settlement & reconciliation

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
7.1	Payout statements and reports: three months per platform	25 Oct–5 Nov	Project Manager Finance	I-07	Samples
7.2	Settlement plan and automation level, following Odoo's official response	8–12 Nov	Project Manager Functional	7.1, D-09	Settlement plan
7.3	Clearing account per platform; import of statements; commission bill with VAT; promotions, refunds, cancellations, penalties, delivery charges; bank reconciliation	15–26 Nov	Functional	7.2	Configured
7.4	Reports by platform, brand and branch; tested with a real payout per platform	6–17 Dec	Functional Finance	7.3	UAT result

WS 8 Payments

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
8.1	Odoo 19 availability confirmed for Geidea, NearPay and Paymob terminals, before you commit	25–29 Oct	Technical	I-09	Note → D-06 by 5 Nov
8.2	Merchant accounts and keys, test and live: Paymob (Saudi), Tabby, Tamara	by Thu 5 Nov	Finance	—	Keys shared securely
8.3	Paymob (standard Odoo 19 provider): test mode, methods synchronised, card incl. Mada. Apple Pay route per D-14 (not in Odoo's Paymob connector today)	8–12 Nov	Technical	8.2	Test payments

TASK LIST

Tasks by Workstream

WS 8 Payments

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
8.4	Tabby & Tamara: through Paymob where enabled on your Paymob account (standard); a Code-ox module only for a method Paymob does not provide	8–19 Nov	Technical	8.2, 8.3	Payments + refunds
8.5	POS terminal integration for the provider(s) in D-06	15–26 Nov	Technical IT	D-06, I-19	Pilot-outlet test
8.6	Rules: paid only on terminal or gateway confirmation; refunds to original method; failed payments retried or switched; split payments	22–26 Nov	QA	8.3–8.5	Test cases passed

WS 9 WhatsApp

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
9.1	Meta Business verification, dedicated number, Business Manager access	by Thu 5 Nov	Marketing Meta	—	Verified account
9.2	Odoo WhatsApp connected to Meta (no third-party provider); templates on POS orders and invoices: receipts, order confirmations, customer messages	8–12 Nov	Functional	9.1	Drafts
9.3	Templates submitted to Meta; kitchen and delivery status messages reviewed case by case (D-08)	by Thu 19 Nov	Functional Marketing	9.2	Meta approval
9.4	Automatic sending through automation rules; tested	22–26 Nov	Functional	9.3	Messages received

WS 10 Loyalty, promotions & rewards

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
10.1	Management session: each loyalty idea classed as standard, configuration, supported app or custom	1–5 Nov	Project Manager Marketing	—	Ideas assessed
10.2	Programs agreed (D-07)	by Thu 12 Nov	Marketing	10.1	Program list
10.3	Discount & Loyalty programs per brand (limited to that brand's POS and website): points, rewards, coupons, promo codes, Buy X Get Y, gift cards, eWallet	15–26 Nov	Functional	10.2, 5.4	Configured
10.4	Demo to your team; Foodics loyalty and gift-card balances loaded as available	Thu 26 Nov	Project Manager	10.3, 12.1	Demo held

WS 11 ZATCA Phase 2

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
11.1	Saudi e-invoicing modules incl. POS; company ZATCA fields; invoice journal per POS; default walk-in customer	1–12 Nov	Functional	2.3	Configured
11.2	Fatoora administrator nominated with simulation access	by Thu 19 Nov	Finance	—	Access confirmed

TASK LIST

Tasks by Workstream

WS 11 ZATCA Phase 2

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
11.3	Simulation onboarding per POS journal (one-time code valid 60 minutes, scheduled together) and compliance checks	22–26 Nov	Functional Finance ZATCA	11.1, 11.2	Compliance passed
11.4	UAT: simplified and standard invoices, credit notes, B2B clearance, rejected-invoice handling	6–17 Dec	QA Finance	11.3	UAT result
11.5	Production onboarding per POS journal (switch is one-way)	27–30 Dec	Functional Finance	M10	Certificates

WS 12 Foodics extraction, loads & archive

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
12.1	Foodics console and API access; data inventory; gap report on what cannot be exported (e.g. balances)	15–22 Oct	Project Manager IT	I-05	Gap report
12.2	Full extraction: menus, categories, products, modifiers, customers; history to date: orders, payments, discounts, refunds, inventory, balances, tax and financial reports, branch set-up	15 Oct–5 Nov	Technical IT	12.1	Data set v1 in your storage
12.3	Field mapping per brand	25 Oct–5 Nov	Functional	12.2	Mapping sheet
12.4	Clean-up by your team: prices, active items, duplicate customers	1–5 Nov	Operations Marketing	12.3	Validated files
12.5	Trial load 1 into build environment; counts and samples checked	8–12 Nov	Technical	12.4, 3.9	Load report
12.6	Trial load 2 into UAT environment	29 Nov–1 Dec	Technical	12.5	Load report
12.7	Top-up export of new Foodics transactions	13–17 Dec	Technical	12.2	Archive updated
12.8	Rehearsal load with the cutover method; timings recorded	20–24 Dec	Technical	14.2	Rehearsal report
12.9	Menu freeze in Foodics; later changes applied in both systems by Code-ox	from Sun 27 Dec	Operations	—	Freeze notice
12.10	Final export after the last Foodics transaction	Thu 31 Dec (night)	Technical	M11	Final export
12.11	Opening stock from physical count at every outlet, Main Warehouse and Central Kitchen, posted before the first sale	Thu 31 Dec (night)	Project Manager Inventory Operations	I-23	Count sheets + adjustment
12.12	Final archive with index and data dictionary: dataset, period, content	3–7 Jan	Project Manager	12.10	Archive handed over

WS 13 Testing, UAT & training

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
13.1	Build testing: each item tested before it is shown to Tara	1–26 Nov	QA Functional	—	Each item tested before it is shown

TASK LIST

Tasks by Workstream

WS 13 Testing, UAT & training

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
13.2	System integration test: end-to-end flows including platforms, payments and ZATCA simulation M7	22–30 Nov	QA Technical	13.1	Internal test report · M7
13.3	UAT scenarios, scripts and calendar issued	26 Nov	QA Project Manager Project Owner	13.1, I-21	UAT scripts (DL-12)
13.4	Key-user training (train-the-trainer) before UAT; role guides and quick-reference cards ready by Thu 3 Dec	29 Nov–3 Dec	Project Manager Functional Key users	13.3	Key users trained; attendance recorded
13.5	UAT cycle 1: key users run all scenarios, guided by Code-ox; defects logged in Helpdesk	6–10 Dec	QA Project Manager Finance Kitchen Lead Operations	M8, I-21	All scenarios run; defects logged
13.6	UAT cycle 2 and day-in-the-life: re-tests with kitchen and one outlet team; a full trading day simulated	13–17 Dec	QA Project Manager Finance Kitchen Lead Operations	13.5	Re-tests passed; full trading day simulated
13.7	Role training: finance (2 sessions), procurement & warehouse, central kitchen, marketing	13–17 Dec	Project Manager Functional Finance Procurement Kitchen Lead Marketing	13.4	Attendance recorded per session
13.8	Outlet managers and cashiers by outlet group; IT / developer session	20–24 Dec	Project Manager Functional Operations IT	13.7	Attendance recorded per session
13.9	Regression testing before UAT acceptance	20–24 Dec	QA	13.6	Regression results; no open Critical or High issue
13.10	Refresher and go-live briefing	27–30 Dec	Project Manager Operations Finance	13.8	Briefing held

WS 14 Cutover preparation

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
14.1	Cutover runbook and contingency plan (within Odoo)	13–17 Dec	Project Manager Technical	13.5	Runbook
14.2	Cutover rehearsal on a fresh production copy; timings recorded	20–24 Dec	Technical IT	14.1	Rehearsal report
14.3	UAT acceptance; code freeze M9	Thu 24 Dec	Owner	13.6	M9

TASK LIST

Tasks by Workstream

WS 14 Cutover preparation

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
14.4	Count teams, count sheets, outlet go-live contacts; Foodics end date (D-12)	by Thu 24 Dec	Inventory Operations	I-23	Count plan
14.5	Urban Eats deployed to production: modules from your repository, configuration, master data, users (no transactions)	27–28 Dec	Technical Project Manager	M9	Deployment checklist
14.6	Go / No-Go against the checklist below M10	Tue 29 Dec	Co-founder Owner Sponsor	14.5	M10
14.7	ZATCA production onboarding per POS journal; refresher training	29–30 Dec	Functional Finance	M10	Certificates
14.8	Final checks at every outlet: devices, printers, KDS, terminals, network, platform stores	Wed 30 Dec	Technical Operations	14.5	Outlet checklist

WS 15 Hypercare, handover & support

ID	TASK	WHEN	OWNER	NEEDS	OUTPUT
15.1	Hypercare: daily check-in with the Project Owner; tickets through Helpdesk, phone or WhatsApp under the SLA	3–14 Jan	Project Manager Engagement Lead	M12	Issue log
15.2	Final Foodics archive with index and data dictionary (12.12)	3–7 Jan	Project Manager	12.10	Archive
15.3	Go-live report: what went live, open items, platform status, next steps	Thu 7 Jan	Project Manager Co-founder	M12	Report
15.4	Go-live acceptance feedback within 5 business days	by Thu 7 Jan	Owner	15.3	Acceptance
15.5	Handover pack: source in your repository, deployment notes, migration scripts, technical, integration / API and configuration documents, walked through with your developer M13	10–14 Jan	Technical IT	M12	Signed · M13
15.6	Six months of support under the SLA M14	1 Jan–30 Jun 2027	Engagement Lead	M12	M14

INPUTS AND DECISIONS

What Tara Holding Provides

Tara Holding owes 24 inputs and 14 decisions. Ten of the inputs fall due by 22 October, so the first week carries the most. A late input moves the tasks that depend on it.

24	10	14	1 Dec
inputs from Tara Holding	inputs due by 22 October	decisions	UAT environment, committed

Inputs

ID	INPUT	DUE	OWNER	UNBLOCKS
I-01	Signed agreement and advance payment	Thu 15 Oct	Sponsor	0.1
I-02	Project owner and key users named per area	Thu 15 Oct	Sponsor	0.9
I-03	Odoo.sh access, staging URL + admin login, GitHub read access; Code-ox on the subscription	Thu 15 Oct	IT	1.1 · critical
I-04	Licences and source of third-party modules	Thu 15 Oct	IT	1.4
I-05	Foodics items F1–F9	15–22 Oct	IT, Operations	12.1
I-06	Requirement questionnaires answered per area	Thu 22 Oct	All leads	0.9
I-07	Platform merchant accounts (A) or UrbanPiper order (B); payout samples	Thu 22 Oct	Operations	6.A1 / 6.B1
I-08	Finance validator per company; validation checklist input	Thu 22 Oct	Finance	1.5
I-09	Outlet list: brand, address, hours, devices, platform store IDs	Thu 22 Oct	Operations	6.1, 0.11
I-10	Repository for custom code in Tara's name	Thu 22 Oct	IT	2.7, 6.A3
I-11	Urban Eats CR, VAT, address, accounts, banks	Thu 29 Oct	Finance	2.3
I-12	Suppliers, vendor prices, pack sizes, barcodes	Thu 5 Nov	Procurement	3.5
I-13	Paymob, Tabby, Tamara merchant accounts and keys	Thu 5 Nov	Finance	8.3
I-14	Validated menus per brand; recipes / BoMs	Thu 5 Nov	Operations, Kitchen Lead	4.3, 5.4
I-15	Meta verification, WhatsApp number, access	Thu 5 Nov	Marketing	9.2
I-16	Initial minimum stock levels	Thu 12 Nov	Inventory	3.7
I-17	Fatoora administrator and access	Thu 19 Nov	Finance	11.3
I-18	User list with roles, incl. cashiers	Thu 19 Nov	Operations	2.6
I-19	POS hardware, KDS, terminals, network on site	Thu 26 Nov	IT	5.8, 8.5
I-20	Odoo subscription updated (count from Code-ox by 12 Nov)	Thu 26 Nov	IT	M8
I-21	UAT testers and calendar	Thu 26 Nov	Owner	13.5
I-22	Training attendance lists	Thu 3 Dec	Operations	Training
I-23	Stock count teams; outlet go-live contacts	Thu 24 Dec	Inventory	12.11
I-24	Fatoora codes on call; outlet managers on cutover night	27–31 Dec	Finance, Operations	11.5, 14

TEAM AND GOVERNANCE

Team, Roles & Governance

Raghib Ali Rafeeque is Tara's single point of contact, Shayar CV runs delivery day to day, and Thayif Kabir oversees the engagement and chairs five steering reviews between 29 October and 24 December.

Code-ox Technologies

- **Engagement Lead**: Raghib Ali Rafeeque. First contact for Tara: commercial matters, change requests, platform API requests, joint Odoo / UrbanPiper meetings.
- **Project Manager**: Shayar CV. Runs delivery day to day across all workstreams; owns the tracker and the Thursday status report.
- **Overall monitoring**: Thayif Kabir, Co-founder. Odoo 19 certified solution architect. Approves the architecture and every custom module design, reviews quality at M1, M2, M8 and Go / No-Go, and is the final escalation.
- **Head of Operations**: Shabeeb K. Resourcing and team allocation.

Tara Holding

- **Project Owner**: Eng. AbdulRahman Al-Nouman. Decisions, approvals and access; chairs Go / No-Go with the sponsor.
- **Executive Sponsor**: To be confirmed. Steering member; final Go / No-Go.
- **Area leads**: Finance (plus one validator per company), Procurement & Inventory, Central Kitchen, Operations and outlet managers, Marketing, IT. Validation, recipes, menus, POS, loyalty, WhatsApp, access, devices and handover.

How we stay in sync

FORUM	WHEN	WHO	COVERS
Kick-off	Thu 15 Oct, 2 hours	Both teams, sponsor, Co-founder	Scope, this plan, access checklist, requirement questionnaires, D-01
Status report	Every Thursday	Project Manager to Project Owner	Per workstream: on track, at risk or late; done, next, risks, Tara actions due
Steering review	29 Oct, 12 Nov, 26 Nov, 10 Dec, 24 Dec	Co-founder, Engagement Lead, Project Manager, Owner, Sponsor	Milestones, risks, decisions, change requests
Live tracker	Always	Everyone, via portal	Code-ox Odoo Project: tasks, dates, dependencies, Gantt; Helpdesk for UAT defects and support tickets

CHANGE CONTROL

Change requests are logged in the tracker, and the impact on scope, cost and dates is given before any work starts. Work begins only on written approval. Code freeze starts on **24 December**, with Critical fixes only.

INPUTS AND DECISIONS

Decisions Needed from Tara Holding

Each decision is due on the date shown so the tasks that depend on it can start on time.

ID	DECISION	DUE
D-01	Delivery layer: Option A (Code-ox hub) or B (UrbanPiper)	Thu 15 Oct
D-02	POS revenue tagging: Option 1 standard or Option 2 module	Thu 29 Oct
D-03	Production upgrade window: 6–7 Nov (planned) or 31 Dec	Thu 29 Oct
D-04	Treatment of each third-party module, incl. MCP replacement	Thu 29 Oct
D-05	Product categories, naming and coding	Thu 29 Oct
D-06	POS terminal provider(s): Geidea, NearPay, Paymob	Thu 5 Nov
D-10	Labour and overhead in production cost	Thu 5 Nov
D-14	Apple Pay route on the website	Thu 5 Nov
D-07	Loyalty and promotion programs	Thu 12 Nov
D-08	Kitchen / delivery status messages on WhatsApp	Thu 12 Nov
D-09	Settlement automation level	Thu 12 Nov
D-11	Training languages and format	Thu 26 Nov
D-12	Foodics end date (read-only until archive verified)	Thu 24 Dec
D-13	Go / No-Go	Tue 29 Dec

DATES AND CONDITIONS

The 1 December and 1 January dates hold if the agreement is signed and kick-off is held by **15 October**, inputs arrive on the dates in this plan, UAT feedback is timely, and delivery-platform approvals come through.

DATES IN THIS PLAN

Dates are expected dates from Execution Plan v1.2 (12 October 2026). They move with the signed agreement, Tara's inputs and platform approvals.

RISKS

Top Risks and How They Are Managed

Twelve risks are reviewed every Thursday. The ones that can most directly move the 1 December and 1 January dates are late delivery-platform APIs (R1, R2), rebuilding product and recipe data (R5), and validating six companies in one week (R4).

ID	RISK	MITIGATION	OWNER
R1	**Platform APIs issued late (A)**	Requested already; weekly follow-up; built in order of arrival; late platform keeps its tablet	Code-ox
R2	**UrbanPiper coverage (B): ToYou and The Chefz are not in Odoo's UrbanPiper list today; Ninja not listed for KSA**	Confirm in the joint meeting by 22 Oct; uncovered platform stays on tablet or uses a direct connector	Tara, UrbanPiper
R3	**A third-party module has no Odoo 19 version**	Register by 22 Oct; migrate or replace; nothing removed without approval	Code-ox
R4	**Six companies validated in one week**	Before / after reports prepared so finance reviews differences only	Both
R5	**No recipes in Foodics; product data needs rebuilding**	Templates Day 1; BoM workshops Weeks 2–3; top sellers first	Tara
R6	**Foodics cannot export some data (e.g. balances)**	Gap report by 22 Oct; approach agreed early	Code-ox
R7	**Hardware, terminals or network late**	Spec 29 Oct; on site 26 Nov; pilot test	Tara
R8	**Key users unavailable in December**	Testers and calendar named by 26 Nov	Tara
R9	**ZATCA issue near go-live**	Simulation passed 26 Nov; one-time code process rehearsed	Both
R10	**Apple Pay not in Odoo's Paymob connector**	Route decided by 5 Nov (D-14)	Code-ox
R11	**Lot-tracked ingredients inside POS kits (known Odoo issue)**	Lots and expiry kept in Central Kitchen; outlet kit ingredients untracked	Code-ox
R12	**Late scope changes**	Change control; code freeze from 24 Dec	Both
