



ODOO ERP · RE-IMPLEMENTATION & DIGITAL TRANSFORMATION

One connected system, floor to finance.

A single Odoo platform for Alternative Rebar Plant — manufacturing, inventory, quality, finance, HR and compliance — re-implemented on solid foundations, built to reach SIRI Band 2 and unlock Future Factories grant support.

Manufacturing & MRP**Inventory & traceability****Quality to batch****ZATCA Phase 2****KSA Payroll****SIRI Band 2 ready****DELIVERED BY AN ODOO SILVER PARTNER**

CodeOx Technologies

Official Odoo Silver Partner with certified experts — authorised to sell, implement, configure and support Odoo, with direct access to Odoo's partner channels and pricing.

Odoo Silver Partner**Certified Experts**

PROPOSAL REF

CX-ARP-TP-2026-01

DATE

September 2026

PREPARED FOR

Alternative Rebar Plant

VALIDITY

30 days

OVERVIEW

Executive Summary

Alternative Rebar Plant runs on Odoo today, but the platform is not yet delivering the connected, trustworthy operation a growing GFRP manufacturer needs. This proposal sets out how CodeOx — an **Odoo Silver Partner** — will re-implement and extend your Odoo into one system that runs the plant end to end: **manufacturing, inventory, quality, procurement, finance, HR/payroll and compliance**, with the shop floor and the books finally reading from the same data.

Two threads run through everything that follows. First, a **compliant licensing model** that stops you paying for a user licence per head — the saving you asked about, done exactly the way Odoo intends. Second, alignment to **SIRI Band 2**, the maturity level that opens the government's **Future Factories** grant of up to 80% (cap SAR 300,000) toward this exact kind of ERP work. We begin with a fixed-scope audit at no cost, so nothing is priced before it is understood.

HEADLINE OUTCOMES

One connected system (no re-keying, real stock, true cost) · **a legal licence split** that cuts your per-user bill · **batch traceability & ZATCA compliance** your mega-project clients expect · and a path to **SIRI Band 2** with up to 80% grant funding on the transformation.

WHAT WE WILL DELIVER

- ✓ **Re-implemented Odoo core**
Manufacturing, inventory, quality, purchase and finance, integrated and tested on staging.
- ✓ **Compliant licence model**
Employee / portal / kiosk split with an exact licensed-user count.
- ✓ **KSA HR & payroll**
GOSI, WPS/Mudad, end-of-service, and structured appraisals.
- ✓ **Integrations**
WhatsApp, geolocation, ZATCA Phase 2, and domain / SSO link.
- ✓ **SIRI alignment**
Build configured toward Band 2 with Future Factories grant support.
- ✓ **Training & handover**
Role-based training, source, docs — your team owns the system.

CONTEXT

Understanding of ARP

Alternative Rebar Plant, founded 2019 in Dammam 3rd Industrial City, manufactures **GFRP (glass-fibre reinforced polymer) rebar** using FRT Canada technology. ARP is a registered/approved vendor to **Aramco, NEOM, Red Sea Global, ROSHN, King Salman International Airport, Saudi Water Authority and SABIC**, with SASO, ARAMCO, CE, ASTM and CSA compliance — a supplier operating at mega-project standard.

An Odoo subscription is already in place, but from our discussions the system is under-used and not fully integrated — a normal, maturing stage for a plant that scaled quickly. The opportunity now is not to start over, but to **re-implement on solid foundations**: model manufacturing properly, make inventory trustworthy, connect the modules, and layer on the HR, compliance and integration pieces the business has grown into.

► What ARP makes

GFRP rebar from resin and glass fibre — a real manufacturing flow (raw material → work orders → finished goods) Odoo must model with BOMs, routings, yield and **batch traceability**.

► What ARP needs from Odoo

Trusted stock and cost, quality tied to batches, KSA-compliant invoicing and payroll, department visibility, and a **licence model** that fits a large workforce without a seat per person.

GOALS

Objectives & Scope

#	IN SCOPE FOR THIS ENGAGEMENT
01	Compliant, cost-optimised licensing model Move from licence-per-user to the employee / portal / kiosk split — legal, and a large reduction in paid seats.
02	Inventory set up properly Warehouses, locations, lot/serial traceability, reordering and correct valuation.
03	Manufacturing & quality BOMs and routings for GFRP rebar, work orders, and quality checks linked to production batches.
04	Finance & ZATCA Phase 2 Accounting integrated with operations and compliant e-invoicing.
05	HR: Payroll & Appraisals KSA payroll (GOSI, WPS/Mudad, EOSB) and structured employee appraisals.
06	Integrations WhatsApp, geolocation, and the system linked to your company domain (branded URL, email, optional SSO).
07	Enablement Use-case-specific demos before commitment, and role-based training at handover.
08	SIRI alignment Configure toward SIRI Band 2 and support the Future Factories grant application.

OUT OF SCOPE

Unless separately agreed: shop-floor IoT/PLC hardware supply, third-party module licence fees, and process re-engineering beyond ERP configuration. These are identified in the audit and quoted separately if wanted.

COST MODEL

Licensing Model & Cost

You pay a user licence per person today, which scales badly. The saving is real, and it is **fully legal** — it is Odoo's own model: Odoo bills only for people who log into the backend to create and edit documents. Everyone else is free.

STRAIGHT ANSWER

The **employee-and-portal concept is a standard, fully-licensed Odoo model** — not a loophole. Nothing to worry about on the legal side.

✓ Where you save — 100% legitimate

Employees ≠ Users: an employee record has no login and costs nothing. **Kiosk mode** for attendance/production needs no per-worker login. **Free portal** for customers & suppliers. Licence only the handful who truly transact.

● One practical point

A portal user is free but **limited** — for viewing, not running backend apps. So anyone actively working inside Inventory, Manufacturing, Payroll or Appraisals gets a normal licensed user. We simply count those people accurately.



OUR RECOMMENDATION

The licence split

We map your headcount into three buckets: **employee records (free)** for most of the shop floor, **kiosk** for attendance/production, and **paid licences only for real operators**. You get the cost drop, fully within Odoo's terms — the exact licensed-user count is delivered in the audit.

PRICING

Final per-user pricing is confirmed against the live Odoo KSA price list at quotation time. As your Silver Partner, we secure partner pricing on your behalf.

APPLICATION MAP

Proposed Odoo Modules

The applications that make up the ARP build. The final module list is confirmed in the audit against what is already live.

MODULE	WHAT IT DOES FOR ARP	PRIORITY
Manufacturing (MRP)	BOMs, routings, work orders and yield for GFRP rebar production.	Core
Inventory	Warehouses, locations, lot/serial traceability, reordering, valuation.	Core
Quality	QC control points and checks linked to production batches (ASTM/CSA evidence).	Core
Purchase	RFQs, vendor management, procurement tied to production demand.	Core
Accounting	Financials integrated with operations; ZATCA Phase 2 e-invoicing.	Core
Sales / CRM	Quotations and orders for mega-project clients; pipeline visibility.	High
Employees	Workforce records (free, no licence) — the base of the licence split.	High
Payroll	KSA salary structures, GOSI, WPS/Mudad, end-of-service.	High
Appraisals	Structured performance evaluation cycles.	Medium
Attendance	Kiosk clock-in (no per-worker licence) with optional geolocation.	Medium
Maintenance	Preventive / curative maintenance on production equipment.	Optional
Studio	Custom fields, reports and Arabic/RTL documents where needed.	As needed

NOTE

Module priorities are indicative and refined in the audit. Some may already be partly configured on your current Odoo — where so, we build on the existing setup rather than replace it.

TECHNICAL DETAIL

Technical Work Packages

How each agreed item is delivered. Everything is built and tested on a staging copy first, then handed over with your team trained.

Inventory done properly

Warehouse & location structure, min/max reordering, **lot/serial tracking** for full batch traceability, and correct cost valuation — so on-hand and COGS can be trusted.

Manufacturing & quality

Multi-level BOMs and routings for GFRP rebar, work centres and work orders, with **quality control points linked to each production batch** — the evidence ASTM/CSA/SASO buyers expect.

Finance & ZATCA Phase 2

Chart of accounts, analytics per cost centre, and **ZATCA Phase 2-compliant e-invoicing** (clearance for B2B, QR where applicable) integrated with sales and inventory.

Payroll (KSA)

Salary structures, allowances/deductions, **GOSI, WPS/Mudad** bank file and end-of-service — pay runs produced from Odoo each cycle, compliant.

Appraisals

Evaluation cycles, templates and scoring. Self-assessment needs a licensed login, so we scope reviewers-only licences or an HR-led model with you.

Geolocation

Geo-tagged attendance / field check-ins and delivery/customer mapping — configured where it earns its place, confirmed in the audit.

WhatsApp integration

WhatsApp connected to Odoo for order confirmations, dispatch notifications and internal alerts — one channel, sent from the system.

Domain & access

Odoo bound to your company domain — branded URL, company email on documents, and optional single sign-on with existing work accounts.

Use-case demos

Before full commitment, demos on **your** real flows — a rebar production order, a stock issue, a payroll run — so you see it working on your case.


Training & adoption

Role-based sessions for operators, storekeepers, HR and accounts, with short written guides so the team owns the system after go-live.

PLATFORM

Solution Architecture

A clean, supportable platform your team can own after go-live — one connected line from the shop floor to the books.

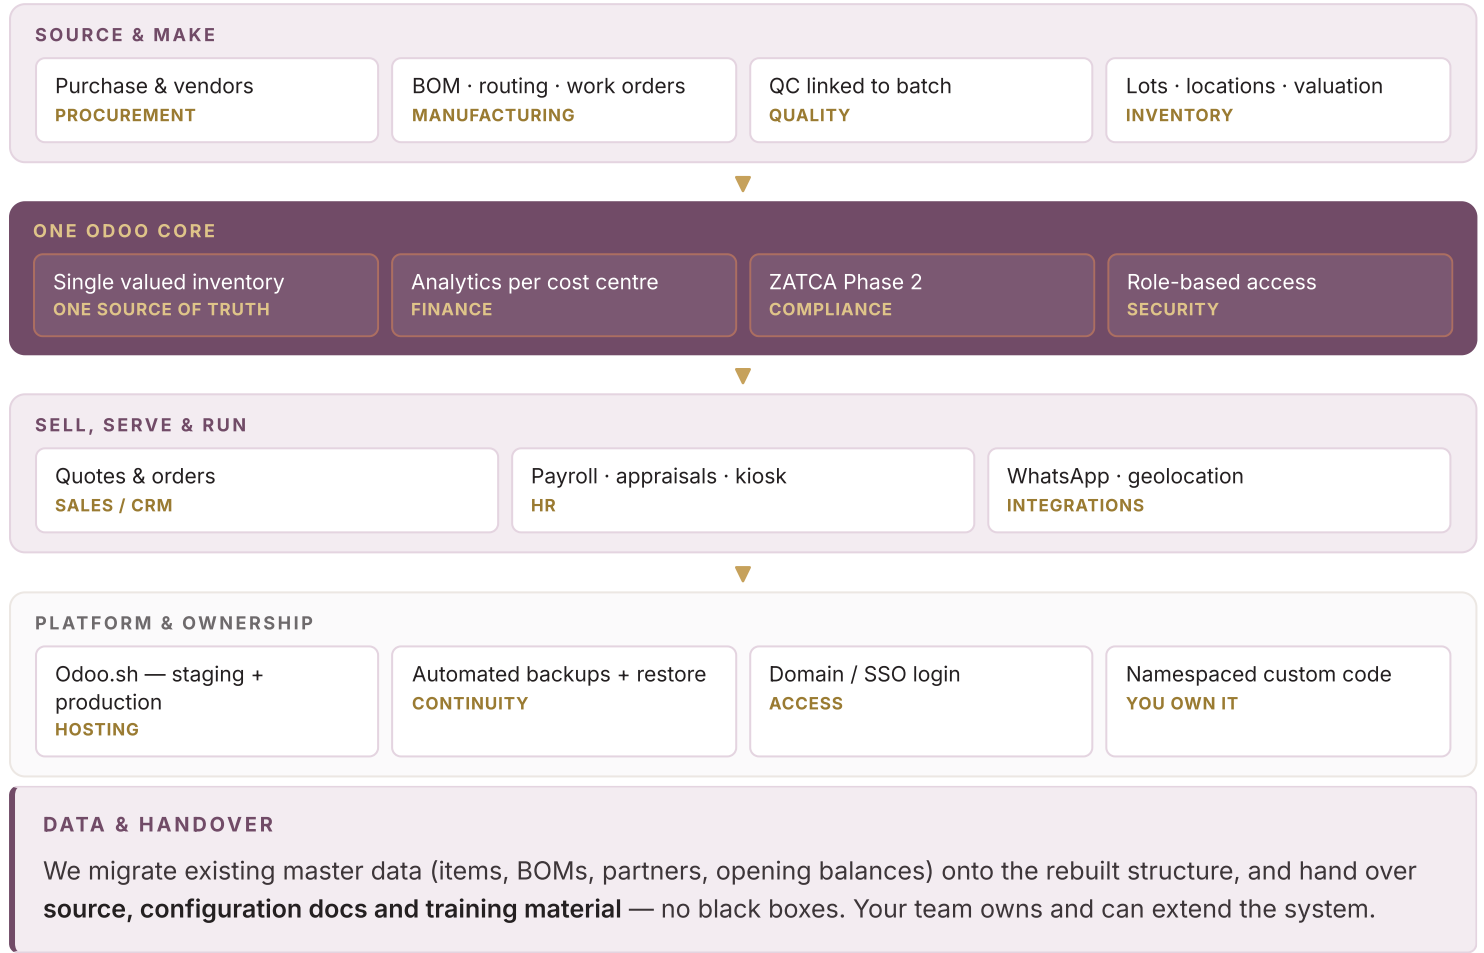

GOVERNMENT SUPPORT · VISION 2030

SIRI & Future Factories Funding

SIRI (Smart Industry Readiness Index) is the framework the Ministry of Industry & Mineral Resources uses to rate factory digital maturity — the only such index endorsed by the World Economic Forum. It gates the **Future Factories Program**, whose grants co-fund exactly the kind of ERP transformation in this proposal. As a 2019 plant, ARP is in the existing-factory track; the practical target is **Band 2**, which an integrated Odoo directly delivers.

up to 80%

funded — capped at SAR 300,000. Illustratively, a SAR 200,000 ERP scope would cost ARP roughly **SAR 40,000**; the Ministry grant covers the rest.

SUPPORT TRACK	COVERAGE	CAP	PURPOSE
Basic Digitization Grant ← ARP	Up to 80%	SAR 300,000	ERP / digital systems to reach SIRI Band 2
Innovative Factories Grant	25%	SAR 10,000,000	R&D and innovation, with research partners
Tanafusiya (SIDF)	Loans + grants	SAR 40,000,000	Automation, digitization, energy efficiency

WHERE CODEOX FITS — STRAIGHT TALK

Odoo delivered here directly raises SIRI Band 2 dimensions (enterprise integration, connectivity, quality-to-batch, cybersecurity). Funded work is submitted through an **approved provider** — a requirement for every vendor — which we deliver by partnering with an accredited provider or securing accreditation. The Odoo project stands on its own value; the grant is **upside**.

IMPORTANT NOTE ON FIGURES

Grant figures (80% / SAR 300k) and the Band 2 target are reported consistently by approved implementation providers but not yet cross-checked against a primary MIM document. Assessment-to-results typically runs 8–14 weeks. Exact terms and the approved-provider route are confirmed with MIM before hard figures are committed — the grant is a target we pursue together, not a guarantee.

HOW WE DELIVER

Delivery Methodology

A staged approach that de-risks every step. Nothing touches production until it is signed off on staging.

- 0

Audit & SIRI gap assessment free

Fixed-scope review of the current Odoo and operations against Band 2 — RAG scorecard, gap register, licence-count, and a phased fix-vs-rebuild roadmap.
- 1

Blueprint & demos

Solution design signed off with your team, plus use-case demos on your real flows before committing to the full build.
- 2

Configure & build (staging)

Modules configured, customisations built, integrations wired — all on a staging clone, code-reviewed with your developer.
- 3

Data migration & UAT

Master data and opening balances migrated; you test core flows and sign off.
- 4

Training & go-live

Role-based training and guides, then a scheduled cutover with a rollback plan.
- 5

Hypercare & SIRI follow-up

Stabilisation support after go-live, and the follow-up SIRI assessment to confirm the new maturity level for the grant.

SCHEDULE

Indicative Timeline

PHASE	FOCUS	DURATION
0 · Audit	Health + SIRI gap assessment, roadmap, licence plan	1-2 weeks
1 · Blueprint & demos	Design sign-off, use-case demos	1-2 weeks
2 · Build	Manufacturing, inventory, quality, finance, HR, integrations	6-10 weeks
3 · Migration & UAT	Data load, testing, sign-off	2-3 weeks
4 · Training & go-live	Training, cutover	1-2 weeks
5 · Hypercare	Stabilisation + SIRI follow-up	2-4 weeks

NOTE

Indicative only — the audit produces the confirmed schedule. Phases overlap where dependencies allow; the SIRI assessment-to-results cycle (≈8-14 weeks) runs in parallel with the build where the program timeline permits.

YOUR PARTNER

Why CodeOx

An **Odoo Silver Partner** with certified experts and a manufacturing/ERP delivery track record. We work on staging first, hand over clean source and documentation, and leave your team owning the system — the practices a SIRI-grade, audit-ready build demands.

Odoo Silver Partner

Official partner status with direct access to Odoo's partner channels and pricing.

Certified Experts

Odoo-certified consultants delivering on the current version, across manufacturing and finance.

Ownership, not lock-in

Namespaced custom code, documentation and training handed over — you own and extend it.

COMMERCIALS

Commercial Approach

We price only what we have looked inside. The engagement therefore starts with a **free, fixed-scope audit** that produces a scored gap report, the exact licensed-user count, and a phased roadmap. A detailed commercial quotation follows the audit, structured so you can commission phase by phase.

HOW THE NUMBERS WORK OUT

Two levers keep your net cost down: the **licence split** (you stop paying per head), and the **Future Factories grant** (up to 80% of the transformation, cap SAR 300,000). Between them, a large share of both the ongoing licence bill and the one-off implementation can be reduced or offset — the audit quantifies exactly how much for ARP.

ON PRICING

No hard SAR figures are quoted in this proposal by design — licensing is confirmed against the live KSA price list, and implementation is scoped from the audit findings. The illustrative SAR 200k → 40k example is for grant mechanics only, not a quotation.

TERMS

Assumptions & Terms

- **Access:** ARP provides timely access to the current Odoo instance, a database + filestore backup, and the relevant staff for discovery and UAT. Delays caused by the client may impact the timeline.
- **Licences & hosting:** Odoo licences and hosting are billed on ARP's subscription; CodeOx secures partner pricing. The final licence count follows the audit.
- **SIRI / grant:** Grant eligibility, figures and the approved-provider route are confirmed with MIM before any funding is treated as firm. The grant is a target pursued together, not a guarantee.
- **Third-party costs:** Any third-party module licences, hardware/IoT, or payment/bank integration fees are billed to ARP by the respective provider.
- **Scope & changes:** Work beyond the configured scope is handled through a written change request and quoted separately.
- **Warranty & support:** A stabilisation (hypercare) period is provided post go-live for the delivered scope. Extended support retainers are available on request.
- **Confidentiality:** Both parties keep the contents of this proposal confidential and do not disclose them to third parties without prior written consent.
- **Validity & governing law:** This proposal is valid for 30 days from issuance and is governed by the laws of the Kingdom of Saudi Arabia.

RECOMMENDED NEXT STEP

Authorise the **free audit & SIRI gap assessment**. It delivers the licence-count, the scored gap report and the phased roadmap — with zero cost and no commitment to the build.

AUTHORIZATION

Acceptance & Authorization

By signing below, both parties confirm acceptance of this technical proposal and authorize commencement of the engagement — beginning with the complimentary audit & SIRI gap assessment — under the scope, approach and terms set out above.

ACCEPTANCE & SIGN-OFF	
FOR ALTERNATIVE REBAR PLANT NAME TITLE SIGNATURE & DATE	FOR CODE-OX TECHNOLOGIES NAME Shabeeb K Head of Operations CONTACT shabeeb.k@code-ox.com +966 53 571 6437 SIGNATURE & DATE

THANK YOU

We look forward to helping Alternative Rebar Plant get more out of Odoo — one connected system, built to a SIRI-grade standard, with government support pursued on your behalf.
